

ID		% Complete	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors	Resource Names	Half 1, 2 J M M	Half 2, 2 J S N	Half 1, 2 J M M	Half 2, 2 J S N	Half 1, 2 J M M	Half 2, 2 J S N	Half 1, 2 J M M
45		0%		BCP Revisions	10 days	Mon 29/09/25	Fri 10/10/25	44	46								
46		0%		PM Review	10 days	Mon 13/10/25	Fri 24/10/25	45	47								
47		0%		Ops Review	10 days	Mon 27/10/25	Fri 07/11/25	46	48								
48		0%		BCP Revisions	10 days	Mon 10/11/25	Fri 21/11/25	47	49								
49		0%		Submit BCP	1 day	Mon 24/11/25	Mon 24/11/25	48	50								
50		0%		BCP Approval	60 days	Tue 25/11/25	Thu 26/02/26	49									
51		45%		BCP3 - Trial Holes BCP	132 days	Wed 30/04/25	Tue 04/11/25										
57		0%		PM Review	5 days	Mon 28/07/25	Fri 01/08/25	56	58SS								
58		0%		Ops Review	5 days	Mon 28/07/25	Fri 01/08/25	57SS	59								
59		0%		BCP Revisions	5 days	Mon 04/08/25	Fri 08/08/25	58	60								
60		0%		Submit BCP	1 day	Mon 11/08/25	Mon 11/08/25	59	61								
61		0%		BCP Approval	60 days	Tue 12/08/25	Tue 04/11/25	60	116								
62		46%		CEXX: Updates Following Site Visit	63 days	Wed 04/06/25	Mon 01/09/25										
63		0%		Hydraulic Calculations for Soakaway Design	5 days	Mon 28/07/25	Fri 01/08/25	80FF	64								
64		0%		Soakaway Design Modification Drawing	10 days	Mon 04/08/25	Fri 15/08/25	139,63									
65		0%		Update to Containment Wall GA for Protection of Substation	10 days	Mon 04/08/25	Fri 15/08/25	93FF									
66		0%		Containment Wall Section Drawing for Poly Silo Tanker Connection	10 days	Mon 18/08/25	Mon 01/09/25	209FF									
68		0%		Site Drainage GA Update for Tertiary Containment	10 days	Mon 04/08/25	Fri 15/08/25	80									
69		88%		Enquiry for Welfare Unit Details	43 days	Wed 04/06/25	Fri 01/08/25		71,203,70								
70		0%		Discuss Welfare Arrangements with DCWW	5 days	Mon 04/08/25	Fri 08/08/25	69	71								
71		0%		Structural Calculations for New Welfare Plinths	10 days	Mon 11/08/25	Fri 22/08/25	69,70	72,333								
72		0%		Bar Bending Schedule/RC Detail for Welfare Plinths	5 days	Tue 26/08/25	Mon 01/09/25	71	333								
73		73%		Permeability Testing Spec	11 days	Wed 16/07/25	Wed 30/07/25		259								
74		49%		Civils	152 days	Mon 14/04/25	Tue 18/11/25										
75		92%		Hydraulic Calculations P01	76 days	Mon 14/04/25	Fri 01/08/25										
78		83%		Hydraulic Calculations P01 Revisions (Flood Gate Location Change)	6 days	Mon 21/07/25	Mon 28/07/25	77	79								
79		0%		Hydraulic Calculations P01 Check	2 days	Tue 29/07/25	Wed 30/07/25	76,77,78	80								
80		0%		Hydraulic Calculations P01 Approval	2 days	Thu 31/07/25	Fri 01/08/25	79	8,6,107,63FF,68								
81		0%		Hydraulic Calculations C01	15 days	Mon 18/08/25	Mon 08/09/25										
82		0%		Hydraulic Calculations C01 Draft	10 days	Mon 18/08/25	Mon 01/09/25	93	83								
83		0%		Hydraulic Calculations C01 Check	3 days	Tue 02/09/25	Thu 04/09/25	82	84								
84		0%		Hydraulic Calculations C01 Approval	2 days	Fri 05/09/25	Mon 08/09/25	83	85,207								
85		0%		Hydraulic Profile	5 days	Tue 09/09/25	Mon 15/09/25	84	207								
86		61%		Secondary Containment	78 days	Mon 28/04/25	Fri 15/08/25										
91		0%		Secondary Containment Structural Calculations Check/Approval	5 days	Mon 28/07/25	Fri 01/08/25	90	92,93								
92		0%		Secondary Containment RC Detail	5 days	Mon 04/08/25	Fri 08/08/25	91	210								
93		0%		Secondary Containment Mark Up	10 days	Mon 04/08/25	Fri 15/08/25	91	209,82,111,65FF								
94		0%		Ducting Design	47 days	Tue 26/08/25	Wed 29/10/25										

Project: Afan Programme 26.02 Date: Tue 05/08/25	Task		Inactive Task		Manual Summary Rollup		External Milestone		Late	
	Split		Inactive Milestone		Manual Summary		Deadline			
	Milestone		Inactive Summary		Start-only		Progress			
	Summary		Manual Task		Finish-only		Manual Progress			
	Project Summary		Duration-only		External Tasks		Critical			

ID		% Complete	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors	Resource Names	Half 1, 2 J M M J	Half 2, 2 J S N	Half 1, 2 J M M J	Half 2, 2 J S N	Half 1, 2 J M M J	Half 2, 2 J S N	Half 1, 2 J M M J
95		0%		P01	10 days	Tue 26/08/25	Mon 08/09/25										
96		0%		Ducting Design Draft	5 days	Tue 26/08/25	Mon 01/09/25	192	97								
97		0%		Ducting Design Check	3 days	Tue 02/09/25	Thu 04/09/25	96	98								
98		0%		Ducting Design Approval	2 days	Fri 05/09/25	Mon 08/09/25	97	211								
99		0%		C01	10 days	Thu 16/10/25	Wed 29/10/25										
100		0%		Ducting Design Draft	5 days	Thu 16/10/25	Wed 22/10/25	196	101								
101		0%		Ducting Design Check	3 days	Thu 23/10/25	Mon 27/10/25	100	102								
102		0%		Ducting Design Approval	2 days	Tue 28/10/25	Wed 29/10/25	101	212								
106		0%		Manhole Schedule	10 days	Mon 04/08/25	Fri 15/08/25										
107		0%		Manhole Schedule Draft	5 days	Mon 04/08/25	Fri 08/08/25	80	108								
108		0%		Manhole Schedule Check	3 days	Mon 11/08/25	Wed 13/08/25	107	109								
109		0%		Manhole Schedule Approval	2 days	Thu 14/08/25	Fri 15/08/25	108	213,111								
110		0%		Roads/Footpaths Design	10 days	Mon 18/08/25	Mon 01/09/25										
111		0%		Roads/Footpaths Design Draft	5 days	Mon 18/08/25	Fri 22/08/25	109,93	112								
112		0%		Roads/Footpaths Design Check	3 days	Tue 26/08/25	Thu 28/08/25	111	113								
113		0%		Roads/Footpaths Design Approval	2 days	Fri 29/08/25	Mon 01/09/25	112	214								
114		29%		Trial Holes	152 days	Mon 14/04/25	Tue 18/11/25										
116		0%		Trial Holes	5 days	Wed 05/11/25	Tue 11/11/25	115,61,208,257	117,18SS-6 wks								
117		0%		Trial Hole Information and Design Revisions	5 days	Wed 12/11/25	Tue 18/11/25	116	345,21								
118		0%		Wall Sealing	10 days	Tue 02/09/25	Mon 15/09/25										
119		0%		Wall Sealing Spec Draft	5 days	Tue 02/09/25	Mon 08/09/25	209,210	120								
120		0%		Wall Sealing Spec Check	3 days	Tue 09/09/25	Thu 11/09/25	119	121								
121		0%		Wall Sealing Spec Approval	2 days	Fri 12/09/25	Mon 15/09/25	120	325								
122		72%		Mechanical	136 days	Mon 07/04/25	Mon 20/10/25										
123		0%		P&IDs C01	10 days	Tue 07/10/25	Mon 20/10/25										
124		0%		P&IDs C01 Draft	5 days	Tue 07/10/25	Mon 13/10/25	8,286	125								
125		0%		P&IDs C01 Check	3 days	Tue 14/10/25	Thu 16/10/25	124	126								
126		0%		P&IDs C01 Approval	2 days	Fri 17/10/25	Mon 20/10/25	125	206								
127		0%		Pipework Schedule	10 days	Tue 02/09/25	Mon 15/09/25										
128		0%		Pipework Schedule Draft	5 days	Tue 02/09/25	Mon 08/09/25	213	129								
129		0%		Pipework Schedule Check	3 days	Tue 09/09/25	Thu 11/09/25	128	130								
130		0%		Pipework Schedule Approval	2 days	Fri 12/09/25	Mon 15/09/25	129	345								
138		60%		CEXX: Update Following Site Visit	43 days	Tue 17/06/25	Thu 14/08/25										
140		83%		Mechanical Install Spec Update	24 days	Mon 30/06/25	Thu 31/07/25	139	141,311,144,307								
141		0%		P&ID Update	5 days	Fri 01/08/25	Thu 07/08/25	140	142								
142		0%		Valve Schedule Update	5 days	Fri 08/08/25	Thu 14/08/25	141									
143		75%		Flood Door Schedule	20 days	Mon 07/07/25	Fri 01/08/25										
144		0%		Trace Heating and Lagging Spec	5 days	Fri 01/08/25	Thu 07/08/25	140									
155		21%		Electrical	128 days	Mon 14/04/25	Wed 15/10/25										
160		0%		Instrument Schedule	10 days	Mon 04/08/25	Fri 15/08/25										

Project: Afan Programme 26.02
Date: Tue 05/08/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Critical

Late

ID		% Complete	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors	Resource Names	Half 1, 2 J M M J	Half 2, 2 J S N	Half 1, 2 J M M J	Half 2, 2 J S N	Half 1, 2 J M M J	Half 2, 2 J S N	Half 1, 2 J M M J
249		0%		Planning Application Approval	15 wks	Thu 13/11/25	Mon 09/03/26	248	414								
250		15%		Procurement	284 days	Mon 12/05/25	Thu 25/06/26										
251		15%		Topographical Survey	55 days	Wed 16/07/25	Wed 01/10/25										
252		80%		Topographical Survey Tender	10 days	Wed 16/07/25	Tue 29/07/25	67	253								
253		0%		Topographical Survey TBA	5 days	Wed 30/07/25	Tue 05/08/25	252	254								
254		0%		Topographical Survey Order Placement	10 days	Wed 06/08/25	Tue 19/08/25	253	255								
255		0%		Topographical Survey Lead Time	10 days	Wed 20/08/25	Wed 03/09/25	254	256								
256		0%		Topographical Survey	5 days	Thu 04/09/25	Wed 10/09/25	255	257								
257		0%		Topographical Survey Results	15 days	Thu 11/09/25	Wed 01/10/25	256	116,194								
258		0%		Permeability Testing	31 days	Thu 31/07/25	Fri 12/09/25										
259		0%		Permeability Testing Tender	10 days	Thu 31/07/25	Wed 13/08/25	73	260								
260		0%		Permeability Testing Order Placement	5 days	Thu 14/08/25	Wed 20/08/25	259	261								
261		0%		Permeability Testing Lead Time	10 days	Thu 21/08/25	Thu 04/09/25	260	262								
262		0%		Permeability Testing Works	1 day	Fri 05/09/25	Fri 05/09/25	261	263								
263		0%		Permeability Testing Results	5 days	Mon 08/09/25	Fri 12/09/25	262	21								
264		98%		MCC Survey	55 days	Mon 12/05/25	Mon 28/07/25										
269		92%		MCC Survey Report	12 days	Fri 11/07/25	Mon 28/07/25	268	177,181								
270		24%		Pre Cast Walls	172 days	Thu 29/05/25	Thu 05/02/26										
271		89%		Pre Cast Walls Tender Return	47 days	Thu 29/05/25	Fri 01/08/25	89	272,345								
272		0%		Pre Cast Walls TBA	5 days	Mon 04/08/25	Fri 08/08/25	271	273,19								
273		0%		Pre Cast Walls Pre Contract Award	5 days	Mon 11/08/25	Fri 15/08/25	272	274								
274		0%		Pre Cast Walls Order Placement	10 days	Mon 18/08/25	Mon 01/09/25	273	275								
275		0%		Pre Cast Walls Update Spec to C01	10 days	Tue 02/09/25	Mon 15/09/25	274	276								
276		0%		Pre Cast Walls Design Received	20 days	Tue 16/09/25	Mon 13/10/25	275	277								
277		0%		Pre Cast Walls Design Approved	5 days	Tue 14/10/25	Mon 20/10/25	276	278								
278		0%		Pre Cast Walls Lead Time	14 wks	Tue 21/10/25	Thu 05/02/26	277	431								
279		27%		Flood Gates	169 days	Mon 19/05/25	Thu 22/01/26										
280		91%		Flood Gates Tender Return	54 days	Mon 19/05/25	Fri 01/08/25	148	281,345								
281		0%		Flood Gates TBA	5 days	Mon 04/08/25	Fri 08/08/25	280	282,190,19								
282		0%		Flood Gates Pre Contract Award	5 days	Mon 11/08/25	Fri 15/08/25	281	283,284								
283		0%		Flood Gates Order Placement	10 days	Mon 18/08/25	Mon 01/09/25	282	285								
284		0%		Flood Gates Update Spec to C01	10 days	Mon 18/08/25	Mon 01/09/25	282	285								
285		0%		Flood Gates Design Received	20 days	Tue 02/09/25	Mon 29/09/25	283,284	286,8								
286		0%		Flood Gates Design Approved	5 days	Tue 30/09/25	Mon 06/10/25	285	287,124								
287		0%		Flood Gates Lead Time	14 wks	Tue 07/10/25	Thu 22/01/26	286	467								
288		0%		MCC	195 days	Tue 16/09/25	Thu 25/06/26										
289		0%		MCC Tender Return	20 days	Tue 16/09/25	Mon 13/10/25	179	290,345								
290		0%		MCC TBA	5 days	Tue 14/10/25	Mon 20/10/25	289	291,19								
291		0%		MCC Pre Contract Award	5 days	Tue 21/10/25	Mon 27/10/25	290	292,293								
292		0%		MCC Order Placement	10 days	Tue 28/10/25	Mon 10/11/25	291	294								

Project: Afan Programme 26.02
Date: Tue 05/08/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Critical

Late

ID		% Complete	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors	Resource Names	Half 1, 2 J M M J	Half 2, 2 J S N J	Half 1, 2 J M M J	Half 2, 2 J S N J	Half 1, 2 J M M J	Half 2, 2 J S N J	Half 1, 2 J M M J
293		0%		MCC Order Update Spec to C01	10 days	Tue 28/10/25	Mon 10/11/25	291	294								
294		0%		MCC Design Received	20 days	Tue 11/11/25	Mon 08/12/25	292,293	295								
295		0%		MCC Design Approved	5 days	Tue 09/12/25	Mon 15/12/25	294	296								
296		0%		MCC Lead Time	26 wks	Tue 16/12/25	Thu 25/06/26	295	470								
297		0%		SI	95 days	Tue 16/09/25	Thu 05/02/26										
298		0%		SI Tender Return	20 days	Tue 16/09/25	Mon 13/10/25	183	299,345								
299		0%		SI TBA	5 days	Tue 14/10/25	Mon 20/10/25	298	300,19								
300		0%		SI Pre Contract Award	5 days	Tue 21/10/25	Mon 27/10/25	299	301,302								
301		0%		SI Order Placement	10 days	Tue 28/10/25	Mon 10/11/25	300	303								
302		0%		SI Order Update Spec to C01	10 days	Tue 28/10/25	Mon 10/11/25	300	303								
303		0%		SI Design Received	20 days	Tue 11/11/25	Mon 08/12/25	301,302	304								
304		0%		SI Design Approved	5 days	Tue 09/12/25	Mon 15/12/25	303	305								
305		0%		SI Lead Time	6 wks	Tue 16/12/25	Thu 05/02/26	304	483,484								
306		28%		Mechanical Install	117 days	Mon 02/06/25	Wed 12/11/25										
307		80%		Mechanical Install Tender Return	40 days	Mon 02/06/25	Tue 12/08/25	154,140	308,345								
308		0%		Mechanical Install TBA	5 days	Wed 13/08/25	Tue 19/08/25	307	309,19								
309		0%		Mechanical Install Pre Contract Award	5 days	Wed 20/08/25	Wed 27/08/25	308	311,310								
310		0%		Mechanical Install Order Placement	10 days	Thu 28/08/25	Wed 10/09/25	309	312								
311		0%		Mechanical Install Update Spec to C01	10 days	Thu 28/08/25	Wed 10/09/25	309,140	312								
312		0%		Mechanical Install Design Received	20 days	Thu 11/09/25	Wed 08/10/25	311,310	313								
313		0%		Mechanical Install Design Approved	5 days	Thu 09/10/25	Wed 15/10/25	312	314								
314		0%		Mechanical Install Lead Time	4 wks	Thu 16/10/25	Wed 12/11/25	313	426								
315		0%		Electrical Install	85 days	Tue 16/09/25	Thu 22/01/26										
316		0%		Electrical Install Tender Return	20 days	Tue 16/09/25	Mon 13/10/25	187	317,345								
317		0%		Electrical Install TBA	5 days	Tue 14/10/25	Mon 20/10/25	316	318,19								
318		0%		Electrical Install Pre Contract Award	5 days	Tue 21/10/25	Mon 27/10/25	317	319,320								
319		0%		Electrical Install Order Placement	10 days	Tue 28/10/25	Mon 10/11/25	318	321								
320		0%		Electrical Install Update Spec to C01	10 days	Tue 28/10/25	Mon 10/11/25	318	321								
321		0%		Electrical Install Design Received	20 days	Tue 11/11/25	Mon 08/12/25	319,320	322								
322		0%		Electrical Install Design Approved	5 days	Tue 09/12/25	Mon 15/12/25	321	323								
323		0%		Electrical Install Lead Time	4 wks	Tue 16/12/25	Thu 22/01/26	322									
324		0%		Wall Sealing	95 days	Tue 16/09/25	Thu 05/02/26										
325		0%		Wall Sealing Return	20 days	Tue 16/09/25	Mon 13/10/25	121	326,345								
326		0%		Wall Sealing TBA	5 days	Tue 14/10/25	Mon 20/10/25	325	327								
327		0%		Wall Sealing Pre Contract Award	5 days	Tue 21/10/25	Mon 27/10/25	326	328								
328		0%		Wall Sealing Order Placement	10 days	Tue 28/10/25	Mon 10/11/25	327	329								
329		0%		Wall Sealing Design Received	20 days	Tue 11/11/25	Mon 08/12/25	328	330								
330		0%		Wall Sealing Design Approved	5 days	Tue 09/12/25	Mon 15/12/25	329	331								
331		0%		Wall Sealing Lead Time	6 wks	Tue 16/12/25	Thu 05/02/26	330	472,473								
332		0%		Welfare	95 days	Tue 02/09/25	Thu 22/01/26										

Project: Afan Programme 26.02
Date: Tue 05/08/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline


Progress

Manual Progress

Critical

Late

ID		% Complete	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors	Resource Names	Half 1, 2 J M M J	Half 2, 2 J S N J	Half 1, 2 J M M J	Half 2, 2 J S N J	Half 1, 2 J M M J	Half 2, 2 J S N J	Half 1, 2 J M M J
333		0%		Welfare Tender	10 days	Tue 02/09/25	Mon 15/09/25	71,72,203	334								
334		0%		Welfare TBA	5 days	Tue 16/09/25	Mon 22/09/25	333	335,19								
335		0%		Welfare Order Placement	5 days	Tue 23/09/25	Mon 29/09/25	334	336								
336		0%		Welfare Drawings Received	10 days	Tue 30/09/25	Mon 13/10/25	335	337								
337		0%		Welfare Drawings Reviewed	5 days	Tue 14/10/25	Mon 20/10/25	336	338								
338		0%		Welfare Lead Time	12 wks	Tue 21/10/25	Thu 22/01/26	337	414								
339		0%		IDP4	102 days	Wed 08/10/25	Tue 10/03/26										
340		0%		Update C&CE	10 days	Wed 22/10/25	Tue 04/11/25	345SS-20 days	341								
341		0%		Submit C&CE	5 days	Wed 05/11/25	Tue 11/11/25	340	342								
342		0%		DCWW Pre-CT Review C&CE Scope and Forward	5 days	Wed 12/11/25	Tue 18/11/25	341	343								
343		0%		DCWW C&CE Review	15 days	Wed 19/11/25	Tue 09/12/25	342	350								
344		0%		Estimating Kick Off	1 day	Wed 08/10/25	Wed 08/10/25	345SS-6 wks									
345		0%		Update LBE	10 days	Wed 19/11/25	Tue 02/12/25	280,289,307,316,24,	340SS-20 days,34								
346		0%		LBE Internal Review	5 days	Wed 03/12/25	Tue 09/12/25	345	347								
347		0%		LBE Management Review	10 days	Wed 10/12/25	Tue 23/12/25	346	348								
348		0%		Submit CA & PSTP Pack and CTC	1 day	Mon 05/01/26	Mon 05/01/26	22,347	349,351								
349		0%		CTC Cost Assurance Review and £.I.G.	20 days	Tue 06/01/26	Mon 02/02/26	348	350,352								
350		0%		Agree Target Price	0 days	Mon 02/02/26	Mon 02/02/26	343,349	353,356,354,25								
351		0%		CIT Submission	0 days	Mon 05/01/26	Mon 05/01/26	348									
352		0%		CIT Approval	0 days	Mon 02/02/26	Mon 02/02/26	349									
353		0%		PRG IDP4	1 day	Tue 03/02/26	Tue 03/02/26	350	357FS-5 days,356								
354		0%		IPG	1 day	Tue 03/02/26	Tue 03/02/26	350	355								
355		0%		IPG MD	1 day	Wed 04/02/26	Wed 04/02/26	354	358,360,359								
356		0%		IDP4 Documentation Prep	5 days	Wed 04/02/26	Tue 10/02/26	350,353	358								
357		0%		IDP4 Prep and Review	5 days	Wed 28/01/26	Tue 03/02/26	353FS-5 days	358								
358		0%		IDP4 Pack Returned from Assets	0 days	Tue 10/02/26	Tue 10/02/26	355,356,357	359								
359		0%		IDP4 Approval	20 days	Wed 11/02/26	Tue 10/03/26	355,358	360								
360		0%		IDP4 - Commit to Detail Design	0 days	Tue 10/03/26	Tue 10/03/26	355,359	414								
361		0%		Afan Emissions - Based on Tanks in Good Condition	732 days	Mon 18/08/25	Mon 19/06/28										
362		0%		Outline Design	452 days	Mon 18/08/25	Mon 24/05/27										
363		0%		Key Meetings	423 days	Mon 18/08/25	Tue 13/04/27										
364		0%		Kick Off Meeting (TBC)	1 day	Mon 18/08/25	Mon 18/08/25		396,399,369								
365		0%		Stakeholder Meeting	1 day	Tue 13/04/27	Tue 13/04/27	388									
366		0%		HAZOP	1 day	Tue 24/03/26	Tue 24/03/26	376FS+10 days	391FS+1 day,367F								
367		0%		ALM	1 day	Wed 08/04/26	Wed 08/04/26	366FS+10 days	388								
368		0%		Design	451 days	Tue 19/08/25	Mon 24/05/27										
369		0%		Data Mining Request	15 days	Tue 19/08/25	Tue 09/09/25	364	370,371								
370		0%		Meeting with Marches Biogas - GAP Analysis and Scope of	1 day	Wed 10/09/25	Wed 10/09/25	369	399								
371		0%		Review Data Mining - Marches Biogas	10 days	Thu 20/11/25	Wed 03/12/25	400,369	372SS,373								
372		0%		3D Scan and Survey by Marches Biogas	5 days	Thu 20/11/25	Wed 26/11/25	371SS	373								

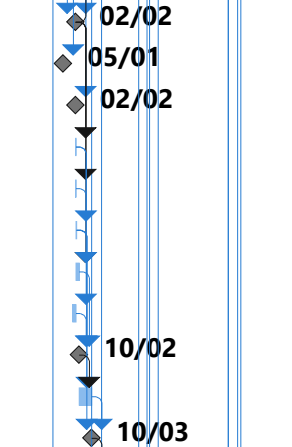

Project: Afan Programme 26.02
Date: Tue 05/08/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress


Critical

Late

ID		% Complete	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors	Resource Names	Half 1, 2 J M M J	Half 2, 2 J S N	Half 1, 2 J M M J	Half 2, 2 J S N	Half 1, 2 J M M J	Half 2, 2 J S N	Half 1, 2 J M M J
373		0%		Calculations and Deliverables by Marches Biogas	30 days	Thu 04/12/25	Mon 26/01/26	371,372	376,374,375								
374		0%		Civils Design for Marches Proposal	20 days	Tue 27/01/26	Mon 23/02/26	373	382,384								
375		0%		Electrical Design for Marches Proposal	40 days	Tue 27/01/26	Mon 23/03/26	373	382,383,384								
376		0%		Data Review by MMB	30 days	Tue 27/01/26	Mon 09/03/26	373	366FS+10 days								
377		0%		Results of Tank Survey	5 days	Tue 07/07/26	Mon 13/07/26	397	380,382,378								
378		0%		Review of Outline Design from Tank Supplier	15 days	Tue 14/07/26	Mon 03/08/26	377	391FS+1 day,379								
379		0%		DSEAR Risk Assessment	15 days	Tue 04/08/26	Mon 24/08/26	378	391FS+1 day								
380		0%		Specification for Tank Covers (4no)	25 days	Tue 14/07/26	Mon 17/08/26	377	402,381								
381		0%		Review Enabling Requirements	20 days	Tue 18/08/26	Mon 14/09/26	380	387								
382		0%		Scope Tracker	15 days	Tue 14/07/26	Mon 03/08/26	374,375,377	384,383								
383		0%		Proposed Load Schedule	10 days	Tue 04/08/26	Mon 17/08/26	375,382									
384		0%		Site GA and Drawings	20 days	Tue 04/08/26	Mon 31/08/26	374,375,382	386,385								
385		0%		Specs for Procurement	20 days	Tue 01/09/26	Mon 28/09/26	384	403,404,405,406,								
386		0%		Outline Commissioning Plan	10 days	Tue 01/09/26	Mon 14/09/26	384									
387		0%		Detailed Design Estimate	6 mons	Tue 15/09/26	Mon 01/03/27	381	388								
388		0%		Estimating	6 wks	Tue 02/03/27	Mon 12/04/27	387,367	365,389								
389		0%		IDP4	30 days	Tue 13/04/27	Mon 24/05/27	388	410								
390		0%		IC5	21 days	Wed 26/08/26	Wed 23/09/26										
391		0%		MMB to Draft IC5 Response	20 days	Wed 26/08/26	Tue 22/09/26	366FS+1 day,378FS+	392								
392		0%		IC5 Submission to DCWW	1 day	Wed 23/09/26	Wed 23/09/26	391									
393		0%		BCP/DCWW Shutdowns (TBC)	80 days	Tue 10/02/26	Mon 01/06/26										
394		0%		Planning for Post Digestion Tank Shutdown Draft/Submission/Approval (if MMB, BCP required)	80 days	Tue 10/02/26	Mon 01/06/26	396	397FS+5 days								
395		0%		Surveys	155 days	Thu 20/11/25	Mon 06/07/26										
396		0%		Biogas Potential Survey	10 wks	Thu 20/11/25	Mon 09/02/26	364,401	394								
397		0%		Post Digestion Tank Clean and Intrusive Survey	20 days	Tue 09/06/26	Mon 06/07/26	394FS+5 days	377								
398		0%		Procurement	325 days	Thu 11/09/25	Mon 21/12/26										
399		0%		Early Engagement and Order Placement with Spec and Scope of Emission Survey and Quote	20 days	Thu 11/09/25	Wed 08/10/25	364,370	400,401								
400		0%		Early Engagement and Order Placement with Marches Biogas - For GAP Analysis and Design	30 days	Thu 09/10/25	Wed 19/11/25	399	371								
401		0%		Early Engagement and Order Placement with Marches Biogas - For Tank Surveying	30 days	Thu 09/10/25	Wed 19/11/25	399	396								
402		0%		Engagement and Order Placement with Supplier for Tank C	25 days	Tue 18/08/26	Mon 21/09/26	380									
403		0%		Eliquo (TBC) Procurement	60 days	Tue 29/09/26	Mon 21/12/26	385									
404		0%		Blower/Compressor Procurement	60 days	Tue 29/09/26	Mon 21/12/26	385									
405		0%		MCC Mods Procurement	60 days	Tue 29/09/26	Mon 21/12/26	385									
406		0%		SI Procurement	60 days	Tue 29/09/26	Mon 21/12/26	385									
407		0%		Mechanical Install Procurement	60 days	Tue 29/09/26	Mon 21/12/26	385									
408		0%		Electrical Install Procurement	60 days	Tue 29/09/26	Mon 21/12/26	385									
409		0%		Construction	280 days	Tue 25/05/27	Mon 19/06/28										

Project: Afan Programme 26.02 Date: Tue 05/08/25	Task		Inactive Task		Manual Summary Rollup		External Milestone		Late	
	Split		Inactive Milestone		Manual Summary		Deadline			
	Milestone		Inactive Summary		Start-only		Progress			
	Summary		Manual Task		Finish-only		Manual Progress			
	Project Summary		Duration-only		External Tasks		Critical			

ID		% Complete	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors	Resource Names	Half 1, 2 J M M J	Half 2, 2 J S N J	Half 1, 2 J M M J	Half 2, 2 J S N J	Half 1, 2 J M M J	Half 2, 2 J S N J	Half 1, 2 J M M J	Half 2, 2 J S N J
450		0%		West Wall (3m length, 1.2m high)	2 days	Thu 08/10/26	Fri 09/10/26											
451		0%		Install Legato Walls from Gas Holder	2 days	Thu 08/10/26	Fri 09/10/26	442	453	Gang 1								
452		0%		North Wall (38m length, 1.2m high)	25 days	Mon 12/10/26	Fri 13/11/26											
453		0%		Concrete Remedial Works in Preparation for Walls (TBC)	10 days	Mon 12/10/26	Fri 23/10/26	451	454	Gang 1								
454		0%		Install Legato Walls	15 days	Mon 26/10/26	Fri 13/11/26	453	456	Gang 1								
455		0%		Entrance Area	31 days	Mon 16/11/26	Mon 28/12/26											
456		0%		Excavate and Install New Gully and Drainage	10 days	Mon 16/11/26	Fri 27/11/26	454	457	Gang 1								
457		0%		Excavate Area and Install New Kerbs	7 days	Mon 30/11/26	Tue 08/12/26	456	458	Gang 1								
458		0%		Remove Existing Speed Hump/Cattle Grid	1 day	Wed 09/12/26	Wed 09/12/26	457	459	Gang 1								
459		0%		Tertiary Containment Concrete Works (TBC)	10 days	Thu 10/12/26	Wed 23/12/26	458	460	Gang 1								
460		0%		Install New Sleeping Policemen (x4)	3 days	Thu 24/12/26	Mon 28/12/26	459	462	Gang 1								
461		0%		Flap Valves	6 days	Tue 29/12/26	Tue 05/01/27											
462		0%		Install New Flap Valve (MH1)	2 days	Tue 29/12/26	Wed 30/12/26	460	463	Gang 1								
463		0%		Install New Flap Valve (MH7)	2 days	Thu 31/12/26	Fri 01/01/27	462	464	Gang 1								
464		0%		Install New Flap Valve (MH)	2 days	Mon 04/01/27	Tue 05/01/27	463	466	Gang 1								
465		0%		Flood Gates	18 days	Wed 06/01/27	Fri 29/01/27											
466		0%		Civils (Channels)	3 days	Wed 06/01/27	Fri 08/01/27	464	467,472,473	Gang 1								
467		0%		Install Flood Gates (Manual and Automated)	10 days	Mon 11/01/27	Fri 22/01/27	466,287,449	468,474	Mechanical Subco								
468		0%		Electrical Install	5 days	Mon 25/01/27	Fri 29/01/27	467	484	Electrical Subcont								
469		0%		MCC	30 days	Fri 26/06/26	Thu 06/08/26											
470		0%		MCC Works	30 days	Fri 26/06/26	Thu 06/08/26	296	483	Electrical Subcont								
471		0%		Finishing Works	75 days	Mon 11/01/27	Fri 23/04/27											
472		0%		Sealing Legato Walls	30 days	Mon 11/01/27	Fri 19/02/27	466,331	481,493,473SS+20 d	Subcontract								
473		0%		Concrete Hardstanding Repairs	10 days	Mon 08/02/27	Fri 19/02/27	466,331,472SS+20 d	481,493	Subcontract								
474		0%		Install Access Stairways	15 days	Mon 25/01/27	Fri 12/02/27	467	480,481,475,493	Mechanical Subcc								
475		0%		Modify Poly Silo Pipework (and Others TBC)	10 days	Mon 15/02/27	Fri 26/02/27	474	476,493	Mechanical Subcc								
476		0%		GRP Deflection Plates Installation on Sludge Pipes	10 days	Mon 01/03/27	Fri 12/03/27	475	477,493	Mechanical Subcc								
477		0%		Rainwater Pipework Rerouting	10 days	Mon 15/03/27	Fri 26/03/27	476	478,493	Mechanical Subcc								
478		0%		Installation of Sealed Access Covers	10 days	Mon 29/03/27	Fri 09/04/27	477	479,493	Mechanical Subcc								
479		0%		Replace Fire Exit Doors with Flood Doors	5 days	Mon 12/04/27	Fri 16/04/27	478	481,493	Mechanical Subcc								
480		0%		Finishing Civil Activities	10 days	Mon 15/02/27	Fri 26/02/27	474	481,493	Gang 1								
481		0%		Demob	5 days	Mon 19/04/27	Fri 23/04/27	480,474,479,472,473	500,501	Gang 1								
482		0%		Commissioning	131 days	Fri 07/08/26	Fri 05/02/27											
483		0%		MCC	5 days	Fri 07/08/26	Thu 13/08/26	470,305	484	SI Subcontractor								
484		0%		Flood Gates	5 days	Mon 01/02/27	Fri 05/02/27	483,468,305	487,490	SI Subcontractor								
485		0%		Handover	80 days	Mon 08/02/27	Fri 28/05/27											
486		0%		Plant in Service	35 days	Mon 08/02/27	Fri 26/03/27											
487		0%		Optimisation / Monitoring /Snagging	5 days	Mon 08/02/27	Fri 12/02/27	484	488,489,496,498,	MMB - Comm								
488		0%		Walkover	5 days	Mon 15/02/27	Fri 19/02/27	487		MMB - Comm								
489		0%		Training	5 days	Mon 15/02/27	Fri 19/02/27	487	491	MMB - Comm								

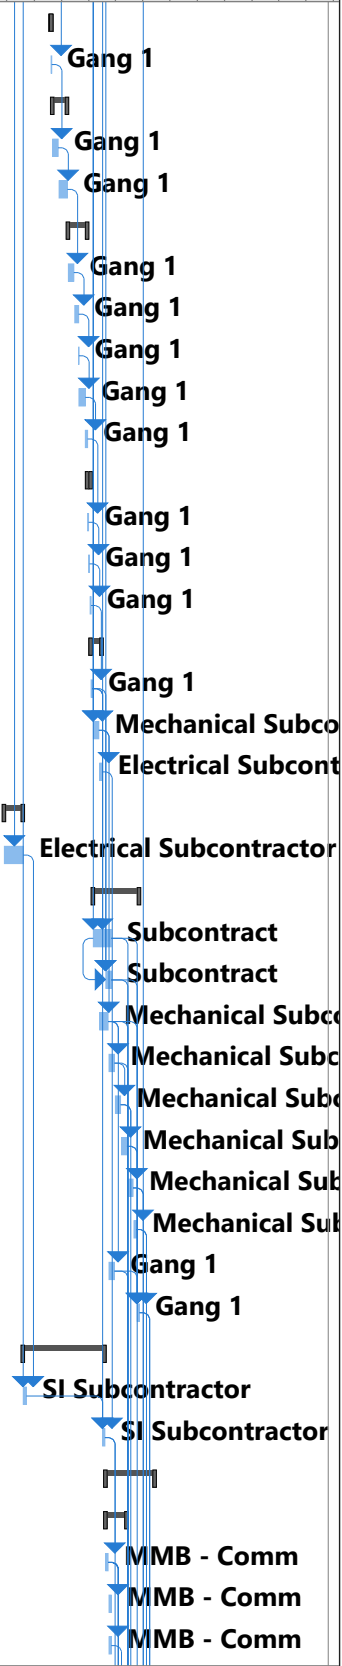

Project: Afan Programme 26.02
Date: Tue 05/08/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress


Manual Progress

Critical

Late

Page 11

ID		% Complete	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors	Resource Names	Half 1, 2 J M M	Half 2, 2 J S N	Half 1, 2 J M M	Half 2, 2 J S N	Half 1, 2 J M M	Half 2, 2 J S N	Half 1, 2 J M M
490		0%		CAF607 Upload	5 days	Mon 08/02/27	Fri 12/02/27	484	491,497	MMB - Comm							
491		0%		Plant in Service	5 days	Mon 22/02/27	Fri 26/02/27	489,490	492,494,493								
492		0%		28 day proving	20 days	Mon 01/03/27	Fri 26/03/27	491	499								
493		0%		Completion Date	0 days	Fri 16/04/27	Fri 16/04/27	472,474,475,476,477									
494		0%		Commissioning Complete	0 days	Fri 26/02/27	Fri 26/02/27	491									
495		0%		CAF601 Telemetry Certificate	5 days	Mon 15/02/27	Fri 19/02/27	487	499								
496		0%		CAF603 Software Handover	5 days	Mon 15/02/27	Fri 19/02/27	487	499								
497		0%		CAF607 Equipment Schedule	5 days	Mon 15/02/27	Fri 19/02/27	490	499								
498		0%		CAF608 O&M	5 days	Mon 15/02/27	Fri 19/02/27	487	499								
499		0%		CAF609 Handover	5 days	Mon 03/05/27	Fri 07/05/27	492,500,498,497,496	505,511								
500		0%		CAF610 H&S File	5 days	Mon 26/04/27	Fri 30/04/27	481	499								
501		0%		CAF616 - Environment Handover	5 days	Mon 26/04/27	Fri 30/04/27	481	502								
502		0%		Hand over documentation	20 days	Mon 03/05/27	Fri 28/05/27	501	514SS-10 days								
503		0%		IDP 5	55 days	Mon 19/04/27	Fri 02/07/27										
504		0%		IDP 5 Milestones	40 days	Fri 07/05/27	Fri 02/07/27										
505		0%		IDP 5 documents uploaded to SharePoint	0 days	Fri 07/05/27	Fri 07/05/27	499	506FS+5 days								
506		0%		Stage 5 - Documents Returned to LAM	0 days	Fri 14/05/27	Fri 14/05/27	505FS+5 days									
507		0%		IDP 5 - Commit to handover	0 days	Fri 18/06/27	Fri 18/06/27	512	508FS+5 days								
508		0%		SAP Upload Complete	0 days	Fri 25/06/27	Fri 25/06/27	507FS+5 days	509FS+5 days								
509		0%		Completion Certificate	0 days	Fri 02/07/27	Fri 02/07/27	508FS+5 days	523								
510		0%		IDP 5 Tasks	45 days	Mon 19/04/27	Fri 18/06/27										
511		0%		Prepare IDP 5 Documents	20 days	Mon 10/05/27	Fri 04/06/27	499	513,512								
512		0%		Submit for IDP 5 and Approval Period	10 days	Mon 07/06/27	Fri 18/06/27	511	507								
513		0%		Print all handover document for site	5 days	Mon 07/06/27	Fri 11/06/27	511									
514		0%		QES4 review	5 days	Mon 19/04/27	Fri 23/04/27	502SS-10 days									
515		0%		Stage 6 - Operate	150 days	Mon 05/07/27	Fri 28/01/28										
516		0%		Stage 6 - Operate Milestones	90 days	Fri 24/09/27	Fri 28/01/28										
517		0%		Submit Final Account	0 days	Fri 24/09/27	Fri 24/09/27	523	524								
518		0%		Final Account Complete	0 days	Fri 19/11/27	Fri 19/11/27	524	525								
519		0%		Unit Cost Database Uploaded	0 days	Fri 03/12/27	Fri 03/12/27	525	520								
520		0%		Scheme Complete	0 days	Fri 03/12/27	Fri 03/12/27	519									
521		0%		Post Project Review	0 days	Fri 28/01/28	Fri 28/01/28	523FS+90 days									
522		0%		Stage 6 - Operate Tasks	110 days	Mon 05/07/27	Fri 03/12/27										
523		0%		Prepare Final Account	60 days	Mon 05/07/27	Fri 24/09/27	509	517,521FS+90 days								
524		0%		Final Account Agreement Period	40 days	Mon 27/09/27	Fri 19/11/27	517	518								
525		0%		Final Account Data Capture	10 days	Mon 22/11/27	Fri 03/12/27	518	519								



Project: Afan Programme 26.02
Date: Tue 05/08/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Critical

Late
