




A465 River Clydach Bridge - Concrete Repairs - Rev02 (8/7/26)

Tender Programme T25/12/170 (Page 1 of 2)



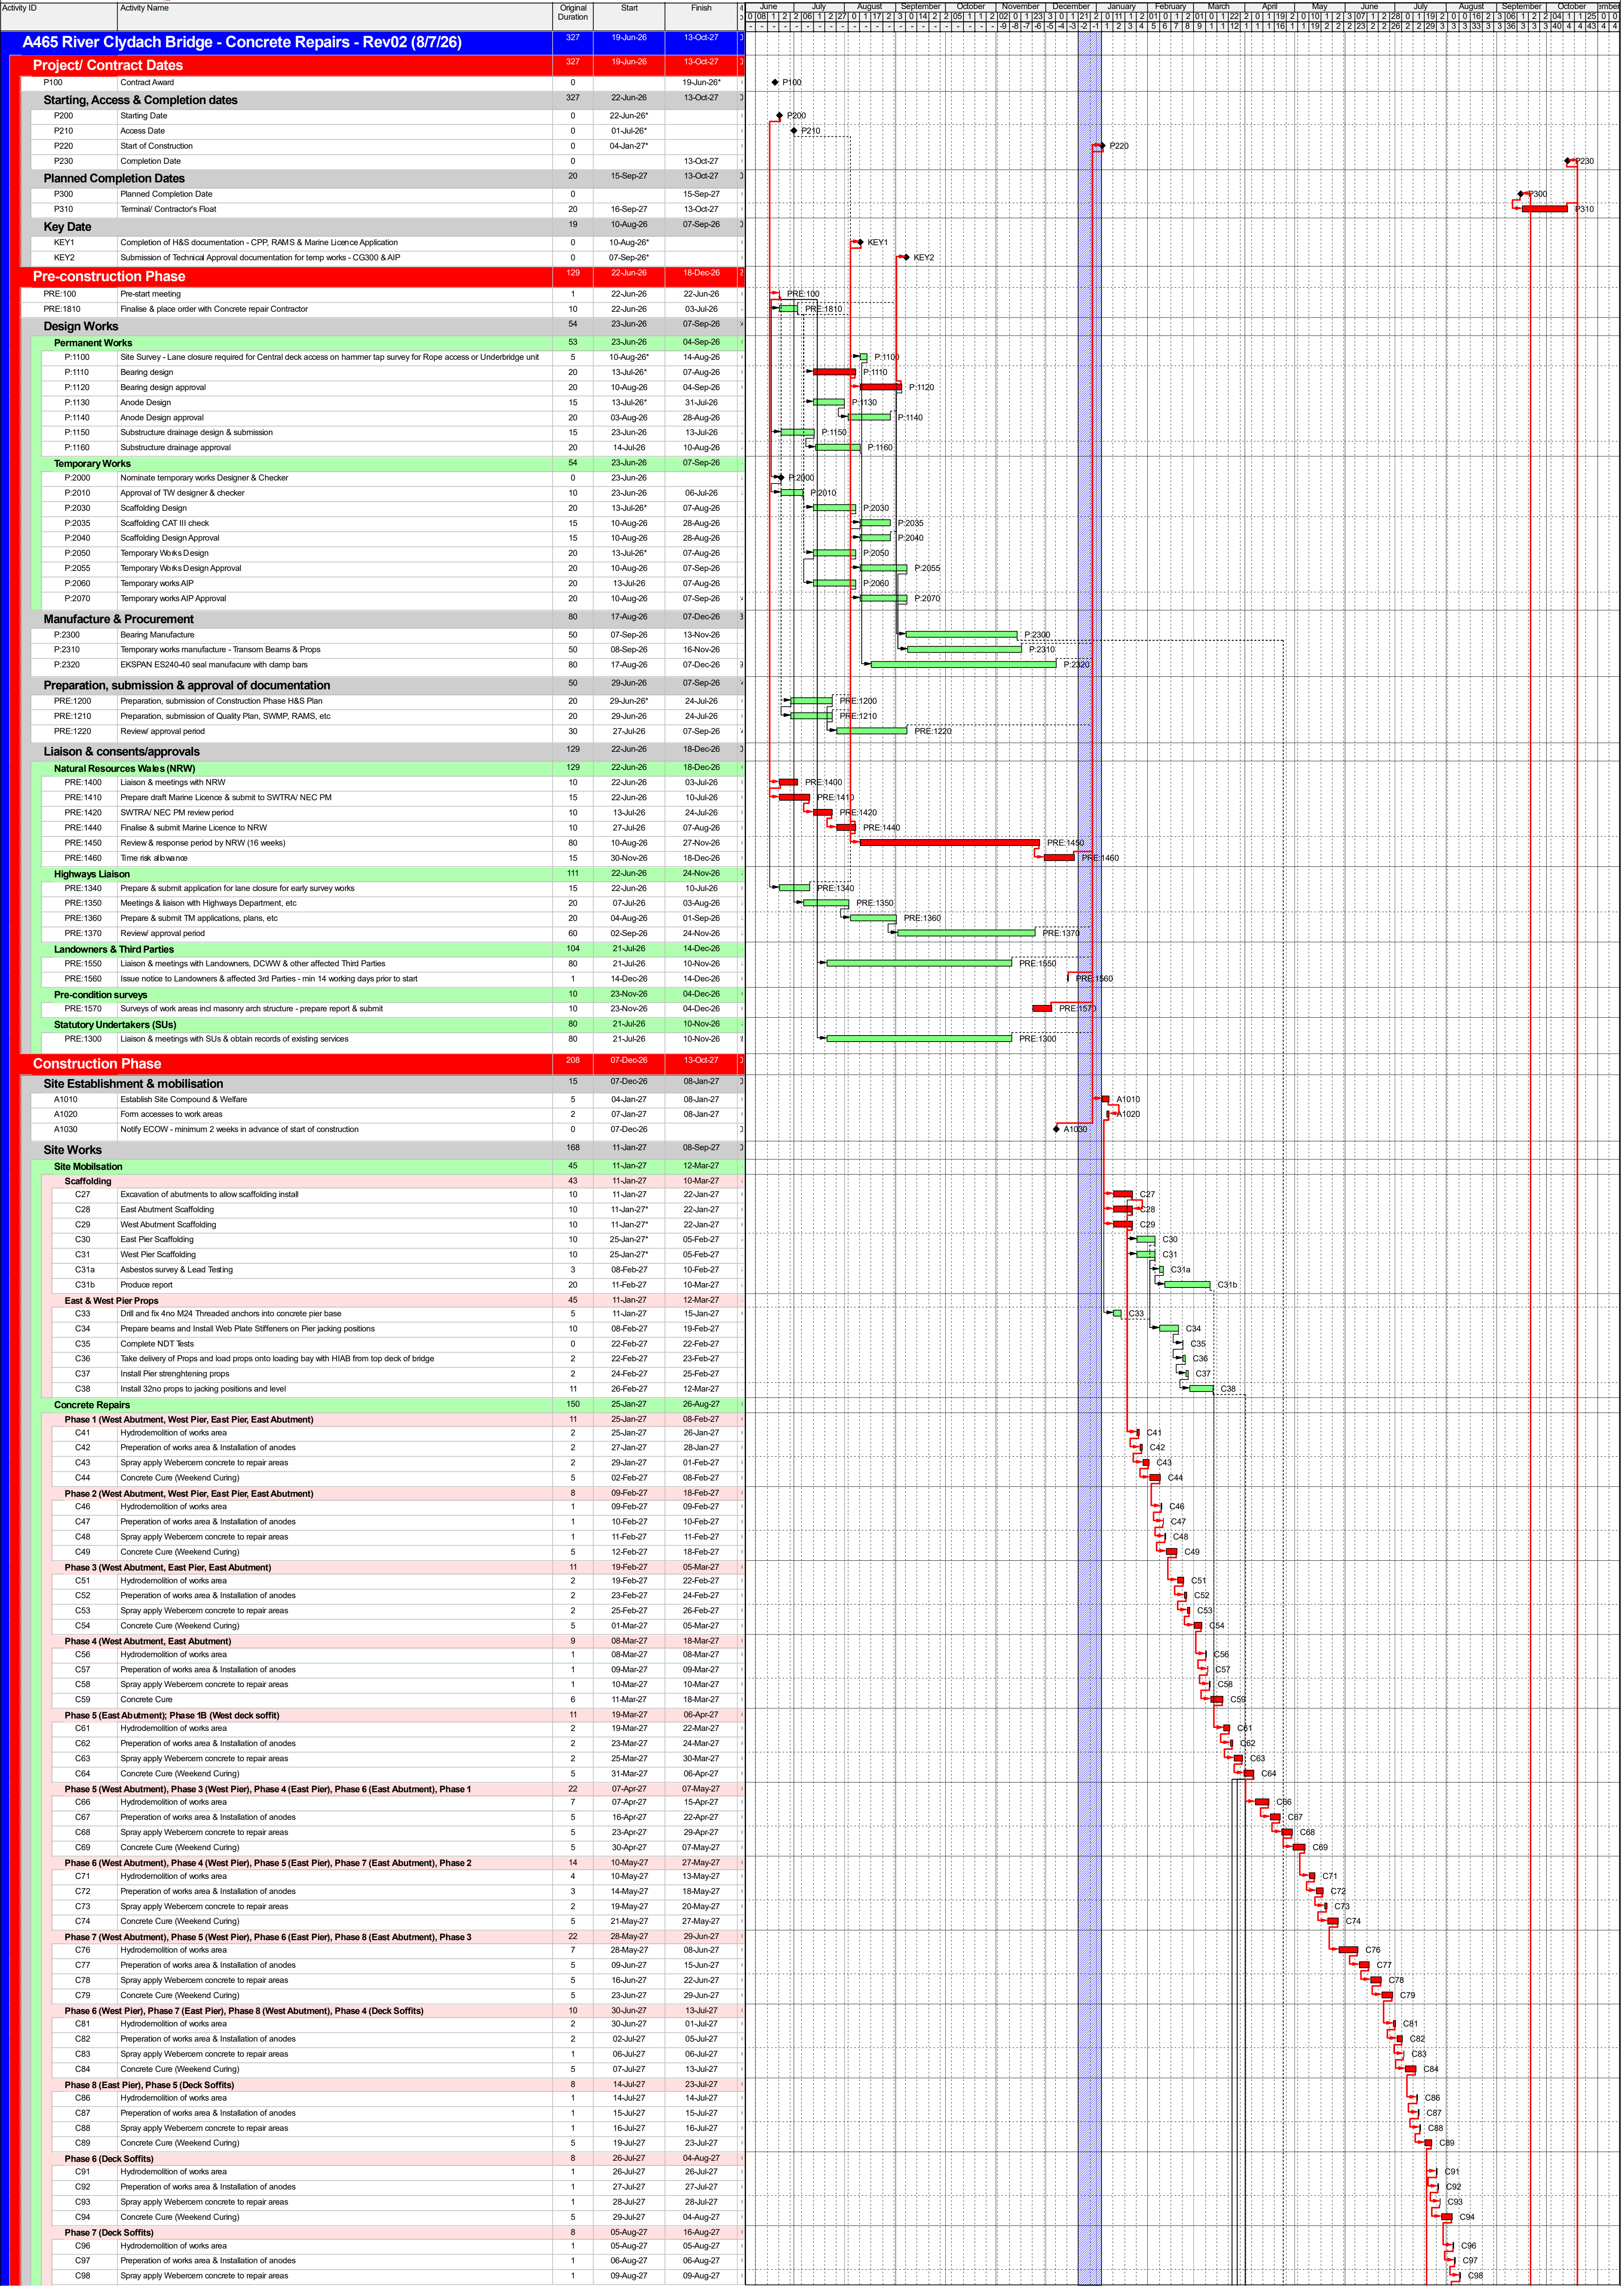

A465 River Clydach Bridge - Concrete Repairs - Rev02 (8/7/26)
Tender Programme T25/12/170 (Page 2 of 2)



Activity ID	Activity Name	Original Duration	Start	Finish	June	July	August	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November
C99	Concrete Cure (Weekend Curing)	5	10-Aug-27	16-Aug-27																		
Phase 8 (Dock Soffits)		8	17-Aug-27	26-Aug-27																		
C101	Hydrodemolition of works area	1	17-Aug-27	17-Aug-27																		
C102	Preparation of works area & Installation of anodes	1	18-Aug-27	18-Aug-27																		
C103	Spray apply Webercem concrete to repair areas	1	19-Aug-27	19-Aug-27																		
C104	Concrete Cure (Weekend Curing)	5	20-Aug-27	26-Aug-27																		
Bearing Replacement		106	30-Mar-27	26-Aug-27																		
Temporary Works Install & Bearing Replacement - West Pier		103	02-Apr-27	26-Aug-27																		
C107	Drill & fix 2no restraints to bearing shelf base	1	02-Apr-27	02-Apr-27																		
C108	Set up 16no jacking assemblies on top of props	2	05-Apr-27	06-Apr-27																		
C109	Jack structure (Night working)	1	07-Apr-27	07-Apr-27																		
C110	Saw out and hydro demolition 16no bearing positions	4	08-Apr-27	13-Apr-27																		
C111	Remove bearings	2	14-Apr-27	15-Apr-27																		
C112	Prep and weld 16no Flange plates to longitudinal beams in final bearing positions	10	16-Apr-27	29-Apr-27																		
C113	NDT Welds	0	30-Apr-27	30-Apr-27																		
C114	Bolt up 16no EKSPAN Spherical bearings and protect bearings	2	30-Apr-27	04-May-27																		
C115	Prep surface, Drill, fix and build new re-inforcement cage	8	16-Apr-27	27-Apr-27																		
C116	Install formwork	8	28-Apr-27	10-May-27																		
C117	Cast concrete	2	11-May-27	12-May-27																		
C118	Concrete cure	5	13-May-27	19-May-27																		
C119	Remove Formwork	1	20-May-27	20-May-27																		
C120	Shutter and cast grout bed to 16no positions	2	21-May-27	24-May-27																		
C121	Grout cure	1	25-May-27	25-May-27																		
C122	Confirm cube strength for concrete & grout	0	26-May-27	26-May-27																		
C123	De-Jack structure (Night working) & Install 3 week period for monitoring	1	26-Jul-27	26-Jul-27																		
C124	Strike Shutters, fettle grout beds	2	27-Jul-27	28-Jul-27																		
C125	Install 35 meters of ES seal using resin fixed anchors @ 200mm centers - 328 drilled holes	7	29-Jul-27	06-Aug-27																		
C126	Remove restraints, hydraulic cylinders, props and make good of works area	8	09-Aug-27	18-Aug-27																		
C127	Paint end beams, flange plates & bearing fixings	5	19-Aug-27	25-Aug-27																		
C128	Remove Monitoring	1	26-Aug-27	26-Aug-27																		
Temporary Works Install & Bearing Replacement - East Pier		103	02-Apr-27	26-Aug-27																		
C130	Drill & fix 2no restraints to bearing shelf base	1	02-Apr-27	02-Apr-27																		
C131	Set up 16no jacking assemblies on top of props	2	05-Apr-27	06-Apr-27																		
C132	Jack structure (Night working)	1	07-Apr-27	07-Apr-27																		
C133	Saw out and hydro demolition 16no bearing positions	4	08-Apr-27	13-Apr-27																		
C134	Remove bearings	2	14-Apr-27	15-Apr-27																		
C135	Prep and weld 16no Flange plates to longitudinal beams in final bearing positions	10	16-Apr-27	29-Apr-27																		
C136	NDT Welds	0	30-Apr-27	30-Apr-27																		
C137	Bolt up 16no EKSPAN Spherical bearings and protect bearings	2	30-Apr-27	04-May-27																		
C138	Prep surface, Drill, fix and build new re-inforcement cage	8	16-Apr-27	27-Apr-27																		
C139	Install formwork	8	28-Apr-27	10-May-27																		
C140	Cast concrete	2	11-May-27	12-May-27																		
C141	Concrete cure (Weekend curing)	5	13-May-27	19-May-27																		
C142	Remove Formwork	1	20-May-27	20-May-27																		
C143	Shutter and cast grout bed to 16no positions	2	21-May-27	24-May-27																		
C144	Grout cure	1	25-May-27	25-May-27																		
C145	Confirm cube strength for concrete & grout	0	26-May-27	26-May-27																		
C146	De-Jack structure (Night working) & Install 3 week period for monitoring	1	26-Jul-27	26-Jul-27																		
C147	Strike Shutters, fettle grout beds	2	27-Jul-27	28-Jul-27																		
C148	Install 35 meters of ES seal using resin fixed anchors @ 200mm centers - 328 drilled holes	7	29-Jul-27	06-Aug-27																		
C149	Remove restraints, hydraulic cylinders, props and make good of works area	8	09-Aug-27	18-Aug-27																		
C150	Paint end beams, flange plates & bearing fixings	5	19-Aug-27	25-Aug-27																		
C151	Remove Monitoring	1	26-Aug-27	26-Aug-27																		
Temporary Works Install & Bearing Replacement - West Abutment		105	30-Mar-27	25-Aug-27																		
C153	Drill & fix 2no restraints to bearing shelf base	2	30-Mar-27	31-Mar-27																		
C154	Install 4no Transom beams to existing girders to enable jacking from bearing shelf	4	01-Apr-27	06-Apr-27																		
C155	Jack structure (Night working)	1	07-Apr-27	07-Apr-27																		
C156	Saw out and hydro demolition 8no bearing positions	2	08-Apr-27	09-Apr-27																		
C157	Remove bearings	1	12-Apr-27	12-Apr-27																		
C158	Prep and weld 8no Flange plates to longitudinal beams in final bearing positions	5	13-Apr-27	19-Apr-27																		
C159	NDT Welds	0	20-Apr-27	20-Apr-27																		
C160	Bolt up 8no EKSPAN Spherical bearings	1	20-Apr-27	20-Apr-27																		
C161	Shutter and cast concrete to 8no bearing positions	2	21-Apr-27	22-Apr-27																		
C162	Concrete cure	5	23-Apr-27	29-Apr-27																		
C163	Shutter and cast grout bed to 8no positions	2	30-Apr-27	04-May-27																		
C164	Grout cure	1	05-May-27	05-May-27																		
C165	Confirm cube strength for concrete & grout	0	06-May-27	06-May-27																		
C166	De-Jack structure (Night working) & Install 3 week period for monitoring	1	26-Jul-27	26-Jul-27																		
C167	Strike Shutters, fettle grout beds	2	27-Jul-27	28-Jul-27																		
C168	Install 35 meters of ES seal using resin fixed anchors @ 200mm centers - 328 drilled holes	7	29-Jul-27	06-Aug-27																		
C169	Remove restraints, hydraulic cylinders, transom beams and make good of works area	7	09-Aug-27	17-Aug-27																		
C170	Paint end beams, flange plates & bearing fixings	5	18-Aug-27	24-Aug-27																		
C171	Remove monitoring	1	25-Aug-27	25-Aug-27																		
Temporary Works Install & Bearing Replacement - East Abutment		105	30-Mar-27	25-Aug-27																		
C173	Drill & fix 2no restraints to bearing shelf base	2	30-Mar-27	31-Mar-27																		
C174	Install 4no Transom beams to existing girders to enable jacking from bearing shelf	4	01-Apr-27	06-Apr-27																		
C175	Jack structure (Night working)	1	07-Apr-27	07-Apr-27																		
C176	Saw out and hydro demolition 8no bearing positions	2	08-Apr-27	09-Apr-27																		
C177	Remove bearings	1	12-Apr-27	12-Apr-27																		
C178	Prep and weld 8no Flange plates to longitudinal beams in final bearing positions	5	13-Apr-27	19-Apr-27																		
C179	NDT Welds	0	20-Apr-27	20-Apr-27																		
C180	Bolt up 8no EKSPAN Spherical bearings	1	20-Apr-27	20-Apr-27																		
C181	Shutter and cast concrete to 8no bearing positions	2	21-Apr-27	22-Apr-27																		
C182	Concrete cure	5	23-Apr-27	29-Apr-27																		
C183	Shutter and cast grout bed to 8no positions	2	30-Apr-27	04-May-27																		
C184	Grout cure	1	05-May-27	05-May-27																		
C185	Confirm cube strength for concrete & grout	0	06-May-27	06-May-27																		
C186	De-Jack structure (Night working) & Install 3 week period for monitoring	1	26-Jul-27	26-Jul-27																		
C187	Strike Shutters, fettle grout beds	2	27-Jul-27	28-Jul-27																		
C188	Install 35 meters of ES seal using resin fixed anchors @ 200mm centers - 328 drilled holes	7	29-Jul-27	06-Aug-27																		
C189	Remove restraints, hydraulic cylinders, transom beams and make good of works area	7	09-Aug-27	17-Aug-27																		
C190	Paint end beams, flange plates & bearing fixings	5	18-Aug-27	24-Aug-27																		
C191	Remove monitoring	1	25-Aug-27	25-Aug-27																		
Hydrophobic Impregnation - Alun Griffiths		9	26-Aug-27	08-Sep-27																		
C193	Complete Hydrophobic Impregnation - Abutments																					
