

Welsh Government


**M4 Corridor around Newport**

August 2017 Environmental  
Statement Supplement  
Appendix ESS5 3.1

Navigation Risk Assessment  
(August 2017)

M4CaN-DJV-EGN-ZG\_GEN-AX-EN-0024

At Issue | August 2017



# M4 Corridor around Newport

## Navigation Risk Assessment

For Arcadis

GM-16-00052-476653

| Rev | Date | Document Status | Manager,<br>Ports and<br>Shipping                                                   | Senior<br>Engineer                                                                   | Manager,<br>Ports and<br>Shipping                                                     |
|-----|------|-----------------|-------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|
|     |      |                 |  |  |  |
|     |      |                 | Jonathan Vine                                                                       | Lovinash Bonomaully                                                                  | Jonathan Vine                                                                         |
| Rev | Date | Document Status | Prepared by                                                                         | Reviewed by                                                                          | Approved by                                                                           |

## Table of Contents

|                                                                           |           |
|---------------------------------------------------------------------------|-----------|
| <b>1. SUMMARY .....</b>                                                   | <b>4</b>  |
| <b>2. INTRODUCTION .....</b>                                              | <b>8</b>  |
| 2.1 M4 CORRIDOR AROUND NEWPORT.....                                       | 8         |
| 2.2 SCOPE OF WORK.....                                                    | 9         |
| 2.3 ACRONYMS .....                                                        | 9         |
| <b>3. SHIPPING ACTIVITY .....</b>                                         | <b>12</b> |
| 3.1 OVERVIEW.....                                                         | 12        |
| 3.2 RIVER USK .....                                                       | 13        |
| 3.3 ABP NEWPORT DOCKS .....                                               | 13        |
| 3.4 RIVER EBBW .....                                                      | 14        |
| <b>4. STAKEHOLDERS .....</b>                                              | <b>16</b> |
| 4.1 OVERVIEW.....                                                         | 16        |
| 4.2 NEWPORT HARBOUR COMMISSIONERS .....                                   | 16        |
| 4.3 ASSOCIATED BRITISH PORTS.....                                         | 17        |
| 4.4 THE ROYAL YACHTING ASSOCIATION.....                                   | 18        |
| 4.5 THE CORPORATION OF TRINITY HOUSE .....                                | 18        |
| 4.6 MARITIME AND COASTGUARD AGENCY .....                                  | 19        |
| 4.7 HANSON AGGREGATES .....                                               | 19        |
| 4.8 CARGO SERVICES (U.K) LIMITED .....                                    | 20        |
| 4.9 SMS TOWAGE .....                                                      | 22        |
| <b>5. NAVIGATIONAL RISK WORKSHOP (22<sup>ND</sup> NOVEMBER 2016).....</b> | <b>23</b> |
| 5.1 CONSULTATION .....                                                    | 23        |
| 5.2 OVERVIEW.....                                                         | 23        |
| 5.3 BOUNDARIES AND ASSUMPTIONS .....                                      | 24        |
| 5.4 ATTENDEES .....                                                       | 24        |
| 5.5 RISK ACCEPTANCE CRITERIA .....                                        | 26        |
| 5.6 HAZARD ASSESSMENT.....                                                | 29        |
| 5.7 GM'S RISK MANAGEMENT TOOL .....                                       | 30        |
| 5.8 RESULTS.....                                                          | 30        |
| 5.9 EVENTS .....                                                          | 31        |
| 5.10 CONSEQUENCE.....                                                     | 32        |
| <b>6. MEETINGS WITH OTHER STAKEHOLDERS .....</b>                          | <b>33</b> |
| 6.1 THE CORPORATION OF TRINITY HOUSE .....                                | 33        |
| 6.2 CARGO SERVICES (UK) LTD.....                                          | 34        |
| <b>7. VESSEL COLLISION WITH ROAD BRIDGE OVER DOCKS.....</b>               | <b>36</b> |
| 7.1 NRA WORKSHOP – NEWPORT DOCKS .....                                    | 36        |
| 7.2 GEOMETRIC ASSESSMENT.....                                             | 36        |
| 7.3 SHIP IMPACT ASSESSMENT .....                                          | 37        |
| 7.4 BRIDGE PROTECTION MEASURES .....                                      | 37        |
| 7.5 FURTHER RISK WORKSHOP (10 <sup>TH</sup> AUGUST 2017).....             | 38        |

## 8. RECOMMENDATIONS .....40

### Appendices

**APPENDIX A WORKSHOP ATTENDANCE SHEET, 22<sup>ND</sup> NOVEMEBER 2016**

**APPENDIX B RISK MANAGEMENT TOOL**

**APPENDIX C NAVIGATION RISK REGISTER (22<sup>ND</sup> NOVEMBER 2016)**

**APPENDIX D MEETING WITH TRINITY HOUSE, 9<sup>TH</sup> DECEMBER 2016**

**APPENDIX E MEETING WITH CARGO SERVICES (UK) LTD, 8<sup>TH</sup> DECEMBER 2016**

**APPENDIX F BRIDGE PROTECTION MEASURES**

**APPENDIX G WORKSHOP ATTENDANCE SHEET, 10<sup>TH</sup> AUGUST 2017**

**APPENDIX H NEWPORT DOCK UPDATED RISK REGISTER (10<sup>TH</sup> AUGUST 2017)**

These materials are the Work Product of Global Maritime, and no reliance on this work product is authorised by Global Maritime, and Global Maritime accepts no liability for any reliance by any person on the work product contained herein.

© This document is the property of Global Maritime Consultancy Ltd. and is not to be copied, nor shown, to third parties without prior consent.

**Global Maritime Consultancy Ltd.**  
Saddlers House  
44 Gutter Lane, Cheapside  
London, EC2V 6BR, England

T +44 (0) 203 465 2500  
F +44 (0) 203 465 2501



REGISTERED IN ENGLAND AND WALES NO. 03201590

## 1. SUMMARY

- 1.1.1 The Welsh Government proposes, as part of the M4 Corridor around Newport Project (from hereon in referred to as 'the Project' or 'the Scheme' to build a new section of motorway to the south of the city of Newport in South Wales.
- 1.1.2 The new section of motorway would run between Junction 29 at Castleton and Junction 23 at Magor. To the east of the Castleton, it would pass to the south of Duffryn before crossing the Rivers Ebbw and Usk to the south of the A48 at Newport Docks.
- 1.1.3 Global Maritime Consultancy (GMC) was instructed by the Welsh Government to assess the impact of the proposed Scheme to the users of the River Usk, River Ebbw and the Newport Docks. The assessment covers both the impact to navigation during the construction and operational phases of the scheme.
- 1.1.4 A navigation risk assessment (NRA) workshop was conducted on the 22<sup>nd</sup> November 2016. The workshop was attended by representatives from Newport Harbour Commissioners (NHC), Associated British Ports (ABP), the Royal Yachting Association (RYA), the Maritime and Coastguard Agency (MCA), SMS Towage, Hanson Aggregates and various members of the M4 CaN Project team.
- 1.1.5 In addition to the NRA workshop, separate meetings were held with Cargo Services (UK) Ltd. on 8<sup>th</sup> December 2016 and with the Corporation of Trinity House on 9<sup>th</sup> December 2016.
- 1.1.6 A HAZID (Hazard Identification) methodology was adopted for the assessment in line with the recommendations of the Port Marine Safety Code (PMSC) and associated guide to good practice (GTGP). The process allowed for a full and detailed discussion with stakeholders, in order to identify the areas of risk, assess the consequences of an event occurring as a result of the risk and to ensure that mitigations or actions are developed in order to reduce the risk. The overall aim was to ensure that all risks are acceptable and as low as reasonably practicable, in accordance with the ALARP principle.
- 1.1.7 In parallel to the above process, GMC conducted a geometric assessment which consisted of the modelling of potential ship impact scenarios with the proposed bridge over the Newport Docks. The geometric assessment concluded that there was potential for errant vessels to contact the bridge structure and support piers with either the vessels' superstructure or bow.
- 1.1.8 Following on from the geometric assessment conducted by GMC a simple probabilistic study in accordance with Eurocodes BS EN 1991-1-7:2006+A1:2014 and supplemented by the UK National Annex and PD 6688-1-7 was conducted by ARUP. The findings of the study are reported in the document M4CaN-DJV-SBR-Z3-GEN-RP-CB-0027.
- 1.1.9 The probabilistic assessment determined that where the proposed bridge crosses Newport Docks at the Junction Cut, the probability of failure is  $2.4 \times 10^{-4}$  per annum (or 2.8% probability of failure over the design life of 120 years). When compared to the recognised level of acceptance data as detailed in Eurocode and DMRB GD04/12 it was found that if this level of risk, if left unmitigated, was considered to be 'unacceptable'.

- 1.1.10 In order to reduce the level of risk to 'tolerable', 'broadly acceptable' or 'acceptable', the introduction of robust mitigation measures would be required.
- 1.1.11 In order to mitigate the potential risk of vessels making colliding with the bridge structure and support piers within the Docks the Welsh Government in consultation with ABP have proposed a number of robust mitigation measures.
- 1.1.12 The mitigation measures proposed include:
- An extension of quayside on either side of the Junction Cut into the South Dock approximately 50m in order to prevent errant vessels making contact with the proposed bridge piers and/or bridge structure. The proposed build-out will have the effect of extending the Junction Cut into the South Dock and will comprise of a backfilled combi-pile walls. The run-in and sides of the newly formed Junction Cut are to be fendered to prevent damage to the quay walls and vessels transiting through.
  - The Junction Cut is to be narrowed to a width of 11m, analysis of historical vessel movements within the Dock has shown that vessels with beam width of 11m or less do not have a high enough air draught to make contact with the bridge.
  - The WG have also considered the installation of some form of electro-optical sensors to be located in the South Lock to act as a virtual trip wire for vessels locking into the South Lock prior to entry into the Docks. The sensors will be able to accurately measure the air draught of vessels alerting the operator of any potential issues prior to the vessel entering the Docks.
- 1.1.13 Further collaboration with ABP in the form of a further navigation risk assessment workshop was held on the 10<sup>th</sup> of August 2017 to address the risk of vessels potentially colliding with the proposed bridge over Newport Docks with the above mitigation measures in place. The workshop was attended by representatives from Associated British Ports (ABP), the Maritime and Coastguard Agency (MCA), SMS Towage, various members of the M4 CaN Project team and Global Maritime (GMC).
- 1.1.14 During the construction phases of the crossings over the river Ebbw, the river Usk and Newport Docks, the main risks to navigation were identified as follows:
- 1) Vessel collision with the bridges crossing the rivers Usk and Ebbw and Newport Docks.
  - 2) Collapse of bridge deck and/or a dropped bridge deck section
  - 3) Other dropped objects (such as tools)
  - 4) Pollution caused by the construction activities or floating debris
  - 5) Congested navigation
  - 6) Conflict with radio communications
  - 7) Presence of background light from construction activities and/or road lighting

8) Congested Newport South dock during periods of restricted access to the North Dock

1.1.15 During the operational phase of the Scheme, the navigation risks to the crossings were identified as follows:

- 1) Vessel collision with the bridge structure and/or support piers
- 2) Dropped objects (such as tools) during maintenance activities
- 3) Pollution caused by maintenance activities and/or floating debris
- 4) Falling objects from the bridge
- 5) Congested Newport South Dock during periods of restricted vessel access to the North dock

1.1.16 The mitigation measures recommended for the construction and the operational phases of the Scheme are broadly defined under the following subheadings:

1) Promulgation of Marine Safety Information

- Navigation warnings and notices to mariners (NTMs) are to be promulgated to all river users in order to inform them of any construction activities and in particular periods when navigation will be restricted.
- Engagement by the project team with stakeholders, dock and river users in order to ensure that navigational warnings have been received and understood.
- Navigation lights to be installed on the river crossings, both upstream and downstream, in order to identify the best point of passage for mariners and river users.
- Safety signage to be in place on the river banks in order to warn river users of low bridge heights, the vertical clearance and identify best point of passage during the day.
- Major bridge maintenance works are to be communicated by Notices to Mariners and navigation warnings.

2) Vessel Traffic Management

- River access to be actively managed during deck launching/lifting over water, when restrictions on navigation may be imposed.
- Continual monitoring of traffic, with a guard vessel available in order to assist in enforcing any restrictions.
- Vessel movements and personnel access at Dallimore's Wharf, to be managed during bridge construction and maintenance operations.
- Small vessels using the River Ebbw are to be monitored by project personnel during construction and maintenance operations.
- No vessels and/or personnel are to be beneath a suspended load during any lifting operations.
- Tugs and small vessels presently berthing in the Newport North Dock in the vicinity of the 'Junction Cut' are to be relocated.

3) Management of Dropped Object Risk

- Dropped object prevention measures are to be implemented at the construction site and during maintenance works.
- Bridge design to include reasonable measures to prevent falling objects.
- Un-authorized access to be prevented by appropriate security controls.
- Dropped object recovery plan to be implemented.
- Mariners and stakeholders to be advised of any dropped objects and/or floating debris which may affect navigation.

#### 4) Marine Safety Management System

- The Port Marine Safety Code requires ABP as the statutory harbour authority (SHA) to maintain marine safety management plan system (MSMS) for marine operations and navigation within Newport Docks. The MSMS must be based on formal risk assessment of these operations.
- Develop interface document and a marine management plan to formalise interfaces, including the emergency primacy between parties.
- Clear communications plan between relevant parties during critical construction activities.

#### 5) Pollution Control

- Construction Environmental Management Plan (CEMP) to include pollution containment procedures and good housekeeping practices.
- Harbour Authority Oil Pollution Preparedness and Response Plan (OPRC).
- Bridge maintenance manual to include pollution response procedures.

#### 6) Direct Interference

- Consider interference of construction radio communications with vessel radio communications, dedicated channels to be in use.
- Construction site flood lighting equipment set-up to consider impairment of mariners' night vision (i.e. positioning/direction of lighting).

## 2. INTRODUCTION

### 2.1 M4 Corridor around Newport

- 2.1.1 The Welsh Government (WG) proposes to build a new section of motorway to the south of the City of Newport in South Wales. The proposed scheme is referred to as the M4 Corridor around Newport (M4 CaN).
- 2.1.2 The proposed new section of motorway would run between Junction 29 at Castleton and Junction 23 at Magor. To the east of the Castleton junction, the proposed new section of motorway would depart from the route of the existing M4 motorway at Junction 29 and would pass to the south of Duffryn before crossing the Rivers Ebbw and Usk to the south of the A48 and across the 'Junction Cut' at Newport Docks.
- 2.1.3 The route for the proposed new section of motorway would cross the South Wales to London mainline railway to the south of Duffryn and to the west of Magor. In addition, the route would cross a number of existing highways, rights of way and private means of access. The proposed new section of motorway would also cross the River Usk, River Ebbw and Newport Docks at a point between the South Dock and the North Dock known as the 'Junction Cut' as can be seen in Figure 2-1.



Figure 2-1 M4 Corridor - Usk, Ebbw and Newport docks crossing

- 2.1.4 Newport Docks, the rivers Ebbw and Usk are principally used by commercial vessels and recreational craft, therefore the Scheme may have an impact on the navigation of vessels using these waterways. Figure 2-2 shows an artist's impression of the proposed River Usk crossing.



Figure 2-2 Artists Impression of the River Usk Crossing

## 2.2 Scope of work

- 2.2.1 Global Maritime (GMC) was instructed by the Welsh Government (WG) in June 2016 to facilitate a formal navigation risk assessment of the potential impact, in terms of navigation, that the proposed Scheme may have on users of rivers Usk, Ebbw and Newport Docks. GMC received further instructions to conduct a follow-up NRA in July 2017, to reassess the impact on the Newport following the potential inclusion of bridge protection measures proposed by the WG.

## 2.3 Acronyms

|       |                                            |
|-------|--------------------------------------------|
| AAJV  | Atkins Arup Joint Venture                  |
| ABP   | Associated British Ports                   |
| ACD   | Admiralty Chart Datum                      |
| ALARP | As Low as Reasonably Practicable           |
| AOD   | Above Ordnance Datum                       |
| CEMP  | Construction Environmental Management Plan |

|        |                                                                       |
|--------|-----------------------------------------------------------------------|
| CHA    | Competent Harbour Authority                                           |
| CSL    | Cargo Services Ltd.                                                   |
| DWT    | Dead Weight Tonne                                                     |
| GLA    | General Lighthouse Authority                                          |
| GMC    | Global Maritime Consultancy                                           |
| GTGP   | Guide to Good Practice                                                |
| HAZID  | Hazard Identification                                                 |
| IALA   | International Association to Marine Aids to Navigation and Lighthouse |
| IMO    | International Maritime Organisation                                   |
| LOA    | Length Overall                                                        |
| LPS    | Local Port Services                                                   |
| MCA    | Maritime and Coastguard Agency                                        |
| MSMS   | Marine Safety Management System                                       |
| MHWS   | Mean High Water Springs                                               |
| M4 CaN | M4 Corridor Around Newport                                            |
| NAASBA | Not Always Afloat but Safely Aground                                  |
| NRA    | Navigation Risk Assessment                                            |
| NHC    | Newport Harbour Commissioners                                         |
| NUSC   | Newport Uskmouth Sailing Club                                         |
| NTMs   | Notices to Mariners                                                   |
| PEC    | Pilot Exemption Certificate                                           |
| PMSC   | Port Marine Safety Code                                               |
| RMT    | Risk Management Tool                                                  |
| RPS    | RPS Group                                                             |
| RYA    | Royal Yachting Association                                            |
| SAR    | Search and Rescue                                                     |
| SHA    | Statutory Harbour Authority                                           |

|      |                                    |
|------|------------------------------------|
| UKHO | United Kingdom Hydrographic Office |
| VHF  | Very High Frequency                |
| WG   | Welsh Government                   |

### 3. SHIPPING ACTIVITY

#### 3.1 Overview

- 3.1.1 Figure 3-1 below, shows the route for the proposed M4 motorway within the Newport area and shows the proposed crossing points over Newport Docks and the Usk. The plan also shows the active and disused berths on the river and operations presently active within the dock system.

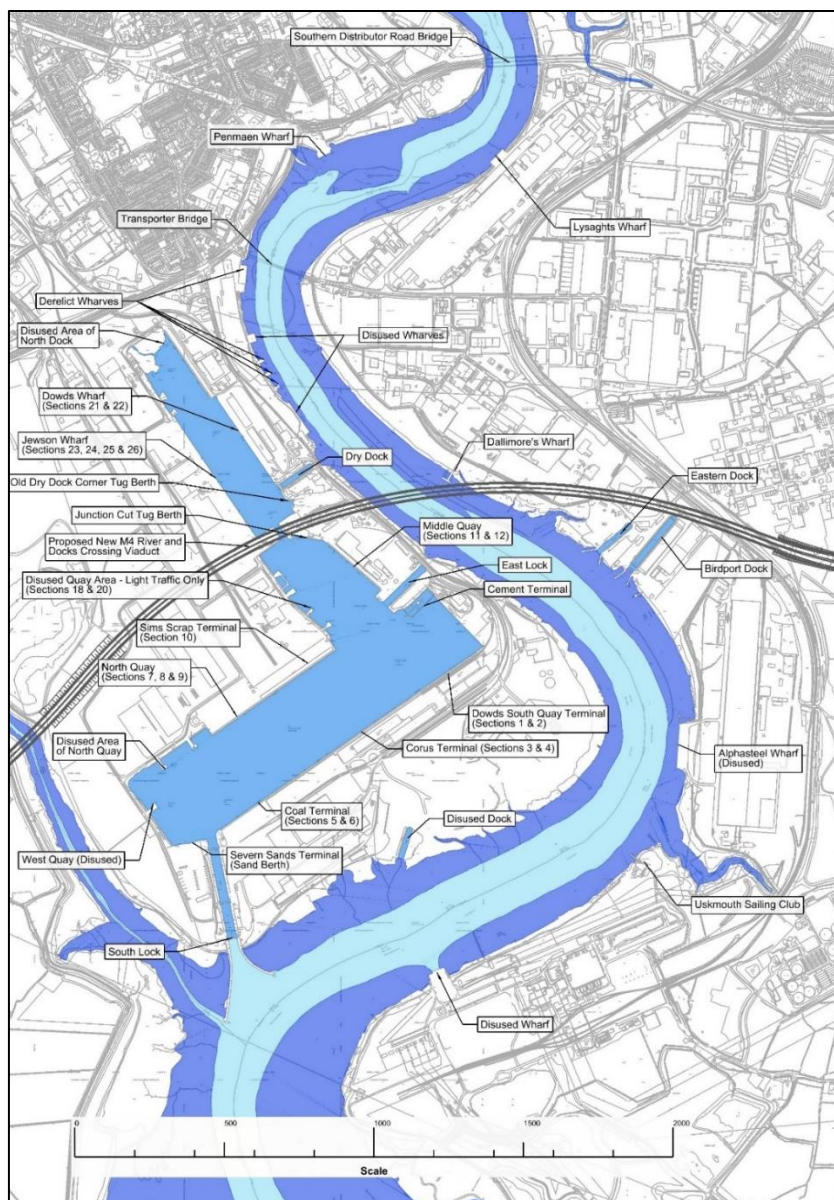


Figure 3-1 Rivers Ebbw and Usk and Newport Docks

### 3.2 River Usk

- 3.2.1 Marine traffic on the River Usk comprises of both commercial and recreational vessel activity.
- 3.2.2 The construction of the new Southern Distributor Road (SDR) Bridge over the River Usk upstream of Lysaght's Wharf (see Figure 3-1) has restricted the air draft clearance above the river channel. Therefore, the disused berths upstream of the SDR Bridge have not been considered for this risk assessment.
- 3.2.3 As can be seen in the Figure 3-1 above, the proposed crossing is to be located in close proximity to Dallimore's Wharf on the eastern side of the river Usk. Dallimore's wharf is situated up stream of the proposed bridge and is presently used to discharge aggregate cargoes. Lysaght's and Penmaen wharves are presently not in use.
- 3.2.4 A cable stay bridge has been designed to cross the River Usk, as shown in Figure 3-2 below. The design of the bridge is such that the bridge piers are outside the wetted channel. The minimum clearance taken from Mean High Water Springs (MHWS) level to the underside soffit of the bridge is 33.54 m.

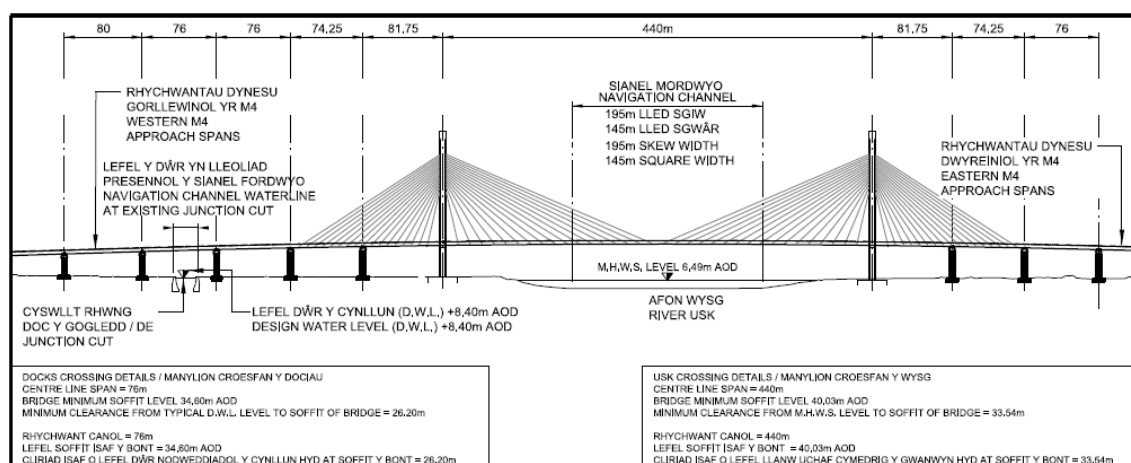


Figure 3-2 River Usk Crossing

### 3.3 ABP Newport Docks

- 3.3.1 Newport Docks are situated on the north side of the river Usk and comprise of the North and South docks as can be seen in Figure 3-3. The two docks are joined by an access known as the Junction Cut.
- 3.3.2 Newport Docks handle a wide variety cargo such as timber, bulk cargoes, agri-bulk cargoes, steel products, scrap steel, coal, explosives, aggregates and project cargoes.
- 3.3.3 Under the proposed Scheme it is intended to construct a road bridge crossing the Newport Docks at the access point between the North and South Docks known as the Junction Cut.

- 3.3.4 The bridge design allows for a 26.2m vertical clearance between the maximum retained dock water level of 8.40m(AOD) and the underside of the soffit of the proposed bridge of 34.60 m (AOD).



Figure 3-3 Newport Docks

### 3.4 River Ebbw

- 3.4.1 River Ebbw is not navigable by the larger commercial vessels that typically serve the Newport Docks and the river Usk. The river Ebbw is however used by small privately owned recreational vessels such as dinghies, kayaks and small motor cruisers.
- 3.4.2 Figure 3-5 shows the minimum vertical clearance from the Mean High Water Springs (MHWS) level to underside of the bridge soffit is 4.01 metres.



Figure 3-4 River Ebbw

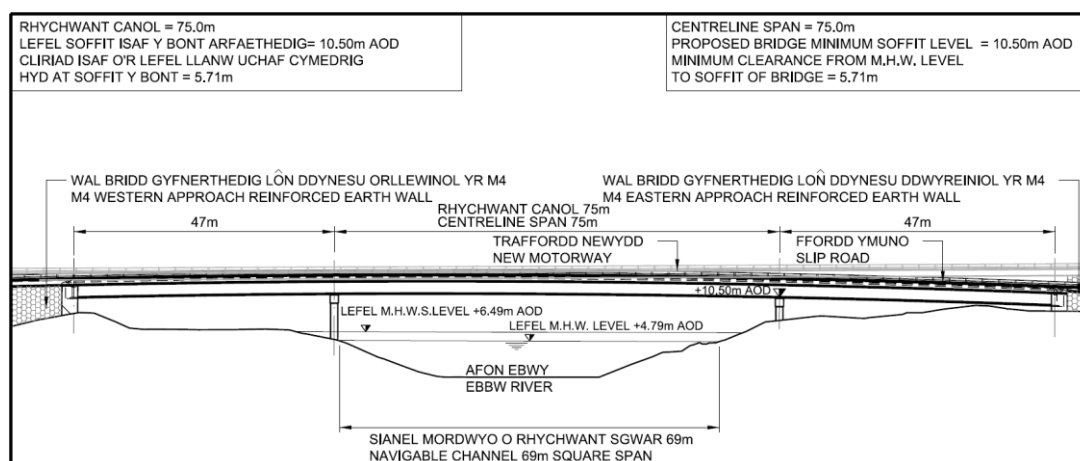


Figure 3-5 River Ebbw Crossing

## 4. STAKEHOLDERS

### 4.1 Overview

- 4.1.1 As far as practicable, as wide a range of stakeholders as possible were identified for attendance at the NRA and encouraged to participate in the hazard identification process.

### 4.2 Newport Harbour Commissioners

- 4.2.1 The Newport Harbour Commissioners are the Statutory and Competent Harbour Authority for the Port of Newport. The NHC's area of jurisdiction does not include Newport Docks and is shown on the navigation chart in Figure 4-1 below:

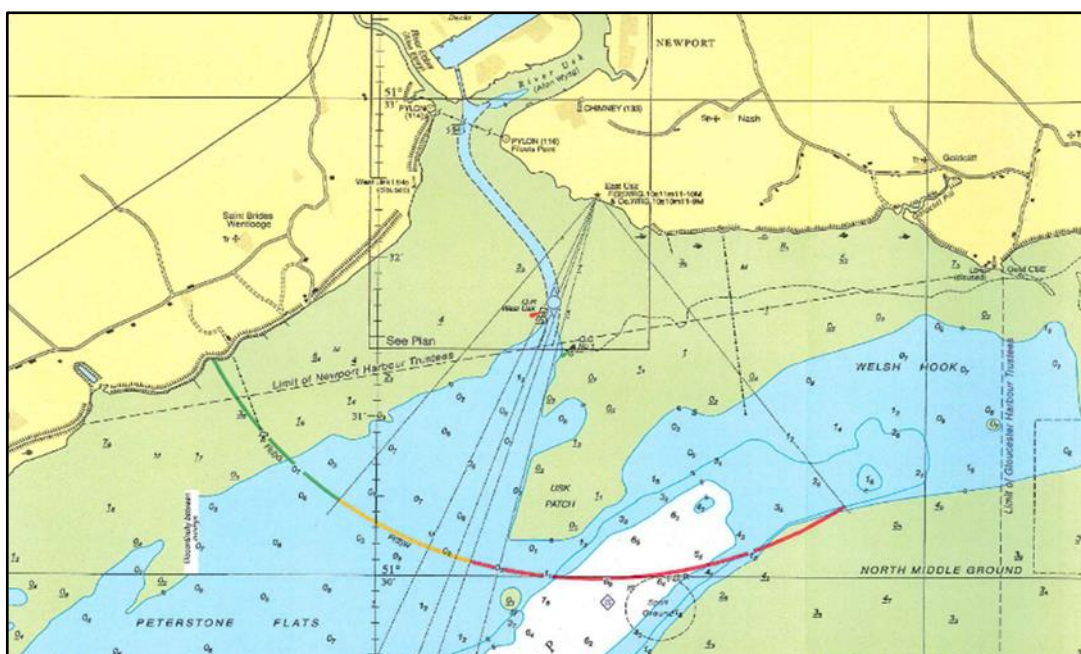


Figure 4-1 The extent of NHC's Jurisdiction as SHA

- 4.2.2 Their responsibilities include, but are not limited to:
- Regulation of navigation within statutory harbour limits.
  - Provision of a pilotage service.
  - Local lighthouse authority establishing and maintaining lights and marks.
  - Hydrographic surveying of harbour area.
  - Removal of wrecks.

- To make and enforce byelaws relating to the conduct of vessels and promulgate that information by appropriate means, as required to ensure all harbour users are aware of the requirement for safe navigation in the harbour area.
- To act upon observations of contracted Marine staff and stakeholders to ensure compliance with byelaws.
- Advising stakeholders port waste reception facilities.
- Development of harbour oil spill contingency plans as required by the Merchant Shipping (Oil Pollution Preparedness Response and Co-operation Convention) Regulations 1998.

4.2.3 Many of the NHC's responsibilities, such as pilotage, are carried out by ABP under contract.

### **4.3 Associated British Ports**

- 4.3.1 Associated British Ports (ABP) own and operate the Newport Docks and are the Statutory and Competent Harbour Authority for the docks.
- 4.3.2 As the Competent Harbour Authority the company has been conferred statutory powers under enabling legislation (principally the Harbours Act 1964, the Pilotage Act 1987, the Marine Navigation Act 2013 and local legislation) to, amongst other things, create bylaws, provide a pilot service and direct shipping.
- 4.3.3 ABP's jurisdiction in the above role extends for a distance of 100 yards beyond the Newport Docks boundary as can be seen in Figure 4-2.

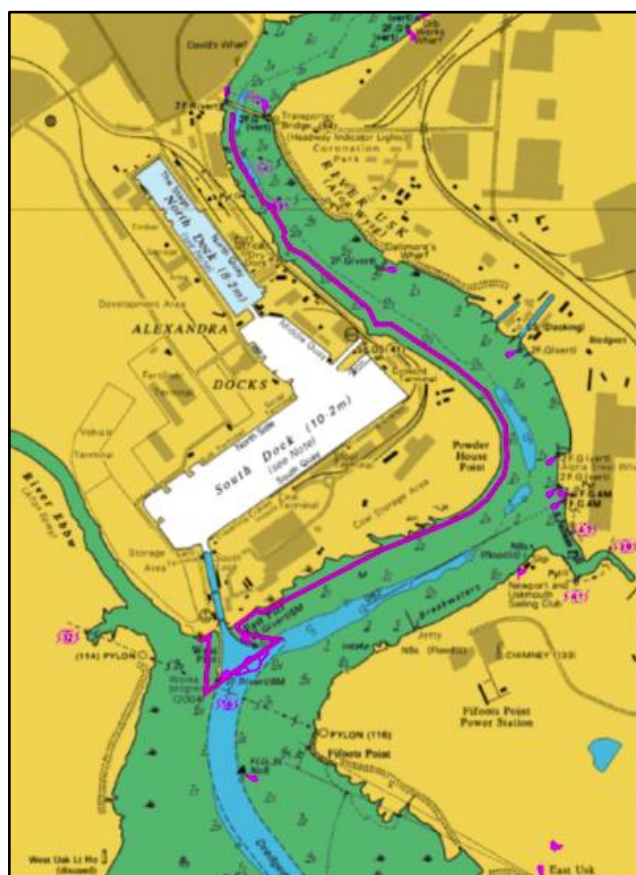


Figure 4-2 Extent of ABP's Jurisdiction as SHA

#### 4.4 The Royal Yachting Association

- 4.4.1 The Royal Yachting Association (RYA) is the national body for all forms of boating, including dinghy and yacht racing, motor and sail cruising, RIBs, powerboat racing, windsurfing, canal boats, river boat cruising and personal watercraft.
- 4.4.2 The RYA were invited to participate in the navigation risk assessment workshop as a key stakeholder in the interests of recreational boat owners within the Newport area and to communicate the findings of the workshop to its members.

#### 4.5 The Corporation of Trinity House

- 4.5.1 Trinity House is the General Lighthouse Authority (GLA) for England, Wales, the Channel Islands and Gibraltar. Trinity House is a corporation established by Royal Charter, and its powers as a GLA are principally derived from the Merchant Shipping Act 1995, as amended.
- 4.5.2 Their primary role is to deliver a reliable, efficient and cost-effective aids to navigation service for the benefit and safety of all mariners commensurate with

the level of risk. This includes the superintendence and management of all lighthouses, buoys and beacons within our area.

#### **4.6 Maritime and Coastguard Agency**

- 4.6.1 With their main headquarters in Southampton, UK, the Maritime Coastguard Agency (MCA) is an executive agency, sponsored by the Department for Transport and is set up in order to prevent the loss of life on the UK coast and at sea.
- 4.6.2 The MCA advises on legislation, produce guidance on maritime matters, and provide certification to seafarers.
- 4.6.3 The MCA are mainly responsible for:
  - The provision of a 24-hour maritime search and rescue (SAR) service.
  - The safety of all persons on a vessel in UK waters.
  - Ensuring all vessels and their equipment meet UK and International standards.
  - UK ship registration.
  - Seafarers' standards, certification, health and safety.
  - The environmental safety of the UK coast and waters.
  - The accuracy of hydrographic data on UK charts.
  - Overseeing the port state control inspection regime.
  - The arrest and detention of substandard and unseaworthy vessels.

#### **4.7 Hanson Aggregates**

- 4.7.1 Hanson Aggregate Marine operate a fleet of trailing suction hopper dredgers and are Europe's largest producer of marine dredged sand and gravel.
- 4.7.2 Their operation in the Newport area is run from their facility at Dallimore's Wharf situated on the river Usk, see Figure 4-3 below.
- 4.7.3 Their suction hopper dredgers the Arco Dart and Welsh Piper are regular visitors to Dallimore's Wharf, berthing port side alongside in order to discharge aggregate cargoes.
- 4.7.4 The vessel's berthing at Dallimore's wharf are in the region of 68 metres in length (LOA) and therefore overhang the berth by a considerable amount, resulting in their bows positioned close to the proposed river Usk crossing.



Figure 4-3 Dallimore's Wharf

#### **4.8 Cargo Services (U.K) Limited**

- 4.8.1 Cargo Services (U.K) Limited operate Birdport which is situated on the eastern side of the river Usk approximately 0.3 nm downstream from the proposed River Usk crossing as depicted in Figure 4-4.
- 4.8.2 The port handles a wide range of commodities such as steel products, bulk cargoes and timber.
- 4.8.3 The port consists of a gated dock which is capable of handling vessels of up to 8,000 DWT.
- 4.8.4 Vessels visiting the dock are categorised for insurance purposes as 'Not Always Afloat but Safely Aground' (NAABSA).

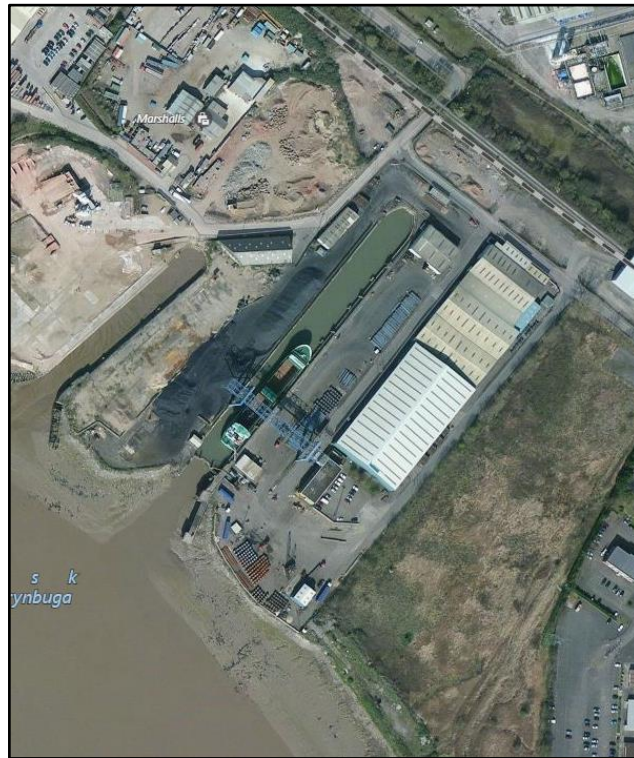


Figure 4-4 Birdport

#### 4.9 SMS Towage

- 4.9.1 SMS Towage provides harbour towage facilities for vessels in the Bristol Channel and operate from the South Wales Ports of Cardiff, Barry and Newport.
- 4.9.2 SMS Towage harbour tugs are regularly berthed on the north eastern side of the Junction Cut as can be seen in **Error! Reference source not found.** below, in order to load bunkers and fresh water, rest crews, change out crew members, carry out maintenance and stand-by awaiting call-out.
- 4.9.3 Tug crew members live on board their vessels during their period of engagement.



Figure 4-5 SMS Harbour Tug - Trueman

#### 4.9.4

## **5. NAVIGATIONAL RISK WORKSHOP (22<sup>ND</sup> NOVEMBER 2016)**

### **5.1 Consultation**

- 5.1.1 As recognised by the Welsh Government, safety is of paramount importance for all parties involved in marine operations within the port of Newport, whether commercial or leisure, and is no longer the sole responsibility of the Statutory Harbour Authority (SHA).
- 5.1.2 The Welsh Government felt it was essential to involve those working within and using the port in the risk assessment process and any further reviews in order to utilise their specialist knowledge and skills.

### **5.2 Overview**

- 5.2.1 The approach adopted for this formal risk assessment was a HAZID (Hazard Identification). The process allows for a full and detailed discussion with main stakeholders in order to identify the areas of risk and to assess the consequences of an event occurring as a result of the risk. From this, mitigations or measures are introduced in order to reduce the risk to an acceptable level.
- 5.2.2 The methodology satisfies the requirements of a Formal Safety Assessment (FSA), as set out by the International Maritime Organisation (IMO), and recommended by the Port Marine Safety Code (PMSC) and associated guides to good practice (GTGP).
- 5.2.3 An FSA is defined by the IMO as “a structured and systematic methodology, aimed at enhancing maritime safety, including protection of life, health, the marine environment and property, by using risk analysis and cost benefit assessment. FSA can be used as a tool to help in the evaluation of new regulations for maritime safety and protection of the marine environment or in making a comparison between existing and possibly improved regulations, with a view to achieving a balance between the various technical and operational issues, including the human element, and between maritime safety or protection of the marine environment and costs”.
- 5.2.4 This planned Formal Risk Assessment consists of a five step approach, as follows:
  - 1) Identification of hazards (a list of all relevant accident scenarios with potential causes and outcomes);
  - 2) Assessment of risks (evaluation of risk factors);
  - 3) Risk control options (devising regulatory measures to control and reduce the identified risks);
  - 4) Cost benefit assessment (determining cost effectiveness of each risk control option); and
  - 5) Recommendations for decision-making (information about the hazards, their associated risks and the cost effectiveness of alternative risk control options is provided).

- 5.2.5 The approach adopted for this navigation risk assessment incorporates steps 1, 2 and 3. Steps 4 and 5 are outside the scope of this assessment and are considered in the construction risk assessment.

### **5.3 Boundaries and Assumptions**

- 5.3.1 The risk assessment focussed on the risk to navigation during both the construction and operational phases of the Scheme. Risks associated with the construction activities are covered in the relevant construction risk register prepared by the project team.
- 5.3.2 In order to focus the assessment on navigational issues only, it was necessary to define the study area, with all parties taking an objective approach to the exercise.
- 5.3.3 The boundaries of the assessment were defined as follows:
- Newport Harbour Commissioners – Statutory Harbour Authority limits of jurisdiction
  - Newport Docks – ABP Statutory Harbour Authority limits of jurisdiction
- 5.3.4 The assumptions adopted during the HAZID process were:
- All vessels using the navigable waterways at issue in this study are seaworthy. However, it is recognised that errant vessels may not be in a seaworthy condition and vessel issues may not have been reported by the vessel master to the pilot and or harbour authority.
  - The relevant harbour authority would be responsible for managing the response to an incident that occurs within their jurisdiction.
  - Crews would be well trained and competent in compliance with industry standards and regulations. However, it is recognised that human error can be a contributory factor in marine accidents and incidents.
  - Pilots and Pilot Exemption Certificate (PEC) holders are competent and experienced in ship handling. However, it is recognised that human error can be a contributory factor in marine accidents and incidents.
  - When used, tugs have the minimum bollard pull and capabilities as required. However, it is recognised that in some circumstances tugs' equipment and/or machinery can fail, and that human error can be a further contributory factor in marine accidents and incidents.
  - Recreational users of the waterways are not always safety conscious, well trained, experienced, nor are they always affiliated to local clubs or the RYA.

### **5.4 Attendees**

- 5.4.1 The formal risk assessment on the impact to navigation as a result of the proposed Scheme was carried out at the M4 CaN Project office at Longcross Court in Cardiff.

5.4.2 The attendees comprised of members of the M4 CaN project team, port users and stakeholders with an interest in any potential impact the Scheme may have on navigational safety.

5.4.3 A signed attendance sheet is included in Appendix A.

| <b>Name</b>         | <b>Position</b>           | <b>Company</b>                 |
|---------------------|---------------------------|--------------------------------|
| Miles Chidlow       | Harbour Master            | Newport Harbour Commissioners  |
| Rod Lewis           | Marine Operations Manager | Associated British Ports       |
| Sean Hunter         | Project Manager           | Hanson Aggregates              |
| Charlie Smith       | First mate                | Hanson Aggregates              |
| Peter Baker         | M.C.A Surveyor            | Maritime and Coastguard Agency |
| Peter Ireland       | Environmental Coordinator | RPS Group                      |
| Eunince Stephenson  | Environmental Consultant  | RPS Group                      |
| Patrick Lyon        | Managing Director         | SMS Towage                     |
| Mike Butterfield    | Chairman, Cyrmu Wales     | Royal Yachting Association     |
| Jonathan Vine       | Principal Mariner         | Global Maritime                |
| Lovinash Bonomaully | Senior Engineer           | Global Maritime                |
| Dave Ritchie        | QHSE Manager              | Global Maritime                |
| Martin Bates        | Project Director          | Welsh Government               |
| Peter Allott        | Civil Engineer            | Arup                           |
| Barry Woodman       | Project Director          | Vinci-Costain JV               |
| Matthew Jones       | Project Engineer          | Welsh Government               |

Table 5-1 List of attendees

## 5.5 Risk acceptance criteria

- 5.5.1 GMC's risk scoring matrix has been developed based on guidance from the International Marine Contractors Association (IMCA); and the International Maritime Organization (IMO) in line with the requirements of the PMSC and associated guidance.
- 5.5.2 The risk scoring matrix is presented in Figure 5-1, and shows a standard 5 x 5 risk matrix. The levels of risk and their significance for decision making are presented in Figure 5-2. The definitions for the different Severity Categories and Probability Ratings are presented in Figure 5-3 and Figure 5-4.

| Severity Category  | Probability          |                 |                 |               |                    |
|--------------------|----------------------|-----------------|-----------------|---------------|--------------------|
|                    | A<br>(Very Unlikely) | B<br>(Unlikely) | C<br>(Possible) | D<br>(Likely) | E<br>(Very Likely) |
| 1<br>(Negligible)  | L                    | L               | L               | M             | M                  |
| 2<br>(Minor)       | L                    | L               | M               | M             | M                  |
| 3<br>(Significant) | L                    | M               | M               | M             | H                  |
| 4<br>(Serious)     | M                    | M               | M               | H             | H                  |
| 5<br>(Critical)    | M                    | M               | H               | H             | H                  |

Figure 5-1 Matrix

| Risk Level    |                                                                                                                                                                                                           |                                                                                                              |
|---------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------|
| <b>LOW</b>    | As a guide, when a LOW risk level is calculated, then no additional controls are required. However monitoring should take place to ensure that the controls are implemented and where possible, improved. | <b>Acceptable</b><br>Task/ Activity may be carried out by those authorised to do so                          |
| <b>MEDIUM</b> | Where a risk level has been calculated to be MEDIUM, further controls should be identified where possible, in order to reduce the risk to As Low As Reasonably Practical (ALARP).                         | <b>Tolerable</b><br>Task/ Activity may only proceed with Management authorisation                            |
| <b>HIGH</b>   | A HIGH risk level is considered intolerable, and work must not commence or continue until the risk has been reduced significantly. If it is not possible to reduce the risk, work is not permitted        | <b>Unacceptable</b><br>Work must not proceed change task or further control measures required to reduce risk |

Figure 5-2 Risk Levels

| Severity Category          |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               |
|----------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>1<br/>(Negligible)</b>  | <ul style="list-style-type: none"> <li>- Minimal injury or health implications requiring no treatment; no absence from work; requires first aid treatment only (First Aid Case FAC)</li> <li>- Minimal or limited pollution effect/impact; negligible recovery work (spills of up to 1 litre)</li> <li>- Insignificant or slight property/equipment damaged (&lt;USD \$10,000)</li> <li>- Negligible damage to reputation, including some minor negative feedback</li> </ul>                                                                                  |
| <b>2<br/>(Minor)</b>       | <ul style="list-style-type: none"> <li>- Minor injury or illness requiring medical treatment (Medical Treatment Case - MTC)</li> <li>- An Environmental incident contained within the site boundary; short-term impact; recovery work by worksite personnel (spills of up to &lt;10 litres)</li> <li>- Minor repairs required for damaged property/equipment (USD \$10,000 - &lt;USD \$100,000)</li> <li>- Formal complaint by a Client or 3rd party (reputation damage)</li> </ul>                                                                           |
| <b>3<br/>(Significant)</b> | <ul style="list-style-type: none"> <li>- Restricted Work Case (RWC) injury; without long term disablement</li> <li>- An Environmental incident went beyond the site boundary, moderate short-term impact, recovery may requires external assistance (Up to &lt;100 litres)</li> <li>- Damage to property/equipment requiring significant repair with costs up to USD \$500,000</li> <li>- Local media coverage, and local community complaint</li> </ul>                                                                                                      |
| <b>4<br/>(Serious)</b>     | <ul style="list-style-type: none"> <li>- Serious injury/illness leading to days away from work or involving a single lost work day case (LWDC)</li> <li>- Serious medium-term environmental effects; recovery requires external assistance; pollution incurring significant restitution costs (spills between 100 litres to &lt;100 m3)</li> <li>- Damage to property/equipment resulting in major loss of operational capability; costs up to USD \$1,000,000</li> <li>- Regional-level negative publicity/ media coverage</li> </ul>                        |
| <b>5<br/>(Critical)</b>    | <ul style="list-style-type: none"> <li>- A fatality(s) or multiple serious injuries leading to permanent disability or terminal disease</li> <li>- Extensive pollution with long-term implications or massive site impact and recovery work; very high restitution costs resulting in serious economic liability on the business; spill in excess of 100m3</li> <li>- Damage with major long-term implications on operational capability; extensive costs in excess of USD \$1,000,000</li> <li>- International negative publicity/ media coverage</li> </ul> |

Figure 5-3 Definitions of severity categories

|                                    | Probability Rating                                                                                                                                                                                                                  |
|------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>A</b><br><b>(Very Unlikely)</b> | <ul style="list-style-type: none"> <li>- Never happened at GM or known to GM to have happened within the industry</li> <li>- A freak combination of factors would be required for an incident to occur</li> </ul>                   |
| <b>B</b><br><b>(Unlikely)</b>      | <ul style="list-style-type: none"> <li>- Unlikely to occur</li> <li>- May have happened once at GM, or in the industry</li> <li>- A rare combination of factors would be required for an incident to occur</li> </ul>               |
| <b>C</b><br><b>(Possible)</b>      | <ul style="list-style-type: none"> <li>- Could possibly occur</li> <li>- Additional factors to be combined/ present for an incident to occur</li> </ul>                                                                             |
| <b>D</b><br><b>(Likely)</b>        | <ul style="list-style-type: none"> <li>- Has happened more often than once, at GM, or known to have happened multiple times within the industry</li> <li>- An additional factor may be required to result in an incident</li> </ul> |
| <b>E</b><br><b>(Very Likely)</b>   | <ul style="list-style-type: none"> <li>- A regular occurrence in the industry</li> <li>- Almost inevitable that an incident may happen</li> </ul>                                                                                   |

Figure 5-4 Definition of Probability ratings

## 5.6 Hazard Assessment

5.6.1 The attendees were given a presentation on the Scheme and the proposed construction methodology. The HAZID methodology was also explained to all

participants with particular reference to the requirement for an objective approach to be taken during the workshop.

- 5.6.2 The International Maritime Organisation (IMO) define a hazard as 'something with the potential to cause harm, loss or injury'. It therefore follows that a risk is the measure of the frequency and consequence of a potential hazard.
- 5.6.3 Risks for the Usk, Ebbw and Newport Docks were all assessed separately. The assessment was further separated in order to capture the risk during both the construction and operational phases of the Scheme.
- 5.6.4 Each hazard and the identified potential impact was assessed against the following criteria: Injury to personnel (life), Damage to bridge and/or port infrastructure, Damage to a vessel and an Environmental impact.
- 5.6.5 Existing measures and standard marine practice which would mitigate the probability of the event were identified. Project specific mitigation measures were also identified by parties present at the workshop.
- 5.6.6 Finally, the residual risk identified for each risk category providing the project specific mitigation measures are adopted have been estimated. Where identified, actions have been recorded and are reported in this document.

## **5.7 GM's Risk Management Tool**

- 5.7.1 Global Maritime Consultancy Ltd are external marine consultants who have been engaged by the Welsh Government in order to facilitate the navigational risk assessment.
- 5.7.2 Global Maritime Proprietary tool GM Risk Management Tool (as detailed in Appendix B), is specifically developed for facilitating risk assessment workshops and was employed for this assessment.
- 5.7.3 The tool has been built to focus all prepared information into one application and displayed on one screen. It is possible to upload videos, drawings and documents to a specific chapter under discussion. By using this approach it is easy to keep control, stay on track and for all participants to follow the discussion.
- 5.7.4 The GM risk management tool (RMT) has been developed in order to facilitate risk assessment workshops including HAZOP, HAZID, ALARP, SWIFT, feasibility analysis, concept selection, layout analysis and design reviews.

## **5.8 Results**

- 5.8.1 The results of the Navigation Risk HAZID are contained in the risk registers in Appendix C.

## 5.9 Events

- 5.9.1 The number of credible hazards were identified by the participants of the NRA workshop and are tabulated in Table 5-2.

| Location     | Phase               | No of identified Hazards |
|--------------|---------------------|--------------------------|
| River Usk    | Scheme construction | 11                       |
| River Usk    | Scheme in operation | 6                        |
| River Ebbw   | Scheme construction | 5                        |
| River Ebbw   | Scheme in operation | 3                        |
| Newport Dock | Scheme construction | 10                       |
| Newport Dock | Scheme in operation | 6                        |

Table 5-2 Table of Hazards

- 5.9.2 During construction of the river and dock crossings, the main risks to navigation were identified as follows:

- 1) Collision with the rivers and dock bridges.
- 2) Collapse of bridge deck/dropped deck section.
- 3) Dropped objects (for example, tools).
- 4) Construction Pollution/floating debris.
- 5) Congested navigation/increased traffic density.
- 6) Conflict with radio communications.
- 7) Presence of background light.
- 8) Congested Newport South dock during restricted access to the North dock.

- 5.9.3 During operation of the scheme, the navigation risks can be summarised as follows:

- 1) Vessel collision with the rivers and dock bridges.
- 2) Dropped objects, such as tools, during maintenance.
- 3) Maintenance pollution/ floating debris.
- 4) Falling objects from bridge.
- 5) Congested Newport South dock during restricted access to the North dock.

## **5.10 Consequence**

5.10.1 The consequences of interaction between the Scheme and navigation can be summarised as follows:

- 1) Death/Injury to personnel.
- 2) Damage to bridge and/or infrastructure.
- 3) Damage to vessel.
- 4) Environmental impact.

## 6. MEETINGS WITH OTHER STAKEHOLDERS

### 6.1 The Corporation of Trinity House

6.1.1 A representative from Trinity House was unable to attend the NRA workshop, therefore a meeting was held with Trinity House on the 9<sup>th</sup> December 2016 at Trinity House in London. The meeting attendees are provided in Table 6-1 below, a signed attendance sheet is attached in Appendix D.

| Name                | Position                   | Company         |
|---------------------|----------------------------|-----------------|
| Nick Dodson         | Navigation Manager         | Trinity House   |
| Martin Thomas       | Navigation Support Officer | Trinity House   |
| Trevor Harris       | Local AtoN Manager         | Trinity House   |
| Jonathan Vine       | Principal Mariner          | Global Maritime |
| Lovinash Bonomaully | Senior Engineer            | Global Maritime |
| Peter Allott        | Civil Engineer             | Arup            |

Table 6-1 List of attendees

6.1.2 The meeting was conducted as below:

- 1) Introductions.
- 2) A short safety presentation was delivered by GMC.
- 3) An overview of the Scheme and the proposed construction methodology was presented.
- 4) Trinity House participants were invited to comment on the navigational risk registers.
- 5) Trinity House is of the opinion that whilst Marking and Lighting for the section over the Dock (best point of passage) is a matter Trinity House / ABP. Trinity House understand that there is an issue with air drafts within the dock which is a matter for ABP and therefore this was not discussed at this meeting.

6.1.3 The risk register (see Appendix C) was updated to include the comments from Trinity House, see below:

- Consider close vessel control utilising the marine control at Newport Docks as Cardiff LPS does not have full visual of Newport Docks and the rivers Ebbw and Usk.
- Navigation lights and signage to be installed on the river crossings, both upstream and downstream, in order to identify the best point of passage for mariners and other river users.

- Directional construction lighting to be considered in order to avoid impairment of mariners' night vision and to ensure navigation lights are readily identifiable.
- Admiralty charts to be updated to include river and dock crossings.
- With regards to Dallimore's wharf consideration must be given to the scenario where a different vessel visits the wharf.
- Following a possible dropped object, such as a bridge deck section, issues relating to the available depth of navigable water are to be addressed.

- 6.1.4 Cardiff LPS have a distribution list for promulgating navigation warnings.
- 6.1.5 Comments from Trinity House have been included in the navigation risk register.
- 6.1.6 River Ebbw crossing to indicate clearance height of bridge using signage as recommended by IALA.
- 6.1.7 River Usk and Ebbw to be lit as per IALA recommendations in order to indicate both the up and downstream best points of passage.

## 6.2 Cargo Services (UK) Ltd

- 6.2.1 Cargo Services (UK) Ltd operate Birdport, which is located on the River Usk.
- 6.2.2 A meeting was held with Cargo Services Ltd on 8<sup>th</sup> December 2016. The list of attendees are provided in Table 6-2 below and a signed attendance sheet is provided in Appendix E.

| Name                | Position          | Company            |
|---------------------|-------------------|--------------------|
| John Davey          | Managing Director | Cargo Services Ltd |
| Jonathan Vine       | Principal Mariner | Global Maritime    |
| Lovinash Bonomaully | Senior Engineer   | Global Maritime    |

Table 6-2 List of attendees

- 6.2.3 The meeting was conducted as below:
- 1) Introductions
  - 2) A short safety presentation was delivered by GMC.
  - 3) An overview of the Scheme and the proposed construction methodology was presented
  - 4) The representative from Cargo Services (UK) Ltd was invited to comment on the navigational risk registers.
- 6.2.4 It should be noted, that Birdport is situated in the River Usk, the River Ebbw and the Newport Dock crossings were not relevant to this particular stakeholder and as such were not discussed.

- 6.2.5 The CSL representative was in agreement with the hazards identified and the measures identified to be implemented.

## **7. VESSEL COLLISION WITH ROAD BRIDGE OVER DOCKS**

### **7.1 NRA Workshop – Newport Docks**

- 7.1.1 During the navigation risk assessment workshop described in the last section, the risk of a vessel colliding with the proposed bridge was identified as requiring further consideration.
- 7.1.2 The potential risk of a vessel colliding with the bridge is identified in the risk register (see Appendix C), and corresponds to Hazard ID 3.1.1 and 3.2.1.
- 7.1.3 The Welsh Government undertook further studies in order to assess the potential risk of a vessel colliding with the proposed bridge. These studies took the form of a geometric assessment (TN-16-00056-5 Draft), which identified a number of potential vessel impact scenarios with the bridge within the dock. On the basis of the scenarios identified within the geometric assessment, a ship impact assessment (M4CaN-DJV-SBR-Z3-GEN-RP-0027), was conducted, in order to determine potential ship impact loads and estimate the frequency of occurrence of any such incidents.

### **7.2 Geometric Assessment**

- 7.2.1 In order to determine whether the proposed bridge where it crossed the Newport Docks at the Junction Cut was vulnerable to a collision with a vessel using the Docks, GMC were instructed to carry out a geometric assessment in which various vessel to bridge impact scenarios were modelled. The methodology and the conclusions to the study are contained GM-TN16-00056 and should be referred to for more detailed information.
- 7.2.2 However, in brief, the study modelled a number of vessel to bridge impact scenarios, which included cruise ships, handymax bulk carriers, naval patrol vessels, cargo vessels and coasters and demonstrated how potentially these vessels may contact the bridge in the event of an uncontrolled situation such as an engine, steering, mooring line and tug failure.
- 7.2.3 It was observed that an errant cruise liner could potentially contact the bridge soffit or supports piers with either the vessel superstructure or bow the greatest impact to the bridge piers and or soffit. There also appeared to be potential for the superstructure at the after end of the cruise liner to make contact with the bridge soffit.
- 7.2.4 A number of bulk carriers, with deadweights ranging from 26,000 to 47,000 tonnes were also modelled. In these scenarios it was observed that should the any of these vessels move stern first towards the bridge then there was potential for contact between the bridge soffit and the vessels' funnels and/or main masts.
- 7.2.5 Should these vessels move uncontrollably towards the bridge bow first then it was noted that there was potential for a forward mast strike and/or ships' crane impact.

- 7.2.6 In the case of the cargo vessels within the 5,600 tonnes and 8,000 tonnes deadweight range, there was potential for contact between the vessels' main masts and funnels and the lower soffit of the bridge. Similarly, it was noted that the naval patrol radar mast could potentially contact the bridge.
- 7.2.7 The above findings clearly demonstrated that there was potential for vessel/bridge contact and the consequences of which could be catastrophic. It was therefore necessary to consider a number of mitigation measures which would be designed to prevent vessels colliding with the bridge and the bridge support piers.

### **7.3 Ship Impact Assessment**

- 7.3.1 Using the various scenarios from the geometric assessment outlined above, the AAJV carried out a probabilistic risk assessment in order to assess the level of risk of ship to bridge impacts. The methodology and conclusions of the study are contained in AAJV document M4CaN-DJV-SBR-Z3-GEN-RP-0027 and should be referred to for more detailed information.
- 7.3.2 Deterministic ship impact loads were calculated. Design bow impact forces for the design vessels range from 20 MN up to a maximum of 110 MN. The authors of the study concluded qualitatively that it would be unfeasible to design the bridge to resist the full magnitude of these impact loads.
- 7.3.3 The first stage of the probabilistic risk assessment showed that the unmitigated risk of ship impacts causing damage, failure, injury or death is at a level which is considered to be unacceptable with reference to Eurocodes and DMRB standard GD04/12.
- 7.3.4 The second stage of the above risk assessment has considered in more detail the risk to road users and other third parties such as seafarers and dock workers.

### **7.4 Bridge Protection measures**

- 7.4.1 Both studies suggest that bridge protection measures are required for the bridge in the region of the Junction Cut in order to reduce the risk of impact from vessels in both the South and the North Docks to a minimum level of 'tolerable'.
- 7.4.2 The M4CaN Project team is currently in the process of finalising the bridge protection measure in collaboration with Associated British Ports (ABP). However, it is understood that the bridge protection measures will include:
- 7.4.3 Details of the proposed bridge protection measures can be found in Appendix F.
- 7.4.4 The following quantitative risk assessments have been conducted to assess the residual risk after mitigation


## 7.5 Further risk workshop (10<sup>th</sup> August 2017)

- 7.5.1 A further formal risk assessment to finalise the bridge protection measures was held on the 10<sup>th</sup> of August 2017 at the M4 CaN Project office at Longcross Court in Cardiff.
- 7.5.2 The attendees comprised of members of the M4 CaN project team, port users and stakeholders with an interest in any potential impact the Scheme may have on navigational safety.

| Name                | Position                    | Company                        |
|---------------------|-----------------------------|--------------------------------|
| Rod Lewis           | Marine Operations Manager   | Associated British Ports       |
| Peter Baker         | MCA Surveyor                | Maritime and Coastguard Agency |
| Peter Ireland       | Environmental Coordinator   | RPS Group                      |
| Martin Bates        | Project Director            | Welsh Government               |
| Ashan Khan          | MCA Surveyor                | Maritime and Coastguard Agency |
| Gareth Escreet      | Director                    | SMS Towage                     |
| Jonathan Vine       | Manager, Ports and Shipping | Global Maritime                |
| Lovinash Bonomaully | Senior Engineer             | Global Maritime                |
| Peter Allott        | Civil Engineer              | Arup                           |

Table 7-1 List of attendees Newport Docks NRA workshop 10<sup>th</sup> August 2017

- 7.5.3 The formal safety assessment methodology adopted for the 22<sup>nd</sup> November workshop, as described above, was again used at the 10<sup>th</sup> August workshop. An updated navigation risk register for Newport Docks has been appended to this report in Appendix H.
- 7.5.4 The navigation risks were assessed on the basis of the WG's proposal for extending the quayside by 50m into the South Dock and narrowing the Junction Cut from the eastern side to 11m for both the construction and the operational phases of proposed bridge.

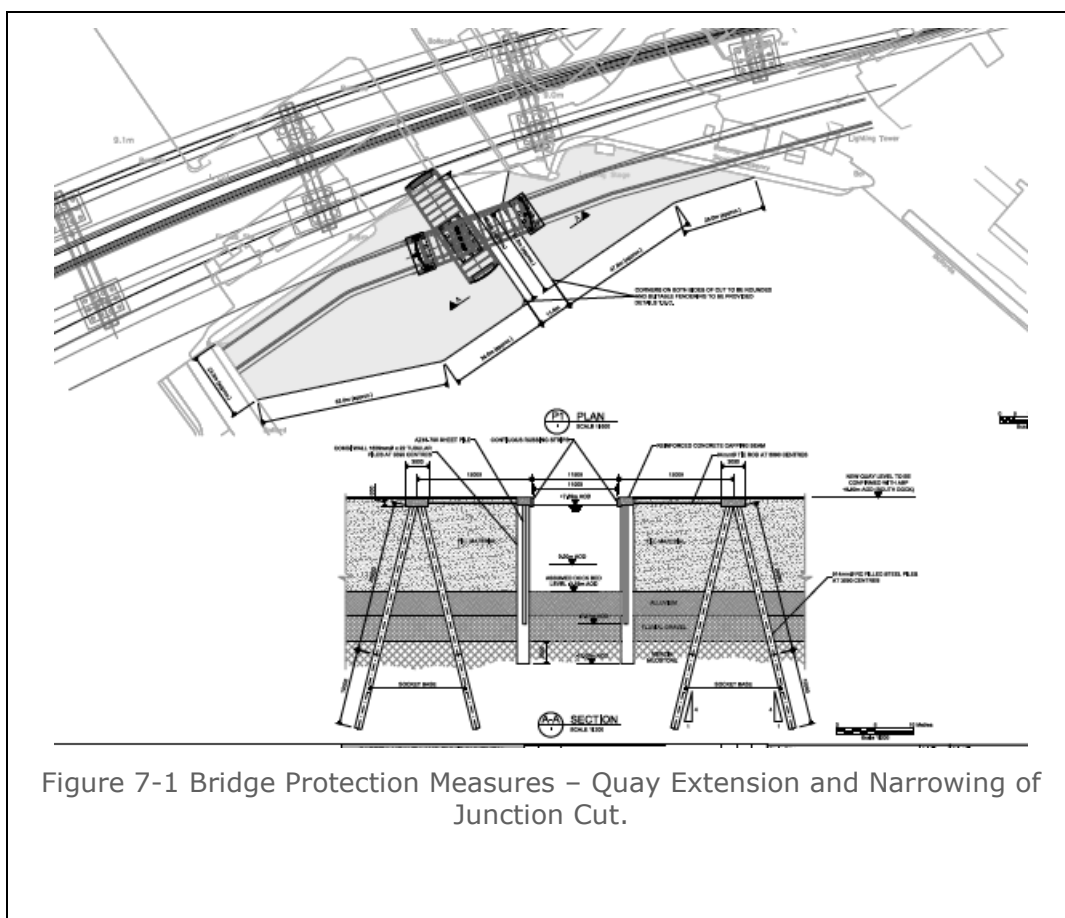

## 8. RECOMMENDATIONS

8.1.1 A number of recommendations have been made as a result of the formal risk assessment in order to mitigate the identified risks. With regard to the rivers Usk and Ebbw, the recommendations were discussed in detail with the relevant stakeholders and the recommendations from the discussions are detailed below.

8.1.2 The recommendations in terms of the navigational risk are generic for the Newport Docks and both the rivers Usk and Ebbw and are listed below:

### 1) Promulgation of Marine Safety Information

- Navigation warnings and notices to mariners (NTMs) are to be promulgated to all river users in order to inform them of any construction activities and in particular periods when navigation will be restricted.
- Engagement by the project team with stakeholders, dock and river users in order to ensure that navigational warnings have been received and understood.
- Navigation lights to be installed on the river crossings, both upstream and downstream, in order to identify the best point of passage for mariners and river users.
- Safety signage to be in place on the river banks in order to warn river users of low bridge heights, the vertical clearance and identify best point of passage during the day.
- Major bridge maintenance works are to be communicated by Notices to Mariners and navigation warnings.

### 2) Vessel Traffic Management

- River access to be actively managed during deck launching/lifting over water, when restrictions on navigation may be imposed.
- Continual monitoring of traffic, with a guard vessel available in order to assist in enforcing any restrictions.
- Vessel movements and personnel access at Dallimore's Wharf, to be managed during bridge construction and maintenance operations.
- Small vessels using the River Ebbw are to be monitored by project personnel during construction and maintenance operations.
- No vessels and/or personnel are to be beneath a suspended load during any lifting operations.
- Tugs and small vessels presently berthing in the Newport North Dock in the vicinity of the 'Junction Cut' are to be relocated.

### 3) Management of Dropped Object Risk

- Dropped object prevention measures are to be implemented at the construction site and during maintenance works.
- Bridge design to include reasonable measures to prevent falling objects.
- Unauthorised access will be prevented by appropriate security controls.
- Dropped object recovery plan to be implemented.
- Mariners and stakeholders to be advised of any dropped objects and/or floating debris which may affect navigation.

### 4) Marine Safety Management System

- SHA's Marine Safety Management System to risk assess the bridge construction and the operational phases of the proposed Scheme in order to manage navigation and marine operations.
- Develop interface document and a marine management plan to formalise interfaces, including the emergency primacy between parties.
- Clear communications plan between relevant parties during critical construction activities.

#### 5) Pollution Control

- Construction Environmental Management Plan (CEMP) to include pollution containment procedures and good housekeeping practices.
- Harbour Authority Oil Pollution Preparedness and Response Plan (OPRC).
- Bridge maintenance manual to include pollution response procedures.

#### 6) Direct Interference

- Consider interference of construction radio communications with vessel radio communications, dedicated channels to be in use.
- Construction site flood lighting equipment set-up to consider impairment of mariners' night vision (i.e. positioning/direction of lighting).

#### 8.1.3 With regards to risk of vessels colliding with the bridge within the Newport Dock,

- The geometric assessment demonstrated a number of the vessel to bridge impact scenarios which can occur. The most severe of which was a potential impact from an errant cruise liner with either the bridge superstructure or the supporting piers.
- The ship impact assessments have concluded that the risk due to vessel collision would be unacceptable based on recognised acceptability criteria (Eurocode and DMRB GD04/12), therefore bridge protection measures need to be adopted in order to mitigate the risk to an acceptable level.

#### 8.1.4 Further collaboration with ABP in the form of a further navigation risk assessment workshop was held on the 10<sup>th</sup> of August 2017 to address the risk of vessels potentially colliding with the proposed bridge over Newport Docks with the above mitigation measures in place. The workshop was attended by representatives from Associated British Ports (ABP), the Maritime and Coastguard Agency (MCA), SMS Towage, various members of the M4 CaN Project team and Global Maritime (GMC).

#### 8.1.5 The bridge protection measures currently proposed by the Welsh Government include:

- An extension of quayside on either side of the Junction Cut into the South Dock approximately 50m in order to prevent errant vessels making contact with the proposed bridge piers and/or bridge structure. The proposed build-out will have the effect of extending the Junction Cut into the South Dock and will comprise of a backfilled combi-pile walls. The run-in and sides of the newly formed Junction Cut are to be fendered to prevent damage to the quay walls and vessels transiting through.

- The Junction Cut is to be narrowed to a width of 11m, analysis of historical vessel movements within the Dock has shown that vessels with beam width of 11m or less do not have a high enough air draught to make contact with the bridge.
- The WG have also considered the installation of some form of electro-optical sensors to be located in the South Lock to act as a virtual trip wire for vessels locking into the South Lock prior to entry into the Docks. The sensors will be able to accurately measure the air draught of vessels alerting the operator of any potential issues prior to the vessel entering the Docks.


## **APPENDICES**

- APPENDIX A WORKSHOP ATTENDANCE SHEET, 22<sup>ND</sup> NOVEMBER 2016**
- APPENDIX B RISK MANAGEMENT TOOL**
- APPENDIX C NAVIGATION RISK REGISTER (22<sup>ND</sup> NOVEMBER 2016)**
- APPENDIX D MEETING WITH TRINITY HOUSE, 9<sup>TH</sup> DECEMBER 2016**
- APPENDIX E MEETING WITH CARGO SERVICES (UK) LTD, 8<sup>TH</sup> DECEMBER 2016**
- APPENDIX F BRIDGE PROTECTION MEASURES**
- APPENDIX G WORKSHOP ATTENDANCE SHEET, 10<sup>TH</sup> AUGUST 2017**
- APPENDIX H NEWPORT DOCK UPDATED RISK REGISTER (10<sup>TH</sup> AUGUST 2017)**

**APPENDIX A    WORKSHOP ATTENDANCE SHEET, 22<sup>ND</sup> NOVEMBER 2016**

# Meeting Attendance Sheet

|          |                                   |        |                 |       |                                |
|----------|-----------------------------------|--------|-----------------|-------|--------------------------------|
| Meeting: | Navigation Risk Assessment M4 Can | Venue: | Longcross Court | Date: | 22 <sup>nd</sup> November 2016 |
|----------|-----------------------------------|--------|-----------------|-------|--------------------------------|

|    | Name              | Position                  | Company          | Email Address                     | Signature                                                                             |
|----|-------------------|---------------------------|------------------|-----------------------------------|---------------------------------------------------------------------------------------|
| 1  | MARTIN BATES      | PROJECT DIRECTOR          | WELSH GOVERNMENT | Martin.bates@wales.gov.uk         |  |
| 2  | MATT JONES        | PROJECT ENGINEER          | "                | Matthew.Jones@wales.gov.uk        |  |
| 3  | Rob Lewis         | ABP                       | ABP              | rob.lewis@abp.co.uk               |  |
| 4  | MICHAEL CHADWICK  | NITC HOUSE MASTER         | NITC / ABP       | michael.chadwick@nitc.co.uk       |   |
| 5  | PETER BAKER       | M.C.A SUPERVISOR          | MCA              | peter.baker@mca.gov.uk            |    |
| 6  | Michael Bellfield | RYA Director              | RYA              | mbellfield@rya.org.uk             |    |
| 7  | PATRICK LYON      | MD                        | SHIPS TO WATCHE  | patrick.lyon@stwatch.co.uk        |    |
| 8  | SEAN HUNTER       | PROJECT MANAGER           | MANSON           | sean.hunter@manson.co.uk          |    |
| 9  | CHARLIE SMYTH     | First Mate                | MANSON           | charlie.smyth@manson.co.uk        |    |
| 10 | LORNA BONDMAULLY  | Senior Engineer           | GM               | lorna.bondmaully@gethmaritime.com |    |
| 11 | JOE VINE          | PRINCIPAL MARLIN          | "                | joe.vine@gethmaritime.com         |    |
| 12 | BARRY WOODMAN     | Project Director          | CVTV             | barry.woodman@cvtv.co.uk          |    |
| 13 | DAVE RITCHIE      | HSE                       | GM               | dave.ritchie@gethmaritime.com     |    |
| 14 | LENN KILGARD      | ENVIRONMENTAL COORDINATOR | ABP              | lenn.kilgard@abp.co.uk            |    |
| 15 | EUROPE STEPHENSON | ENVIRONMENTAL CONSULTANT  | ABP              | stephenstephenson@psgroup.co.uk   |    |

## APPENDIX B RISK MANAGEMENT TOOL

# Ports and Shipping (Eagle Lyon Pope)



## Risk Management Tool

# Risk Management Tool

Ports and Shipping (Eagle Lyon Pope) uses the GM Risk Management Tool (RMT) to ensure efficient risk workshop facilitations, reporting, communication and follow-up actions are delivered to best practice. It is based on industry standard HAZOP methodology but facilitates greater flexibility for project specific requirements.

The tool has been built to focus all prepared information into one application, displayed on one screen. It is possible to upload videos, drawings and documents to a specific chapter under discussion. By using this approach it is easy to keep control, stay on track and for all participants to follow the discussion. GM RMT has been built to handle most common risk workshops including HAZOP, HAZID, ALARP, SWIFT, feasibility analysis, concept selection, layout analysis and design reviews.

## Expertise

Our staff have extensive experience of facilitating and recording risk workshops and preparing Hazard and Effects Registers for projects that include port developments, subsea pipeline installations and vessel traffic system (VTS) studies.

GLOBAL MARITIME

Risk Management Tool

Admin mode

Matrix

Invite to collaborate

User manual

origin

On Passage Inwards 1.jpg

1. Introduction

2. On Passage Inwards

2.1 Poor Weather Conditions

2.1.1 Outer Approaches

2.1.2 Pilotage Area

2.1.3 Port Approach Channel

2.2 Ship Equipment Failure

2.3 Port Equipment Failure

2.4 High Traffic Volume

2.5 Loss of Containment

2.6 Emergency

2.7 Clip 1

3. Berthing

4. Alongside

5. Un-Berthing

6. On Passage Outwards

7. Anchoring

8. Accident at ChemaWEyatt terminal

9. Future Port Developments

2.1.1 Outer Approaches


Options

Fullscreen

| Item    | What? How? Could? Is it Possible? | Causes | Consequence                                                                            | Risk Control Measures (RCM)                                                                                                | M.. | M.. | M..  | Recommendations                                                                                                                                                          | Responsibility |
|---------|-----------------------------------|--------|----------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------|-----|-----|------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------|
| 2.1.1.1 | Poor weather conditions           | Nature | Grounding with damage to hull and contact with undersea pipeline and fibre optic cable | National wx forecast upon request<br>Wave-rider buoy<br>VTMIS management                                                   |     | 1   | 15   | National wx forecast system is being investigated.<br>VTMIS approval at national and international level being processed<br>National contingency plan to be investigated | Port           |
| 2.1.1.2 |                                   |        | Foundering                                                                             | National wx forecast upon request<br>Wave-rider buoy<br>VTMIS management                                                   | 17  | 17  | 7 12 | National wx forecast system is being investigated.<br>VTMIS approval at national and international level being processed                                                 | Port           |
| 2.1.1.3 |                                   |        | Collision with another vessel                                                          | National wx forecast upon request<br>Wave-rider buoy<br>VTMIS management<br>Relief channel available for vessels up to 11m |     |     |      | VTMIS<br>LNG rules for navigation to develop for future<br>Port to develop a navigation master plan for LNG vessels                                                      | Port           |

Please contact us for further information:

Global Maritime, Saddlers House, 44 Gutter Lane,  
London, EC2V 6BR +44 (0) 203 465 2500  
portsandshipping@globalmaritime.com  
www.globalmaritime.com



## **APPENDIX C   NAVIGATION RISK REGISTER (22<sup>ND</sup> NOVEMBER 2016)**

Session: Navigation Risk Assessment - M4 CaN 22 November 2016

1 River Usk

## 1.1 Bridge Construction

| Item  | Activity                       | Hazards                                                      | Consequences                                                                                          | Injury/Illness | Environmental Impact | Financial Loss/<br>Property damage/<br>Reputation | Existing Measures/<br>Standard Marine Practice                                                                                                                                                                                                                                                                                      | Project Specific Mitigation Measures                                                                                                                                                                                                                                                                                            | Residual Injury/<br>Illness | Residual Environmental Impact | Residual Financial Loss/<br>Property damage/<br>Reputation | Actions                        | Action Party /<br>Due Date |
|-------|--------------------------------|--------------------------------------------------------------|-------------------------------------------------------------------------------------------------------|----------------|----------------------|---------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-------------------------------|------------------------------------------------------------|--------------------------------|----------------------------|
| 1.1.1 | Navigation by merchant vessels | Collision with bridge during navigation, or by errant vessel | - Damage to bridge<br>- Damage to vessel<br>- Fatality/ Injury to personnel<br>- Environmental impact | H              | M                    | H                                                 | 1. Large passage plan vessels for the south dock to arrive just before high water, with aid of tugs/ aid of pilots.<br>2. Vessel anchors to be clear and ready for deployment.<br>3. Ship Oil Pollution Emergency Plan (SOPEP) in place onboard merchant vessels.<br>4. Natural Resources Wales (NRW) to be notified of all spills. | 1. During construction activities, navigation warnings and notices to mariners to be promulgated to all river users<br>2. Develop interface document/ marine management plan to formalise interfaces, including emergency primacy, between parties<br>3. Navigation lights on bridge.<br>4. Clearance provided in bridge design | M                           | M                             | M                                                          | Develop Marine Management Plan |                            |

| Item  | Activity                                                                         | Hazards                                                                                    | Consequences                                          | Injury/Illness | Environmental Impact | Financial Loss/ Property damage/ Reputation | Existing Measures/ Standard Marine Practice                                                                                    | Project Specific Mitigation Measures                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           | Residual Injury/ Illness | Residual Environmental Impact | Residual Financial Loss/ Property damage/ Reputation | Actions | Action Party / Due Date |
|-------|----------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------|-------------------------------------------------------|----------------|----------------------|---------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------|-------------------------------|------------------------------------------------------|---------|-------------------------|
| 1.1.2 | Navigation by all river users (merchant vessels, recreational vessels, dredgers) | Collapse/ dropped deck sections during construction/ gantry operations/ lifting operations | - Damage to vessel<br>- Fatality/ Injury to personnel | H              | L                    | H                                           | 1. Continual monitoring and control of marine traffic by Cardiff Local Port Service (LPS)/ Newport Harbour Commissioners (NHC) | 1. During construction activities, navigation warnings and notices to mariners to be promulgated to all river users<br>2. River access managed during deck launching/ lifting over water, as required<br>3. Continual monitoring of marine traffic during deck launching, and guard vessel/ craft to be available to enforce restricted access<br>4. Good communication between parties during critical construction activities<br>5. Develop interface document/ marine management plan to formalise interfaces, including emergency primacy, between parties | M                        | L                             | M                                                    |         |                         |
| 1.1.3 | Navigation by all river users (merchant vessels, recreational vessels, dredgers) | Dropped tools/ objects during construction activities                                      | - Damage to vessel<br>- Fatality/ Injury to personnel | H              | L                    | M                                           | 1. Continual monitoring and control of marine traffic by Cardiff LPS/ NHC                                                      | 1. Implementation of dropped objects prevention measures at construction site<br>2. During construction activities, navigation warnings and notices to mariners to be promulgated to all river users                                                                                                                                                                                                                                                                                                                                                           | M                        | L                             | L                                                    |         |                         |

| Item  | Activity                                                                      | Hazards                                                                                                                 | Consequences                                                                     | Injury/Illness | Environmental Impact | Financial Loss/ Property damage/ Reputation | Existing Measures/ Standard Marine Practice                                                                                                                                                                     | Project Specific Mitigation Measures                                                                                                                                                                                                                  | Residual Injury/ Illness | Residual Environmental Impact | Residual Financial Loss/ Property damage/ Reputation | Actions | Action Party / Due Date |
|-------|-------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------|----------------|----------------------|---------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------|-------------------------------|------------------------------------------------------|---------|-------------------------|
| 1.1.4 | Navigation by all river users (cargo vessels, recreational vessels, dredgers) | Construction pollution/ floating debris                                                                                 | - Damage to vessel<br>- Environmental impact/ pollution                          | L              | M                    | M                                           | 1. Pollution/ debris to be reported immediately, and recovered where possible<br>2. Cardiff LPS/ NHC notified, and navigational warning issued<br>3. Natural Resources Wales (NRW) to be notified of all spills | 1. Construction Environmental Management Plan - CEMP, in place: pollution containment equipment and procedure; storage requirements; good housekeeping<br>2. Bridge construction activities over water powered by electric supply (eg. no generators) | L                        | L                             | L                                                    |         |                         |
| 1.1.5 | Navigation by all river users (cargo vessels, recreational vessels, dredgers) | Congested navigation channel/ increased vessel to vessel encounters, during construction (causing collision/ grounding) | - Damage to vessels<br>- Fatality/ Injury to personnel<br>- Environmental impact | M              | M                    | M                                           | 1. Continual monitoring and control of marine traffic by Cardiff LPS/ NHC<br>2. Natural Resources Wales (NRW) to be notified of all spills                                                                      | 1. During construction activities, navigation warnings and notices to mariners to be promulgated to all river users                                                                                                                                   | M                        | M                             | M                                                    |         |                         |
| 1.1.6 | Navigation by all river users (cargo vessels, recreational vessels, dredgers) | Conflict with radio communications/ communication breakdown (causing collision/ grounding)                              | - Damage to vessels<br>- Fatality/ Injury to personnel<br>- Environmental impact | M              | M                    | M                                           | 1. Dedicated VHF/UHF channels used by vessels<br>2. Natural Resources Wales (NRW) to be notified of all spills                                                                                                  | 1. Construction radio communications to consider interference with vessel communications<br>2. Develop interface document/ marine management plan to formalise interfaces/ communications                                                             | M                        | M                             | M                                                    |         |                         |
| 1.1.7 | Navigation by all river users (cargo vessels, recreational vessels, dredgers) | Presence of background light from construction sites/ vehicles (causing collision/ grounding)                           | - Damage to vessels<br>- Fatality/ Injury to personnel<br>- Environmental impact | M              | M                    | M                                           |                                                                                                                                                                                                                 | 1. Construction site flood lighting equipment set-up to consider vessel navigation (ie. positioning/ direction of lighting)<br>2. Develop interface document/ marine management plan to formalise interfaces/ communications                          | M                        | M                             | M                                                    |         |                         |

| Item   | Activity                                                                      | Hazards                                                                                                     | Consequences                                                                                                     | Injury/Illness | Environmental Impact | Financial Loss/ Property damage/ Reputation | Existing Measures/ Standard Marine Practice                                                                                                                                        | Project Specific Mitigation Measures                                                                                                                                                                                                                                                         | Residual Injury/ Illness | Residual Environmental Impact | Residual Financial Loss/ Property damage/ Reputation | Actions | Action Party / Due Date |
|--------|-------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------|----------------|----------------------|---------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------|-------------------------------|------------------------------------------------------|---------|-------------------------|
| 1.1.8  | Dallimore's wharf activities, including berthing/ unberthing                  | Dropped objects during construction activities/ deck launching, in vicinity of Dallimore's wharf            | - Fatality/ injury to personnel (vessel crew and berthing personnel)<br>- Damage to vessels<br>- Damage to wharf | H              | L                    | H                                           | 1. Continual monitoring and control of marine traffic by Cardiff LPS/ NHC                                                                                                          | 1. Manage access to wharf by vessels and personnel, during deck launching/ lifting operations, as required<br>2. Develop interface document/ marine management plan to formalise interfaces/ communications                                                                                  | M                        | L                             | M                                                    |         |                         |
| 1.1.9  | Navigation by all river users (cargo vessels, recreational vessels, dredgers) | Dropped deck section into river (collision/ grounding hazard, or restricted access)                         | - Damage to vessels<br>- Commercial impact<br>- Fatality/ Injury to personnel<br>- Environmental impact          | M              | M                    | M                                           | 1. Natural Resources Wales (NRW) to be notified of any dropped objects impacting the environment                                                                                   | 1. Navigation warnings and notices to mariners to be promulgated to all river users<br>2. Dropped objects to be recovered<br>3. Guard vessel to be available if required<br>4. Hazard to be marked using 'Special Marks' following IALA Guidelines. Special Marks must be available for use. | M                        | M                             | M                                                    |         |                         |
| 1.1.10 | Birdport vessel activities                                                    | Uncontrolled vessel approach to Birdport, resulting in bridge collision or exposure to dropped objects      | - Damage to bridge<br>- Damage to vessel<br>- Fatality/ Injury to personnel<br>- Environmental impact            | M              | M                    | M                                           | 1. Vessel anchors to be clear and ready for deployment<br>2. Ship Oil Pollution Emergency Plan (SOPEP) in place onboard merchant vessels<br>3. Vessel approach close to high water | 1. River access managed during deck launching/ lifting over water, as required<br>2. During construction activities, navigation warnings and notices to mariners to be promulgated to all river users                                                                                        | M                        | M                             | M                                                    |         |                         |
| 1.1.11 | Liberty steel vessel activities                                               | Uncontrolled vessel approach to Liberty Steel, resulting in bridge collision or exposure to dropped objects | - Damage to bridge<br>- Damage to vessel<br>- Fatality/ Injury to personnel<br>- Environmental impact            | M              | M                    | M                                           | 1. Vessel anchors to be clear and ready for deployment<br>2. Ship Oil Pollution Emergency Plan (SOPEP) in place onboard merchant vessels<br>3. Vessel approach close to high water | 1. River access managed during deck launching/ lifting over water, as required<br>2. During construction activities, navigation warnings and notices to mariners to be promulgated to all river users                                                                                        | M                        | M                             | M                                                    |         |                         |

## 1 River Usk

## 1.2 Bridge Operation

| Item  | Activity                                                                         | Hazards                                                      | Consequences                                                                                | Injury/Illness | Environmental Impact | Financial Loss/ Property damage/ Reputation | Existing Measures/ Standard Marine Practice                                                                                                                                                                                                                                                    | Project Specific Mitigation Measures                                                                                                                                                                                                            | Residual Injury/ Illness | Residual Environmental Impact | Residual Financial Loss/ Property damage/ Reputation | Actions | Action Party / Due Date |
|-------|----------------------------------------------------------------------------------|--------------------------------------------------------------|---------------------------------------------------------------------------------------------|----------------|----------------------|---------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------|-------------------------------|------------------------------------------------------|---------|-------------------------|
| 1.2.1 | Navigation by merchant vessels                                                   | Collision with bridge during navigation, or by errant vessel | - Damage to bridge<br>- Damage to vessel<br>- Injury to personnel<br>- Environmental impact | M              | M                    | M                                           | 1. Large passage plan vessels for the south dock to arrive just before high water, with aid of tugs/ pilots<br>2. Vessel anchors to be clear and ready for deployment<br>3. Ship Oil Pollution Emergency Plan (SOPEP) in place onboard merchant vessels<br>4. NRW to be notified of all spills | 1. Navigation lights and marks on bridge to conform to IALA guidelines. Point of best passage to be indicated.<br>2. Clearance provided in bridge design                                                                                        | M                        | M                             | M                                                    |         |                         |
| 1.2.2 | Navigation by all river users (merchant vessels, recreational vessels, dredgers) | Dropped tools/ objects during maintenance activities         | - Damage to vessel<br>- Fatality/ Injury to personnel                                       | H              | L                    | M                                           |                                                                                                                                                                                                                                                                                                | 1. Implementation of dropped objects prevention measures during maintenance activities, to be addressed in bridge maintenance manual<br>2. Major bridge maintenance works to include promulgation of notice to mariners / navigational warnings | M                        | L                             | L                                                    |         |                         |
| 1.2.3 | Navigation by all river users (cargo vessels, recreational vessels, dredgers)    | Maintenance pollution/ floating debris                       | - Environmental impact/ pollution<br>- Damage to vessel                                     | L              | M                    | L                                           | 1. Pollution/ debris to be reported immediately, and recovered where possible<br>2. Cardiff LPS/ NHC notified, and navigational warning issued<br>3. Natural Resources Wales (NRW) to be notified of all spills                                                                                | 1. Pollution response procedures addressed in bridge maintenance manual                                                                                                                                                                         | L                        | L                             | L                                                    |         |                         |

| Item  | Activity                                                       | Hazards                                                                                                | Consequences                                                                                                     | Injury/Illness | Environmental Impact | Financial Loss/Property damage/Reputation | Existing Measures/Standard Marine Practice                                                                                                                                         | Project Specific Mitigation Measures                                                                                                                                                                                                            | Residual Injury/Illness | Residual Environmental Impact | Residual Financial Loss/Property damage/Reputation | Actions | Action Party / Due Date |
|-------|----------------------------------------------------------------|--------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------|----------------|----------------------|-------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|-------------------------------|----------------------------------------------------|---------|-------------------------|
| 1.2.4 | Dallimore's wharf activities, including berthing/unberthing    | Dropped objects during maintenance activities, in the vicinity of Dallimore's Wharf                    | - Fatality/ injury to personnel (vessel crew and berthing personnel)<br>- Damage to vessels<br>- Damage to wharf | H              | L                    | L                                         |                                                                                                                                                                                    | 1. Implementation of dropped objects prevention measures during maintenance activities, to be addressed in bridge maintenance manual<br>2. Major bridge maintenance works to include promulgation of notice to mariners / navigational warnings | M                       | L                             | L                                                  |         |                         |
| 1.2.5 | Birdport vessel activities                                     | Uncontrolled vessel approach to Birdport, resulting in bridge collision or exposure to dropped objects | - Damage to bridge<br>- Damage to vessel<br>- Fatality/ Injury to personnel<br>- Environmental impact            | H              | M                    | H                                         | 1. Vessel anchors to be clear and ready for deployment<br>2. Ship Oil Pollution Emergency Plan (SOPEP) in place onboard merchant vessels<br>3. Vessel approach close to high water |                                                                                                                                                                                                                                                 | M                       | M                             | M                                                  |         |                         |
| 1.2.6 | Navigation by all river users, during normal bridge operations | Falling objects from bridge during operation (vehicles; people; debris)                                | - Damage to vessel<br>- Fatality/ Injury to personnel                                                            | M              | L                    | M                                         |                                                                                                                                                                                    | 1. Bridge design includes barriers to prevent falling objects, and un-authorised personnel access                                                                                                                                               | M                       | L                             | M                                                  |         |                         |

## 2 River Ebbw

### 2.1 Bridge Construction

| Item  | Activity                                       | Hazards                                                             | Consequences                                                                                | Injury/Illness | Environmental Impact | Financial Loss/Property damage/Reputation | Existing Measures/Standard Marine Practice                     | Project Specific Mitigation Measures                                                                                                                                                                                                                                                                                                                                                                                                               | Residual Injury/Illness | Residual Environmental Impact | Residual Financial Loss/Property damage/Reputation | Actions | Action Party / Due Date |
|-------|------------------------------------------------|---------------------------------------------------------------------|---------------------------------------------------------------------------------------------|----------------|----------------------|-------------------------------------------|----------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|-------------------------------|----------------------------------------------------|---------|-------------------------|
| 2.1.1 | Navigation by small vessels/recreational craft | Collision with bridge during navigation                             | - Damage to bridge<br>- Damage to vessel<br>- Injury to personnel<br>- Environmental impact | M              | L                    | M                                         | 1. River Ebbw is used by small vessels/recreational users only | 1. During construction activities, navigation warnings and notices to mariners to be promulgated to all river users<br>2. Signage on river banks (both banks/ both directions/ both sides of bridge) to warn river users<br>3. Continual monitoring from banks, during construction activities                                                                                                                                                     | L                       | L                             | L                                                  |         |                         |
| 2.1.2 | Navigation by small vessels/recreational craft | Collapse/ dropped deck sections during construction/ deck launching | - Damage to vessel<br>- Fatality/ Injury to personnel                                       | H              | L                    | M                                         | 1. River Ebbw is used by small vessels/recreational users only | 1. During construction activities, navigation warnings and notices to mariners to be promulgated to all river users<br>2. River access managed during deck launching/ lifting over water, as required<br>3. Continual monitoring of marine traffic during deck launching, and guard vessel/ craft to be available to enforce restricted areas<br>4. Signage on river banks (both banks/ both directions/ both sides of bridge) to warn river users | M                       | L                             | L                                                  |         |                         |
| 2.1.3 | Navigation by small vessels/recreational craft | Dropped tools/ objects during construction activities               | - Damage to vessel<br>- Fatality/ Injury to personnel                                       | H              | L                    | M                                         |                                                                | 1. Implementation of dropped objects prevention measures at construction site<br>2. During construction activities, navigation warnings and notices to mariners to be promulgated to all river users<br>3. Signage on river banks (both banks/ both directions/ both sides of bridge) to warn river users                                                                                                                                          | M                       | L                             | L                                                  |         |                         |

| Item  | Activity                                       | Hazards                                                        | Consequences                                            | Injury/Illness | Environmental Impact | Financial Loss/Property damage/Reputation | Existing Measures/Standard Marine Practice                                                                                                                                                                      | Project Specific Mitigation Measures                                                                                                                                                                                                                  | Residual Injury/Illness | Residual Environmental Impact | Residual Financial Loss/Property damage/Reputation | Actions | Action Party / Due Date |
|-------|------------------------------------------------|----------------------------------------------------------------|---------------------------------------------------------|----------------|----------------------|-------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|-------------------------------|----------------------------------------------------|---------|-------------------------|
| 2.1.4 | Navigation by small vessels/recreational craft | Construction pollution/ floating debris                        | - Damage to vessel<br>- Environmental impact/ pollution | L              | M                    | L                                         | 1. Pollution/ debris to be reported immediately, and recovered where possible<br>2. Cardiff LPS/ NHC notified, and navigational warning issued<br>3. Natural Resources Wales (NRW) to be notified of all spills | 1. Construction Environmental Management Plan - CEMP, in place: pollution containment equipment and procedure; storage requirements; good housekeeping<br>2. Bridge construction activities over water powered by electric supply (eg. no generators) | L                       | L                             | L                                                  |         |                         |
| 2.1.5 | Navigation by small vessels/recreational craft | Presence of background light from construction sites/ vehicles | - Vessel collision<br>- Injury to personnel             | M              | L                    | M                                         |                                                                                                                                                                                                                 | 1. Construction site flood lighting equipment set-up to consider vessel navigation (ie. positioning/ direction of lighting)                                                                                                                           | M                       | L                             | L                                                  |         |                         |

## 2 River Ebbw

### 2.2 Bridge Operation

| Item  | Activity                                        | Hazards                                              | Consequences                                                                                | Injury/Illness | Environmental Impact | Financial Loss/Property damage/Reputation | Existing Measures/Standard Marine Practice | Project Specific Mitigation Measures                                                                                                                                                                                                            | Residual Injury/Illness | Residual Environmental Impact | Residual Financial Loss/Property damage/Reputation | Actions                           | Action Party / Due Date |
|-------|-------------------------------------------------|------------------------------------------------------|---------------------------------------------------------------------------------------------|----------------|----------------------|-------------------------------------------|--------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|-------------------------------|----------------------------------------------------|-----------------------------------|-------------------------|
| 2.2.1 | Navigation by small vessels/recreational crafts | Collision with bridge during navigation              | - Damage to bridge<br>- Damage to vessel<br>- Injury to personnel<br>- Environmental impact | M              | L                    | M                                         |                                            | 1. Navigation lights on bridge<br>2. Permanent signage on river banks (warning of low bridge and indicating headroom clearance)                                                                                                                 | L                       | L                             | L                                                  | Redundancy for lighting on bridge |                         |
| 2.2.2 | Navigation by small vessels/recreational craft  | Dropped tools/ objects during maintenance activities | - Damage to vessel<br>- Injury to personnel                                                 | L              | L                    | L                                         |                                            | 1. Implementation of dropped objects prevention measures during maintenance activities, to be addressed in bridge maintenance manual<br>2. Major bridge maintenance works to include promulgation of notice to mariners / navigational warnings | M                       | L                             | L                                                  |                                   |                         |

| Item  | Activity                                           | Hazards                                   | Consequences                                 | Injury/Illness | Environmental Impact | Financial Loss/<br>Property damage/<br>Reputation | Existing Measures/<br>Standard Marine Practice                                                                                                                                                                  | Project Specific Mitigation Measures                                    | Residual Injury/<br>Illness | Residual Environmental Impact | Residual Financial Loss/<br>Property damage/<br>Reputation | Actions | Action Party / Due Date |
|-------|----------------------------------------------------|-------------------------------------------|----------------------------------------------|----------------|----------------------|---------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------|-----------------------------|-------------------------------|------------------------------------------------------------|---------|-------------------------|
| 2.2.3 | Navigation by small vessels/<br>recreational craft | Maintenance pollution/<br>floating debris | - Damage to vessel<br>- Environmental impact | L              | M                    | M                                                 | 1. Pollution/ debris to be reported immediately, and recovered where possible<br>2. Cardiff LPS/ NHC notified, and navigational warning issued<br>3. Natural Resources Wales (NRW) to be notified of all spills | 1. Pollution response procedures addressed in bridge maintenance manual | L                           | L                             | L                                                          |         |                         |

### 3 Newport Docks

#### 3.1 Bridge Construction

| Item  | Activity                                                                 | Hazards                                                                         | Consequences | Injury/Illness | Environmental Impact | Financial Loss/<br>Property damage/<br>Reputation | Existing Measures/<br>Standard Marine Practice | Project Specific Mitigation Measures | Residual Injury/<br>Illness | Residual Environmental Impact | Residual Financial Loss/<br>Property damage/<br>Reputation | Actions                                                                                                                                                                                                                                                                                                                                        | Action Party / Due Date |
|-------|--------------------------------------------------------------------------|---------------------------------------------------------------------------------|--------------|----------------|----------------------|---------------------------------------------------|------------------------------------------------|--------------------------------------|-----------------------------|-------------------------------|------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
| 3.1.1 | Dock activities/<br>mooring operations/<br>Vessel movements within docks | Collision with bridge during vessel movements, or by errant vessel within docks |              | 0              | 0                    | 0                                                 |                                                |                                      | 0                           | 0                             | 0                                                          | ABP have declined to participate in discussions for this hazard. This is probably due to their objection to this scheme which relates to air draft and the potential impact of shipping hitting the bridge. WG is presently considering this risk further in a Quantitative Risk Assessment. Engagement with ABP in that regard will continue. |                         |

| Item  | Activity                                                           | Hazards                                                             | Consequences                                                                             | Injury/Illness | Environmental Impact | Financial Loss/Property damage/Reputation | Existing Measures/Standard Marine Practice                             | Project Specific Mitigation Measures                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          | Residual Injury/Illness | Residual Environmental Impact | Residual Financial Loss/Property damage/Reputation | Actions | Action Party / Due Date |
|-------|--------------------------------------------------------------------|---------------------------------------------------------------------|------------------------------------------------------------------------------------------|----------------|----------------------|-------------------------------------------|------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|-------------------------------|----------------------------------------------------|---------|-------------------------|
| 3.1.2 | Dock activities/ mooring operations/ Vessel movements within docks | Collapse/ dropped deck sections during construction/ deck launching | - Damage to vessel<br>- Fatality/ Injury to personnel<br>- Damage to dock infrastructure | H              | L                    | H                                         | 1. Newport Dock marine control to monitor vessel movements within dock | 1. During construction activities, navigation warnings and notices to mariners to be promulgated to all dock users<br>2. Continual monitoring of marine traffic during deck launching, and guard vessel/ craft to be available to enforce restricted access<br>3. Good communication between parties during critical construction activities<br>4. Develop interface document/ marine management plan to formalise interfaces, including emergency primacy, between parties<br>5. Manage vessel access between docks during critical construction activities<br>6. Manning of marine control centre at Newport, during construction activities over junction cut<br>7. Vessels to be berthed at safe location | M                       | L                             | M                                                  |         |                         |

| Item  | Activity                                                           | Hazards                                                                                       | Consequences                                                                                                    | Injury/Illness | Environmental Impact | Financial Loss/Property damage/Reputation | Existing Measures/Standard Marine Practice                             | Project Specific Mitigation Measures                                                                                                                                                                                                                                                                                               | Residual Injury/Illness | Residual Environmental Impact | Residual Financial Loss/Property damage/Reputation | Actions | Action Party / Due Date |
|-------|--------------------------------------------------------------------|-----------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------|----------------|----------------------|-------------------------------------------|------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|-------------------------------|----------------------------------------------------|---------|-------------------------|
| 3.1.3 | Dock activities/ mooring operations/ Vessel movements within docks | Dropped tools/ objects during construction activities                                         | - Damage to vessel<br>- Fatality/ Injury to personnel                                                           | H              | L                    | M                                         | 1. Newport Dock marine control to monitor vessel movements within dock | 1. Implementation of dropped objects prevention measures at construction site<br>2. During construction activities, navigation warnings and notices to mariners to be promulgated to all dock users<br>3. Develop interface document/ marine management plan to formalise interfaces, including emergency primacy, between parties | M                       | L                             | L                                                  |         |                         |
| 3.1.4 | Dock activities/ mooring operations/ Vessel movements within docks | Presence of background light from construction sites/ vehicles (causing collision/ grounding) | - Damage to vessels<br>- Fatality/ Injury to personnel<br>- Environmental impact                                | M              | M                    | M                                         |                                                                        | 1. Construction site flood lighting equipment set-up to consider vessel navigation (ie. positioning/ direction of lighting)<br>2. Develop interface document/ marine management plan to formalise interfaces/ communications                                                                                                       | M                       | M                             | M                                                  |         |                         |
| 3.1.5 | Tug berthing and bunkering at Junction Cut                         | Dropped objects whilst tugs are berthed/ bunkering                                            | - Damage to vessel<br>- Fatality/ Injury to personnel<br>- Environmental Impact/ pollution<br>- Fire/ Explosion | H              | M                    | M                                         |                                                                        | 1. Prevent access to tug berth during construction activities at Junction Cut, and identify suitable alternative location<br>2. Remove any bunkering related materials/ equipment                                                                                                                                                  | L                       | L                             | L                                                  |         |                         |

| Item  | Activity                                                                 | Hazards                                                                                             | Consequences                                                                        | Injury/Illness | Environmental Impact | Financial Loss/<br>Property damage/<br>Reputation | Existing Measures/<br>Standard Marine Practice                                                                                                                                                                            | Project Specific Mitigation Measures                                                                                                                                                                                                                                                                                        | Residual Injury/<br>Illness | Residual Environmental Impact | Residual Financial Loss/<br>Property damage/<br>Reputation | Actions | Action Party / Due Date |
|-------|--------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|----------------|----------------------|---------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-------------------------------|------------------------------------------------------------|---------|-------------------------|
| 3.1.6 | Dock activities/<br>mooring operations/<br>Vessel movements within docks | Congested docks during restricted access/ increased vessel to vessel encounters (causing collision) | - Damage to vessels<br>- Fatality/<br>Injury to personnel<br>- Environmental impact | M              | M                    | M                                                 | 1. Newport Dock marine control to monitor vessel movements within dock<br>2. Natural Resources Wales (NRW) to be notified of all spills<br>3. Ship Oil Pollution Emergency Plan (SOPEP) in place onboard merchant vessels | 1. During construction activities, navigation warnings and notices to mariners to be promulgated to all river users<br>2. Construction activities to be planned in consideration of vessel arrival/ departure times<br>3. Manning of marine control centre at Newport, during critical construction activities, as required | M                           | M                             | M                                                          |         |                         |
| 3.1.7 | Dock activities/<br>mooring operations/<br>Vessel movements within docks | Construction pollution/<br>floating debris                                                          | - Damage to vessel<br>- Environmental impact/<br>pollution                          | L              | M                    | M                                                 | 1. Pollution/ debris to be reported immediately, and recovered where possible<br>2. Newport Dock marine control to be notified<br>3. Natural Resources Wales (NRW) to be notified of all spills                           | 1. Pollution containment equipment and procedure in place (as per Construction Environmental Management Plan - CEMP)<br>2. Bridge construction activities over water powered by electric supply (eg. no generators)                                                                                                         | L                           | L                             | L                                                          |         |                         |
| 3.1.8 | Dock activities/<br>mooring operations/<br>Vessel movements within docks | Destabilizing dock wall during piling activities                                                    | - Damage to dock                                                                    | L              | L                    | M                                                 |                                                                                                                                                                                                                           | 1. Risk has been mitigated during bridge design calculations<br>2. Construction methodology (bored piling)<br>2. Monitoring equipment in place during piling operations                                                                                                                                                     | L                           | L                             | M                                                          |         |                         |

| Item   | Activity                                                                     | Hazards                                                                         | Consequences                                                                     | Injury/Illness | Environmental Impact | Financial Loss/Property damage/Reputation | Existing Measures/Standard Marine Practice    | Project Specific Mitigation Measures                                                                                                                                                      | Residual Injury/Illness | Residual Environmental Impact | Residual Financial Loss/Property damage/Reputation | Actions | Action Party / Due Date |
|--------|------------------------------------------------------------------------------|---------------------------------------------------------------------------------|----------------------------------------------------------------------------------|----------------|----------------------|-------------------------------------------|-----------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|-------------------------------|----------------------------------------------------|---------|-------------------------|
| 3.1.9  | Vessel access by crews and emergency vehicles during construction activities | Obstructed access to vessels                                                    | - Schedule / commercial impact                                                   | L              | L                    | M                                         |                                               | 1. Traffic management plan in place to ensure designated/ continual access for dock users                                                                                                 | L                       | L                             | L                                                  |         |                         |
| 3.1.10 | Dock activities/ mooring operations/ Vessel movements within docks           | Conflict with radio communications/ communication breakdown (causing collision) | - Damage to vessels<br>- Fatality/ Injury to personnel<br>- Environmental impact | M              | M                    | M                                         | 1. Dedicated VHF/UHF channels used by vessels | 1. Construction radio communications to consider interference with vessel communications<br>2. Develop interface document/ marine management plan to formalise interfaces/ communications | M                       | M                             | M                                                  |         |                         |

### 3 Newport Docks

#### 3.2 Bridge Operation

| Item  | Activity                                                           | Hazards                                                                         | Consequences | Injury/Illness | Environmental Impact | Financial Loss/Property damage/Reputation | Existing Measures/Standard Marine Practice | Project Specific Mitigation Measures | Residual Injury/Illness | Residual Environmental Impact | Residual Financial Loss/Property damage/Reputation | Actions                                                                                                                                                                                                                                                                                                                                        | Action Party / Due Date |
|-------|--------------------------------------------------------------------|---------------------------------------------------------------------------------|--------------|----------------|----------------------|-------------------------------------------|--------------------------------------------|--------------------------------------|-------------------------|-------------------------------|----------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
| 3.2.1 | Dock activities/ mooring operations/ Vessel movements within docks | Collision with bridge during vessel movements, or by errant vessel within docks |              | 0              | 0                    | 0                                         |                                            |                                      | 0                       | 0                             | 0                                                  | ABP have declined to participate in discussions for this hazard. This is probably due to their objection to this scheme which relates to air draft and the potential impact of shipping hitting the bridge. WG is presently considering this risk further in a Quantitative Risk Assessment. Engagement with ABP in that regard will continue. |                         |

| Item  | Activity                                                                                 | Hazards                                                                                                      | Consequences                                             | Injury/Illness | Environmental Impact | Financial Loss/Property damage/Reputation | Existing Measures/Standard Marine Practice                                                                                                                                                                         | Project Specific Mitigation Measures                                                                                                                                                                                                            | Residual Injury/Illness | Residual Environmental Impact | Residual Financial Loss/Property damage/Reputation | Actions | Action Party / Due Date |
|-------|------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------|----------------------------------------------------------|----------------|----------------------|-------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|-------------------------------|----------------------------------------------------|---------|-------------------------|
| 3.2.2 | Dock activities/mooring operations/Vessel movements within docks                         | Dropped tools/objects during maintenance activities                                                          | - Damage to vessel<br>- Fatality/<br>Injury to personnel | H              | L                    | M                                         |                                                                                                                                                                                                                    | 1. Implementation of dropped objects prevention measures during maintenance activities, to be addressed in bridge maintenance manual<br>2. Major bridge maintenance works to include promulgation of notice to mariners / navigational warnings | M                       | L                             | L                                                  |         |                         |
| 3.2.3 | Dock activities/mooring operations/Vessel movements within docks                         | Maintenance pollution/ floating debris                                                                       | - Environmental impact/pollution<br>- Damage to vessel   | L              | M                    | L                                         | 1. Pollution/debris to be reported immediately, and recovered where possible<br>2. Newport Docks Marine notified, and navigational warning issued<br>3. Natural Resources Wales (NRW) to be notified of all spills | 1. Pollution response procedures addressed in bridge maintenance manual                                                                                                                                                                         | L                       | L                             | L                                                  |         |                         |
| 3.2.4 | Dock activities/mooring operations/Vessel movements within docks                         | Congested south dock, due to larger vessels unable to enter north dock/increased vessel to vessel encounters |                                                          | 0              | 0                    | 0                                         |                                                                                                                                                                                                                    |                                                                                                                                                                                                                                                 | 0                       | 0                             | 0                                                  |         |                         |
| 3.2.5 | Vessels berthing and bunkering at Junction Cut, during bridge maintenance and operations | Dropped objects whilst vessels are berthed/bunkering                                                         | - Damage to vessel<br>- Fatality/<br>Injury to personnel | H              | L                    | M                                         |                                                                                                                                                                                                                    | 1. Implementation of dropped objects prevention measures during maintenance activities, to be addressed in bridge maintenance manual                                                                                                            | M                       | L                             | L                                                  |         |                         |


| Item  | Activity                                                                                 | Hazards                                                                 | Consequences                                             | Injury/Illness | Environmental Impact | Financial Loss/<br>Property damage/<br>Reputation | Existing Measures/<br>Standard Marine Practice | Project Specific Mitigation Measures                                                              | Residual Injury/<br>Illness | Residual Environmental Impact | Residual Financial Loss/<br>Property damage/<br>Reputation | Actions | Action Party / Due Date |
|-------|------------------------------------------------------------------------------------------|-------------------------------------------------------------------------|----------------------------------------------------------|----------------|----------------------|---------------------------------------------------|------------------------------------------------|---------------------------------------------------------------------------------------------------|-----------------------------|-------------------------------|------------------------------------------------------------|---------|-------------------------|
| 3.2.6 | Vessels berthing and bunkering at Junction Cut, during bridge maintenance and operations | Falling objects from bridge during operation (vehicles; people; debris) | - Damage to vessel<br>- Fatality/<br>Injury to personnel | M              | L                    | M                                                 |                                                | 1. Bridge design includes barriers to prevent falling objects, and un-authorised personnel access | M                           | L                             | M                                                          |         |                         |

## **APPENDIX D MEETING WITH TRINITY HOUSE, 9<sup>TH</sup> DECEMBER 2016**



## **APPENDIX E MEETING WITH CARGO SERVICES (UK) LTD, 8<sup>TH</sup> DECEMBER 2016**


| Meeting | Navigation Risk Assessment M4 CaN | Venue | Cardiff Heliport | Date | 8 <sup>th</sup> December 2016 |
|---------|-----------------------------------|-------|------------------|------|-------------------------------|
|---------|-----------------------------------|-------|------------------|------|-------------------------------|

|    | Name               | Position          | Company         | Email Address                         | Signature                                                                         |
|----|--------------------|-------------------|-----------------|---------------------------------------|-----------------------------------------------------------------------------------|
| 1  | JOHN DAVEY         | MANAGING          | CARGO SERVICES  | john@cargo                            |  |
| 2  |                    | DIRECTOR          | (UK) LTD.       | services@uk.com                       |  |
| 3  | Lovinesh Bondmally | SENIOR ENGINEER   | Global Maritime | lovinesh.bondmally@globalmaritime.com |  |
| 4  | JONATHAN JINE      | PRINCIPAL MARINER | GLOBAL MARITIME | jonathan.jine@globalmaritime.com      |  |
| 5  |                    |                   |                 |                                       |                                                                                   |
| 6  |                    |                   |                 |                                       |                                                                                   |
| 7  |                    |                   |                 |                                       |                                                                                   |
| 8  |                    |                   |                 |                                       |                                                                                   |
| 9  |                    |                   |                 |                                       |                                                                                   |
| 10 |                    |                   |                 |                                       |                                                                                   |
| 11 |                    |                   |                 |                                       |                                                                                   |
| 12 |                    |                   |                 |                                       |                                                                                   |
| 13 |                    |                   |                 |                                       |                                                                                   |
| 14 |                    |                   |                 |                                       |                                                                                   |


## APPENDIX F BRIDGE PROTECTION MEASURES

DO NOT SCALE

100  
0 10  
Millimetres

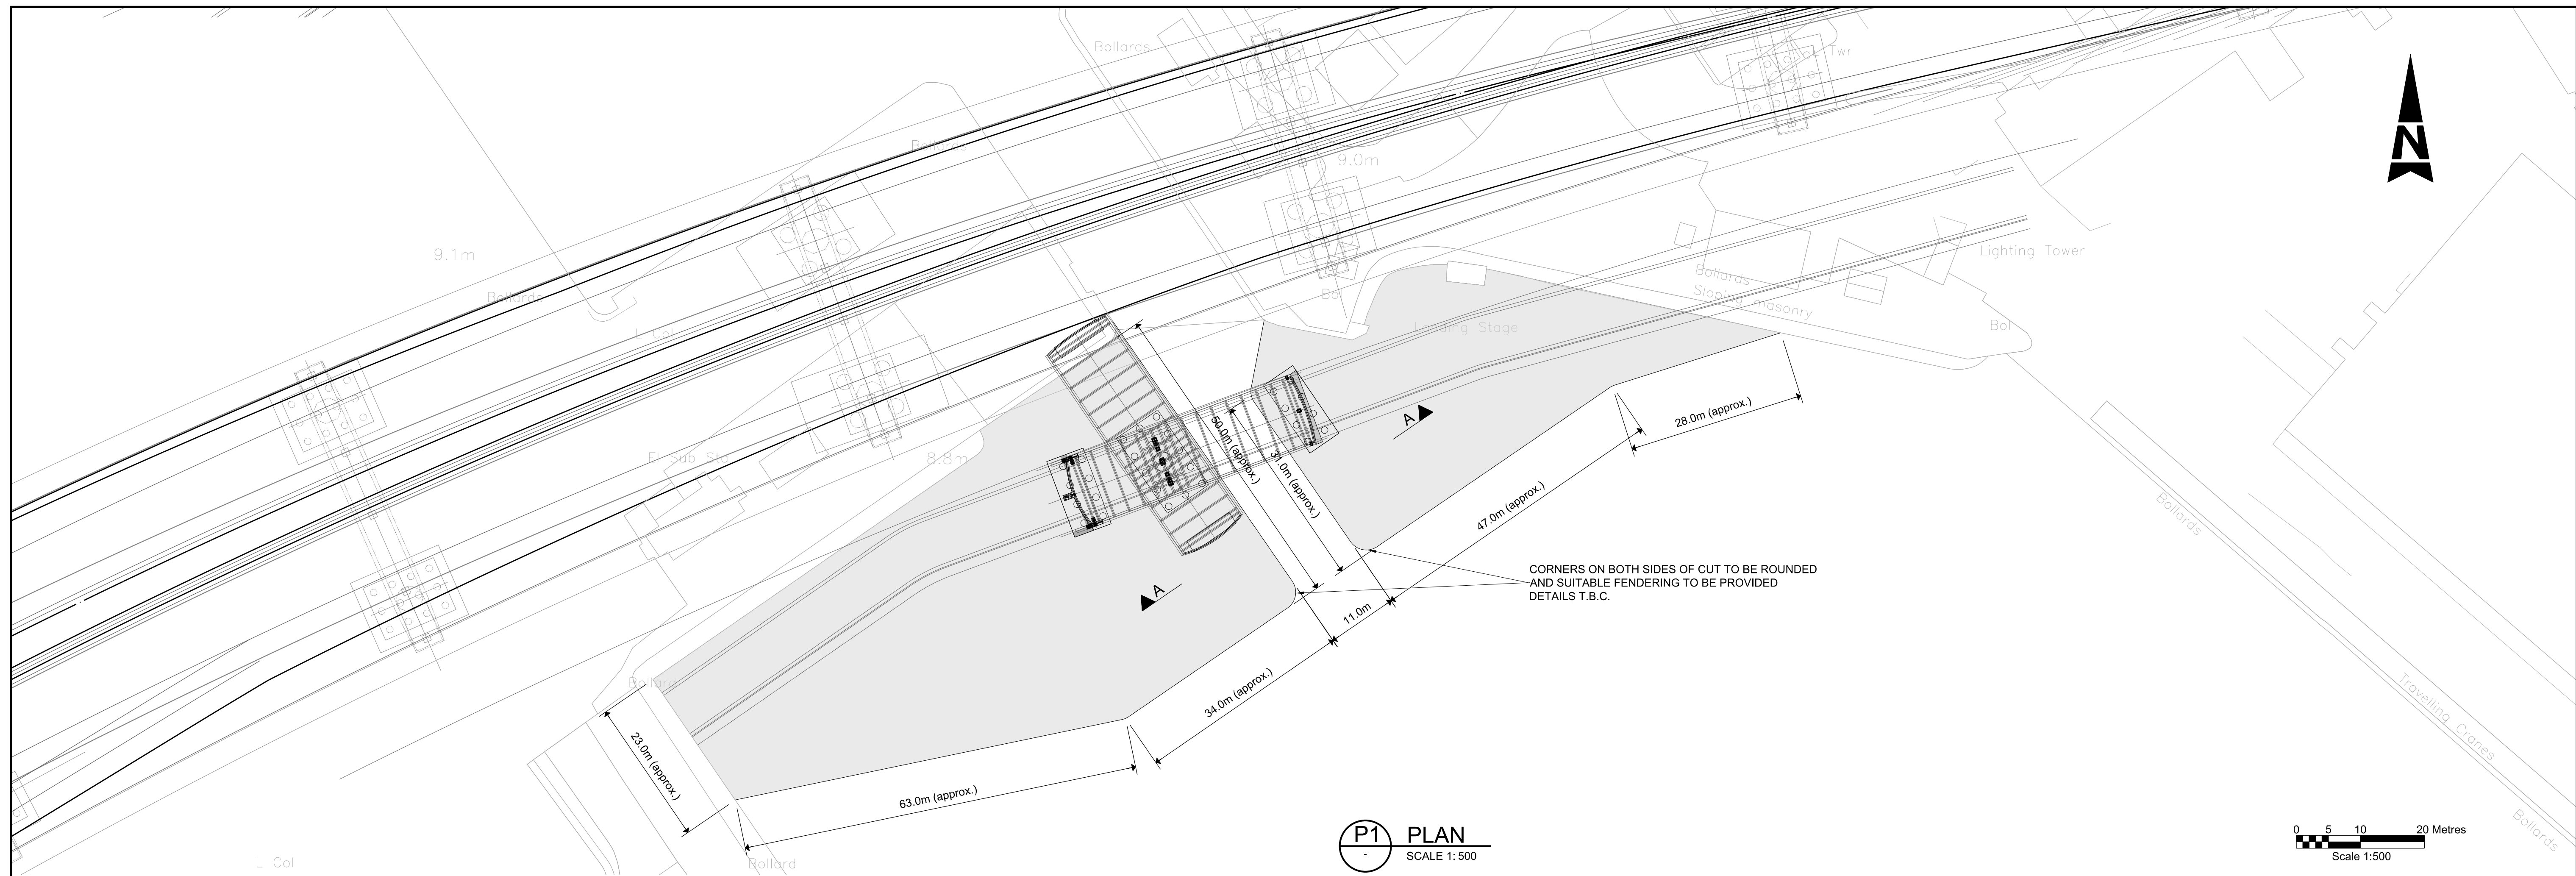

P1 PLAN  
SCALE 1:500

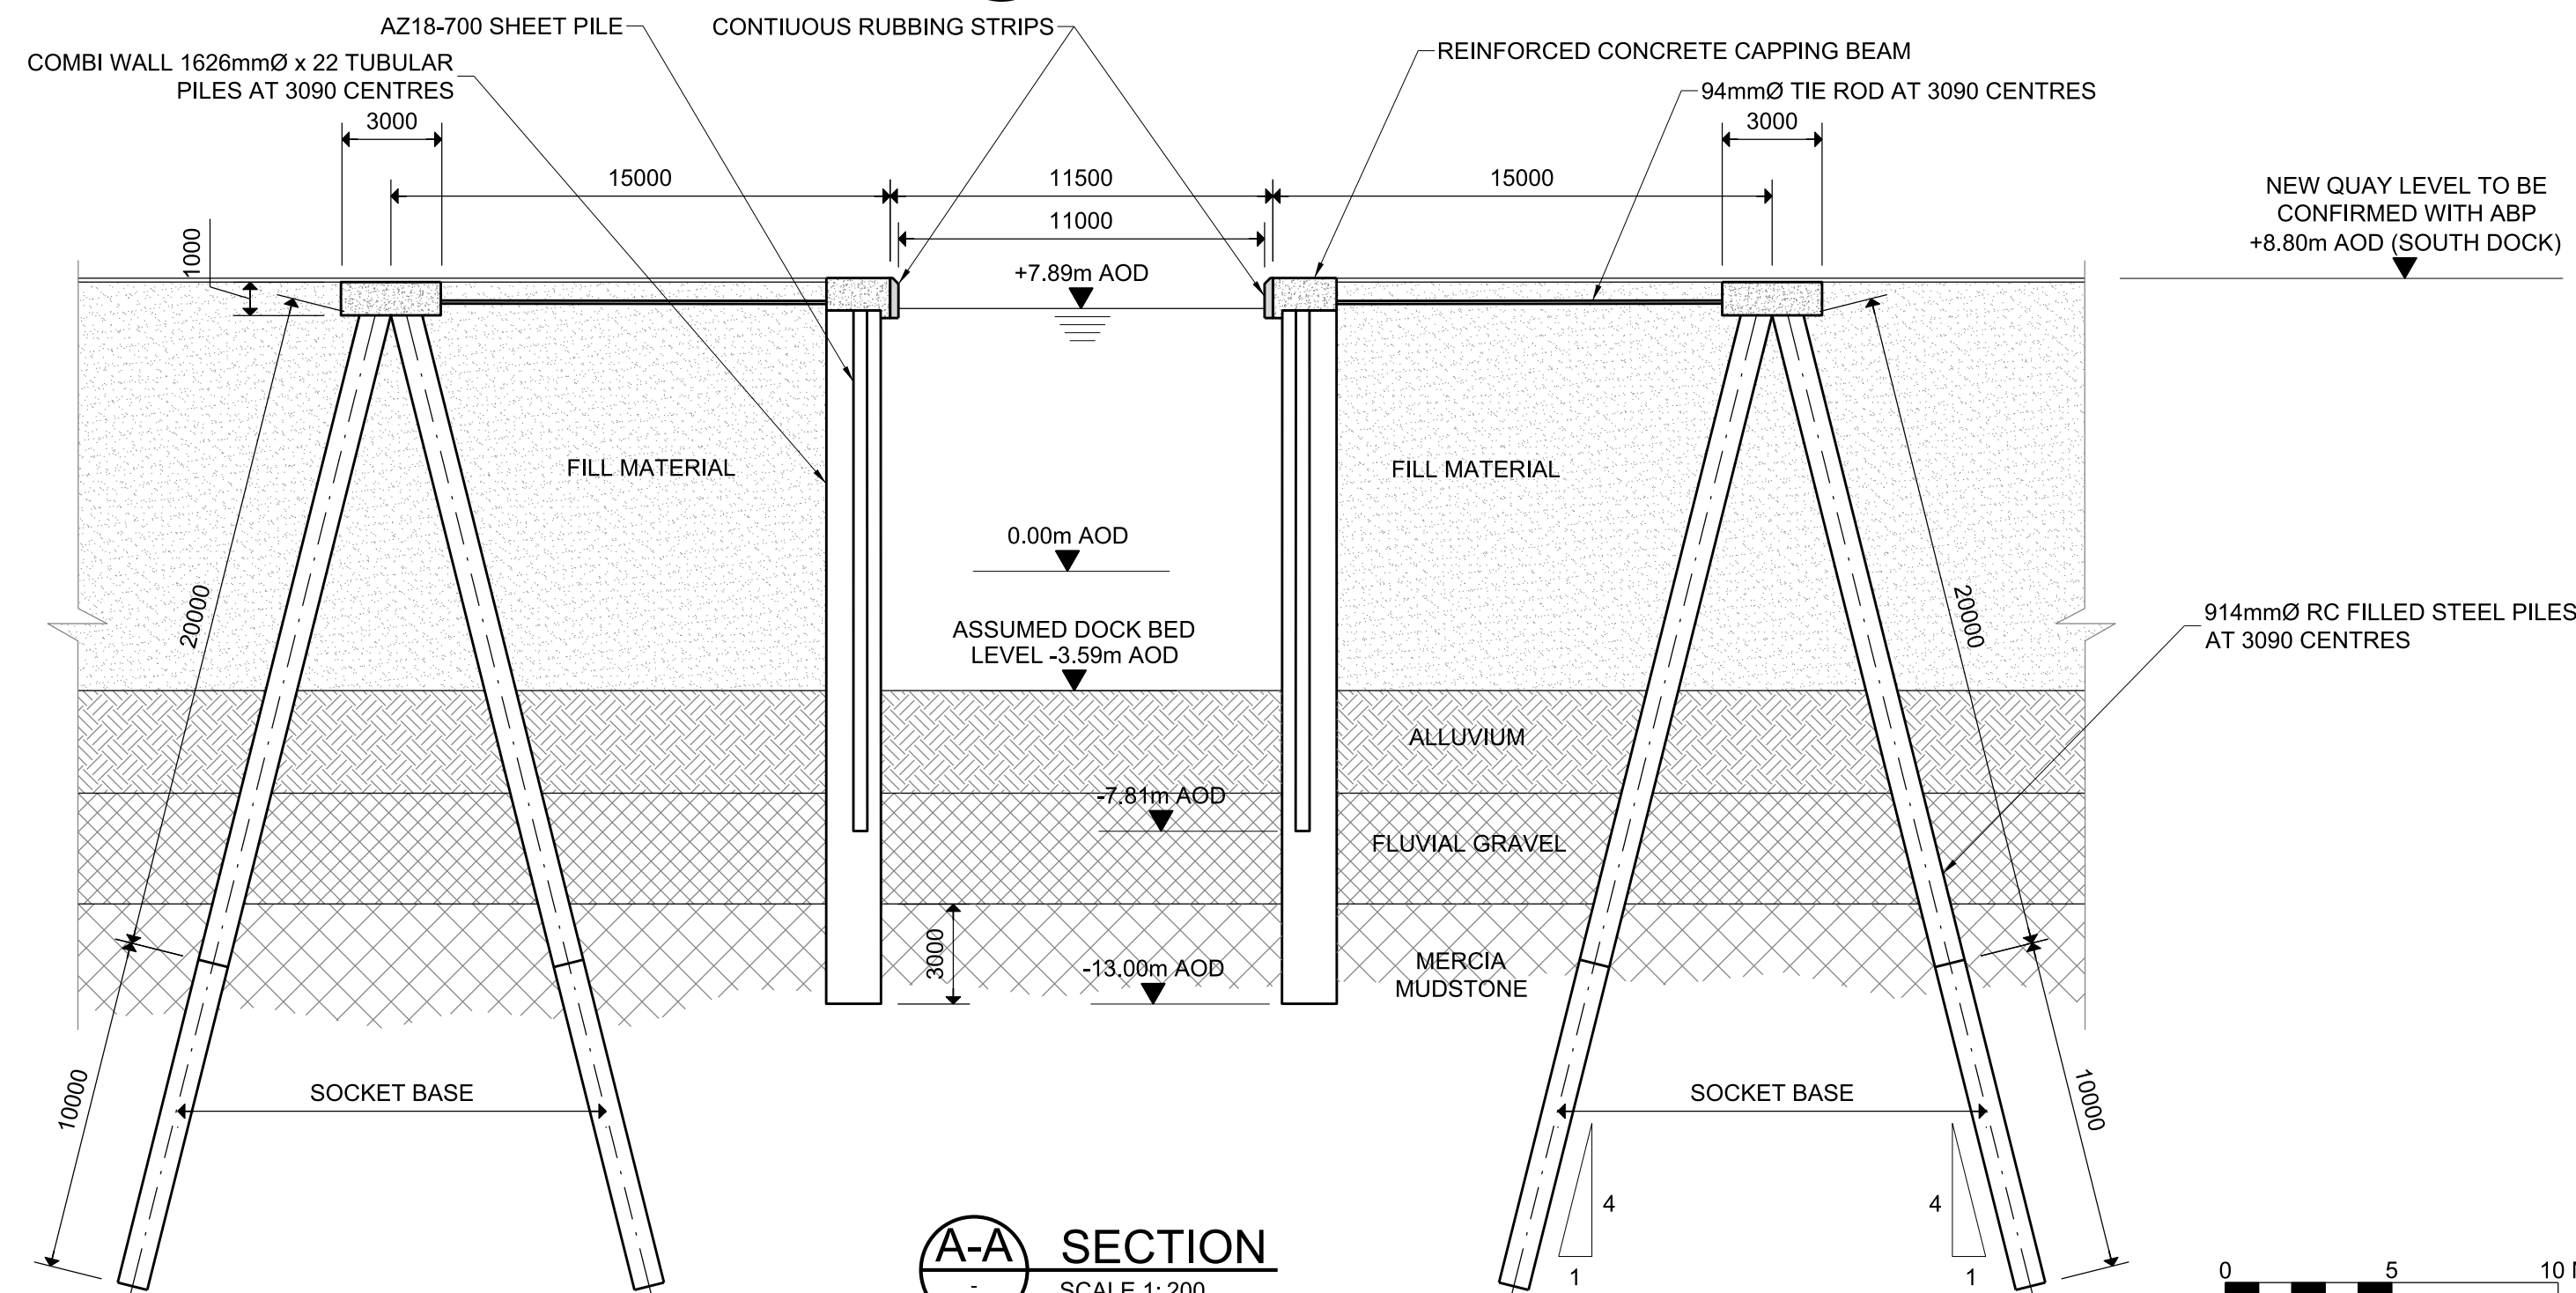

A-A SECTION  
SCALE 1:200

GENERAL NOTES:

- ALL DIMENSIONS ARE IN MILLIMETRES UNLESS NOTED OTHERWISE.
- ONLY WRITTEN DIMENSIONS SHALL BE USED, DO NOT SCALE.
- EXTENT OF NARROWING OF JUNCTION CUT IS PRELIMINARY AND IS SUBJECT TO FURTHER ASSESSMENT.
- DRAWING ISSUED FOR INFORMATION ONLY. DO NOT USE FOR CONSTRUCTION.

SAFETY, HEALTH AND ENVIRONMENTAL INFORMATION

In addition to the hazards/risks normally associated with the types of work detailed on this drawing, note the following significant residual risks (Reference shall also be made to the design hazard log).

Construction  
(Enter "None" if applicable)

Maintenance / Cleaning  
(Enter "None" if applicable)

Use  
(Enter "None" if applicable)

Decommissioning / Demolition  
(Enter "None" if applicable)

|      |          |                     |     |       |       |
|------|----------|---------------------|-----|-------|-------|
| P01  | 26/07/17 | First Issue         | BA  | PDA   | SM    |
| P02  | 07/08/17 | SUPPLEMENTARY ISSUE | GHJ | PDA   | GRD   |
| Rev. | Date     | Description         | By  | Chk'd | App'd |

|                 |                                                                                     |                            |
|-----------------|-------------------------------------------------------------------------------------|----------------------------|
| Drawing Status  | Suitability                                                                         | Project Title              |
| FOR INFORMATION | S2                                                                                  | M4 CORRIDOR AROUND NEWPORT |
| Project Team    | RIVER USK CROSSING<br>BRIDGE PROTECTION MEASURES<br>NARROWING OF JUNCTION CUT (11M) |                            |
| Client          | Llywodraeth Cymru<br>Welsh Government                                               |                            |
| Scale           | Designed / Drawn                                                                    | Checked                    |
| AS SHOWN        | GHJ                                                                                 | PDA                        |
| Original Size   | Date                                                                                | Date                       |
| A1              | 07/08/17                                                                            | 07/08/17                   |
| Drawing Number  | Project                                                                             | Originator                 |
|                 |                                                                                     |                            |
| Location        | Type                                                                                | Role                       |
|                 |                                                                                     |                            |
| Volume          | Number                                                                              | Revision                   |
|                 |                                                                                     |                            |
|                 |                                                                                     | P02                        |

**APPENDIX G    WORKSHOP ATTENDANCE SHEET, 10<sup>TH</sup> AUGUST 2017**

## Navigational Risk Assessment Attendance Sheet

[illegible]

**APPENDIX H    NEWPORT DOCK UPDATED RISK REGISTER (10<sup>TH</sup>  
AUGUST 2017)**

Session: M4CaN Navigation Risk Assessment 10/08/2017

## 1 Newport Docks

### 1.1 Bridge Construction

| Item  | Activity                                                              | Hazards                                                                         | Consequences | Injury/Illness | Environmental Impact | Financial Loss/<br>Property damage/<br>Reputation | Existing Measures/<br>Standard Marine Practice | Project Specific Mitigation Measures                                                                                                                                                                                                                  | Residual Injury/<br>Illness | Residual Environmental Impact | Residual Financial Loss/<br>Property damage/<br>Reputation | Actions                                                                                                                                                       | Action Party / Due Date |
|-------|-----------------------------------------------------------------------|---------------------------------------------------------------------------------|--------------|----------------|----------------------|---------------------------------------------------|------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-------------------------------|------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
| 1.1.1 | Dock activities/<br>mooring operations/ Vessel movements within docks | Collision with bridge during vessel movements, or by errant vessel within docks |              | H              | M                    | H                                                 | 1. SHA Marine Safety Management System.        | No bridge construction spanning the Junction Cut until bridge protection measures are in place.<br>2. Marine safety management plan specific to construction phase.<br>3. Revised vessel acceptance criteria for vessels transiting the Junction Cut. | M                           | L                             | M                                                          | 1. Project specific marine safety management system and construction interface documents to be in place prior to the commencement of construction activities. |                         |

| Item  | Activity                                                              | Hazards                                                             | Consequences                                                                                | Injury/Illness | Environmental Impact | Financial Loss/<br>Property damage/<br>Reputation | Existing Measures/<br>Standard Marine Practice | Project Specific Mitigation Measures                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              | Residual Injury/<br>Illness | Residual Environmental Impact | Residual Financial Loss/<br>Property damage/<br>Reputation | Actions                                                                                                                                                    | Action Party / Due Date |
|-------|-----------------------------------------------------------------------|---------------------------------------------------------------------|---------------------------------------------------------------------------------------------|----------------|----------------------|---------------------------------------------------|------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-------------------------------|------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
| 1.1.2 | Dock activities/<br>mooring operations/ Vessel movements within docks | Collapse/ dropped deck sections during construction/ deck launching | - Damage to vessel<br>- Fatality/<br>Injury to personnel<br>- Damage to dock infrastructure | H              | L                    | H                                                 | 1. SHA Marine Safety Management System.        | 1. During construction activities, navigation warnings and notices to mariners to be promulgated to all dock users<br>2. Restriction of marine traffic during deck launching, bridge protection measures and guard vessel/ craft to be available to enforce restricted access<br>3. Good communication between parties during critical construction activities<br>4. Develop interface document/ marine management plan to formalise interfaces, including emergency primacy, between parties<br>5. Manage vessel access between docks during critical construction activities<br>6. Manning of marine control centre at Newport, during construction activities over junction cut<br>7. Vessels to be berthed at safe location away from construction activities | L                           | L                             | L                                                          | Project specific marine safety management system and construction interface documents to be in place prior to the commencement of construction activities. |                         |

| Item  | Activity                                                                             | Hazards | Consequences                                                                             | Injury/Illness | Environmental Impact | Financial Loss/<br>Property damage/<br>Reputation | Existing Measures/<br>Standard Marine Practice | Project Specific Mitigation Measures                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | Residual Injury/<br>Illness | Residual Environmental Impact | Residual Financial Loss/<br>Property damage/<br>Reputation | Actions                                                                                                                                                    | Action Party / Due Date |
|-------|--------------------------------------------------------------------------------------|---------|------------------------------------------------------------------------------------------|----------------|----------------------|---------------------------------------------------|------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-------------------------------|------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
| 1.1.3 | Collision by vessel to combi-wall during construction of bridge protection measures. |         | -Damage to vessel<br>-Damage to bridge<br>-Injury to personnel<br>- Environmental Impact | H              | L                    | H                                                 | 1. SHA Marine Safety Management System.        | 1. During construction activities, navigation warnings and notices to mariners to be promulgated to all dock users<br>2. Restriction of marine traffic during deck launching, bridge protection measures and guard vessel/ craft to be available to enforce restricted access<br>3. Good communication between parties during critical construction activities<br>4. Develop interface document/ marine management plan to formalise interfaces, including emergency primacy, between parties<br>5. Manage vessel access between docks during critical construction activities<br>6. Manning of marine control centre at Newport, during construction activities over junction cut<br>7. Vessels to be berthed at a safe distance from construction activities.<br>8. All personnel to be wearing appropriate PPE. | L                           | L                             | L                                                          | Project specific marine safety management system and construction interface documents to be in place prior to the commencement of construction activities. |                         |

| Item  | Activity                                                           | Hazards                                                                                       | Consequences                                                                                                    | Injury/Illness | Environmental Impact | Financial Loss/ Property damage/ Reputation | Existing Measures/ Standard Marine Practice | Project Specific Mitigation Measures                                                                                                                                                                                                                                                                                               | Residual Injury/ Illness | Residual Environmental Impact | Residual Financial Loss/ Property damage/ Reputation | Actions                                                                                                                                                    | Action Party / Due Date |
|-------|--------------------------------------------------------------------|-----------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------|----------------|----------------------|---------------------------------------------|---------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------|-------------------------------|------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
| 1.1.4 | Dock activities/ mooring operations/ Vessel movements within docks | Dropped tools/ objects during construction activities                                         | - Damage to vessel<br>- Fatality/ Injury to personnel                                                           |                |                      |                                             | 1. SHA Marine Safety Management System.     | 1. Implementation of dropped objects prevention measures at construction site<br>2. During construction activities, navigation warnings and notices to mariners to be promulgated to all dock users<br>3. Develop interface document/ marine management plan to formalise interfaces, including emergency primacy, between parties |                          |                               |                                                      | Project specific marine safety management system and construction interface documents to be in place prior to the commencement of construction activities. |                         |
| 1.1.5 | Dock activities/ mooring operations/ Vessel movements within docks | Presence of background light from construction sites/ vehicles (causing collision/ grounding) | - Damage to vessels<br>- Fatality/ Injury to personnel<br>- Environmental impact                                |                |                      |                                             | 1. SHA Marine Safety Management System.     | 1. Construction site flood lighting equipment set-up to consider vessel navigation (ie. positioning/ direction of lighting)<br>2. Develop interface document/ marine management plan to formalise interfaces/ communications                                                                                                       |                          |                               |                                                      | Project specific marine safety management system and construction interface documents to be in place prior to the commencement of construction activities. |                         |
| 1.1.6 | Tug berthing and bunkering at Junction Cut                         | Dropped objects whilst tugs are berthed/ bunkering                                            | - Damage to vessel<br>- Fatality/ Injury to personnel<br>- Environmental Impact/ pollution<br>- Fire/ Explosion |                |                      |                                             | 1. SHA Marine Safety Management System.     | 1. Identify suitable alternative location and prevent access to tug berth during construction activities at Junction Cut.                                                                                                                                                                                                          |                          |                               |                                                      | Project specific marine safety management system and construction interface documents to be in place prior to the commencement of construction activities. |                         |

| Item   | Activity                                                                     | Hazards                                                                                             | Consequences                                                                     | Injury/Illness | Environmental Impact | Financial Loss/ Property damage/ Reputation | Existing Measures/ Standard Marine Practice | Project Specific Mitigation Measures                                                                                                                                                                                                                                                                                        | Residual Injury/ Illness | Residual Environmental Impact | Residual Financial Loss/ Property damage/ Reputation | Actions                                                                                                                                                    | Action Party / Due Date |
|--------|------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------|----------------|----------------------|---------------------------------------------|---------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------|-------------------------------|------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
| 1.1.7  | Dock activities/ mooring operations/ Vessel movements within docks           | Congested docks during restricted access/ increased vessel to vessel encounters (causing collision) | - Damage to vessels<br>- Fatality/ Injury to personnel<br>- Environmental impact | M              | M                    | M                                           | 1. SHA Marine Safety Management System.     | 1. During construction activities, navigation warnings and notices to mariners to be promulgated to all river users<br>2. Construction activities to be planned in consideration of vessel arrival/ departure times<br>3. Manning of marine control centre at Newport, during critical construction activities, as required | M                        | M                             | M                                                    | Project specific marine safety management system and construction interface documents to be in place prior to the commencement of construction activities. |                         |
| 1.1.8  | Dock activities/ mooring operations/ Vessel movements within docks           | Construction pollution/ floating debris                                                             | - Damage to vessel<br>- Environmental impact/ pollution                          | L              | M                    | M                                           | 1. SHA Marine Safety Management System.     | 1. Pollution containment equipment and procedure in place (as per Construction Environmental Management Plan - CEMP)<br>2. Bridge construction activities over water powered by electric.f supply (eg. no generators)                                                                                                       | L                        | L                             | L                                                    | Project specific marine safety management system and construction interface documents to be in place prior to the commencement of construction activities. |                         |
| 1.1.9  | Dock activities/ mooring operations/ Vessel movements within docks           | Destabilizing dock wall during piling activities                                                    | - Damage to dock                                                                 | L              | L                    | M                                           | 1. SHA Marine Safety Management System.     | 1. Risk has been mitigated during bridge design calculations<br>2. Construction methodology (bored piling)<br>2. Monitoring equipment in place during piling operations                                                                                                                                                     | L                        | L                             | M                                                    | Project specific marine safety management system and construction interface documents to be in place prior to the commencement of construction activities. |                         |
| 1.1.10 | Vessel access by crews and emergency vehicles during construction activities | Obstructed access to vessels                                                                        | - Schedule / commercial impact                                                   | L              | L                    | M                                           | 1. SHA Marine Safety Management System.     | 1. Traffic management plan in place to ensure designated/ continual access for dock users                                                                                                                                                                                                                                   | L                        | L                             | L                                                    | Project specific marine safety management system and construction interface documents to be in place prior to the commencement of construction activities. |                         |

| Item   | Activity                                                           | Hazards                                                                         | Consequences                                                                     | Injury/Illness | Environmental Impact | Financial Loss/ Property damage/ Reputation | Existing Measures/ Standard Marine Practice                                              | Project Specific Mitigation Measures                                                                                                                                                      | Residual Injury/ Illness | Residual Environmental Impact | Residual Financial Loss/ Property damage/ Reputation | Actions                                                                                                                                                    | Action Party / Due Date |
|--------|--------------------------------------------------------------------|---------------------------------------------------------------------------------|----------------------------------------------------------------------------------|----------------|----------------------|---------------------------------------------|------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------|-------------------------------|------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
| 1.1.11 | Dock activities/ mooring operations/ Vessel movements within docks | Conflict with radio communications/ communication breakdown (causing collision) | - Damage to vessels<br>- Fatality/ Injury to personnel<br>- Environmental impact | M              | M                    | M                                           | 1. SHA Marine Safety Management System.<br>2. Dedicated VHF/UHF channels used by vessels | 1. Construction radio communications to consider interference with vessel communications<br>2. Develop interface document/ marine management plan to formalise interfaces/ communications | M                        | M                             | M                                                    | Project specific marine safety management system and construction interface documents to be in place prior to the commencement of construction activities. |                         |

## 1 Newport Docks

### 1.2 Bridge Operation

| Item  | Activity                                                           | Hazards                                                                         | Consequences                                                                             | Injury/Illness | Environmental Impact | Financial Loss/ Property damage/ Reputation | Existing Measures/ Standard Marine Practice                                                        | Project Specific Mitigation Measures                                                                                                                                                                                                            | Residual Injury/ Illness | Residual Environmental Impact | Residual Financial Loss/ Property damage/ Reputation | Actions | Action Party / Due Date |
|-------|--------------------------------------------------------------------|---------------------------------------------------------------------------------|------------------------------------------------------------------------------------------|----------------|----------------------|---------------------------------------------|----------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------|-------------------------------|------------------------------------------------------|---------|-------------------------|
| 1.2.1 | Dock activities/ mooring operations/ Vessel movements within docks | Collision with bridge during vessel movements, or by errant vessel within docks | -Damage to vessel<br>-Damage to bridge<br>-Injury to personnel<br>- Environmental Impact | L              | L                    | L                                           | 1.Bridge design incorporates bridge protection measures.<br>2. SHA Marine Safety Management System | 1.Navigation lights show point of best passage<br>2. Headroom signage<br>3. Promulgation by SHA of acceptance criteria to the North Dock<br>4. Swing bridge operating procedures                                                                | L                        | L                             | L                                                    |         |                         |
| 1.2.2 | Dock activities/ mooring operations/ Vessel movements within docks | Dropped tools/ objects during maintenance activities                            | - Damage to vessel<br>- Fatality/ Injury to personnel                                    | H              | L                    | M                                           |                                                                                                    | 1. Implementation of dropped objects prevention measures during maintenance activities, to be addressed in bridge maintenance manual<br>2. Major bridge maintenance works to include promulgation of notice to mariners / navigational warnings | M                        | L                             | L                                                    |         |                         |

| Item  | Activity                                                                                 | Hazards                                                                                                       | Consequences                                            | Injury/Illness | Environmental Impact | Financial Loss/Property damage/Reputation | Existing Measures/Standard Marine Practice                                                                                                                                                                          | Project Specific Mitigation Measures                                                                                                 | Residual Injury/Illness | Residual Environmental Impact | Residual Financial Loss/Property damage/Reputation | Actions | Action Party / Due Date |
|-------|------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------|---------------------------------------------------------|----------------|----------------------|-------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------|-------------------------------|----------------------------------------------------|---------|-------------------------|
| 1.2.3 | Dock activities/ mooring operations/ Vessel movements within docks                       | Maintenance pollution/ floating debris                                                                        | - Environmental impact/ pollution<br>- Damage to vessel | L              | M                    | L                                         | 1. Pollution/ debris to be reported immediately, and recovered where possible<br>2. Newport Docks Marine notified, and navigational warning issued<br>3. Natural Resources Wales (NRW) to be notified of all spills | 1. Pollution response procedures addressed in bridge maintenance manual                                                              | L                       | L                             | L                                                  |         |                         |
| 1.2.4 | Dock activities/ mooring operations/ Vessel movements within docks                       | Congested south dock, due to larger vessels unable to enter north dock/ increased vessel to vessel encounters | -Injury<br>-Environment<br>-Financial                   | M              | M                    | M                                         | 1.SHA Marine Safety Management System                                                                                                                                                                               |                                                                                                                                      | M                       | M                             | M                                                  |         |                         |
| 1.2.5 | Vessels berthing and bunkering at Junction Cut, during bridge maintenance and operations | Dropped objects whilst vessels are berthed/ bunkering                                                         | - Damage to vessel<br>- Fatality/ Injury to personnel   | L              | L                    | L                                         | 1. Provision for new tug berth away from bridge                                                                                                                                                                     | 1. Implementation of dropped objects prevention measures during maintenance activities, to be addressed in bridge maintenance manual | L                       | L                             | L                                                  |         |                         |
| 1.2.6 | Vessels berthing and bunkering at Junction Cut, during bridge maintenance and operations | Falling objects from bridge during operation (vehicles; people; debris)                                       | - Damage to vessel<br>- Fatality/ Injury to personnel   | L              | L                    | L                                         | 1. Provision of tug berth away from bridge                                                                                                                                                                          | 1. Bridge design includes barriers to prevent falling objects, and un-authorised personnel access                                    | L                       | L                             | L                                                  |         |                         |



