

FF08 Structure Minor Works PPM Scoping Document

Issue Information

Job Number	1126
Date of Issue	20/06/2024
Name of Issuer	Robert Jones
Report Recipient	markshone@mphconstruction.co.uk
Contact Details of Issuer	Robjones@mphconstruction.co.uk 07496136456
Area	Dovey

Structure Information

ELR	DJP
Mileage	99.0913
Structure ID	99 41.5
Local Name/Structure Name & Location	BARMOUTH VIADUCT -913yd.No.40 - timber viaduct
Structure Type	Viaduct

Environmental & Site Specific Hazards

Sub-Form

Section 1

Ecologist site visit required?	Yes
Natural Resources Wales approvals/consents required?	Yes
Ordinary Watercourse Consent required?	Unknown
Is there any risk of flooding caused by the works?	No
Evidence of spawning aquatic life? (Fish, Reptile etc)	No
Bird Nesting Survey required?	No
Evidence of roosting bats present?	No
Are there any invasive species present? (i.e. Japanese Knotweed, Himalayan Balsam etc)	No
Evidence of door mice or other small mammals present?	No
Is the Structure Listed?	Yes
Is 3rd Party Access Required? (AMP Process)	Unknown
Is a Safe System of work required?	No

FF08 Structure Minor Works PPM Scoping Document

Are there any traffic management requirements?	No
Is rope access required to carry out the works?	No
Are there any other access requirements?	Yes
Please specify	Crown consents?
Is a buried service report required prior to work commencement?	No
Are there any unusual or specific material requirements?	No
Any other site-specific hazards?	Yes
Notes	All work will need to be done during low tide


Project Requirements

Traffic Management Required?	No
Possession(s), Line Block(s), and/or Isolation required?	No
National Resources Wales approval required?	Unknown
Is the structure listed?	Yes
Is the structure suspected or confirmed to have Asbestos Containing Materials?	No
Other third party liaison/approval required, including known land access issues?	Yes
AMP process required?	Unknown
Bridge strike or scour or public interface information plates required?	No
Total days	5
Additional Comments/Notes	Parking at Morfa mawddach station. Can also drive down the lane to viaduct. Repair damaged pile casings throughout, the spilled Casings will need to be broken out and squared off and then repaired with marine friendly concrete repair material. Approx 10 repairs in total. Power wheelbarrow will be needed to transport plant and materials to site and all works to be done on low tide. Mph team Handtools Grinder Breaker Power wheelbarrows Marine friendly concrete repair approx 10 bags



Acknowledgement

Name	Robert Jones
------	--------------

FF08 Structure Minor Works PPM Scoping Document

Job Position	Site manager
Signature	
Date/Time	20/06/2024

Photos/Additional Information

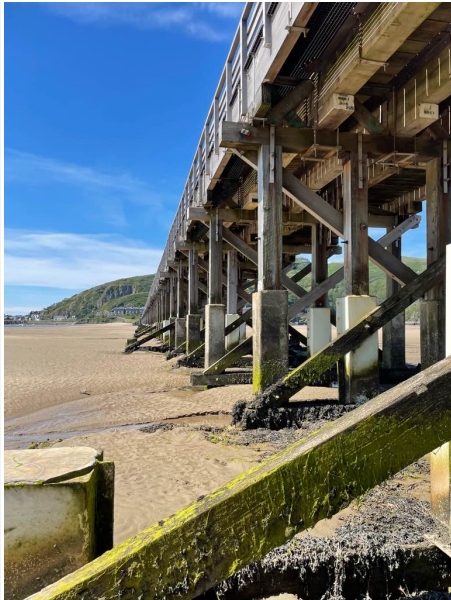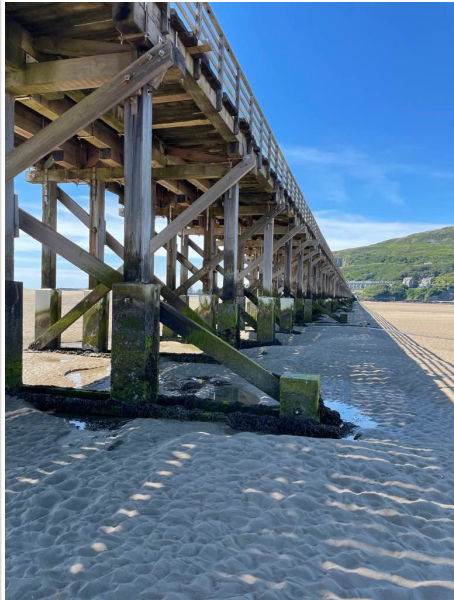What Three Words Location	Alongside.empires.latter	
Before		
	View from low milage access end	View from high milage end

FF08 Structure Minor Works PPM Scoping Document




Various spilled concrete




Repairs at span 17




FF08 Structure Minor Works PPM Scoping Document

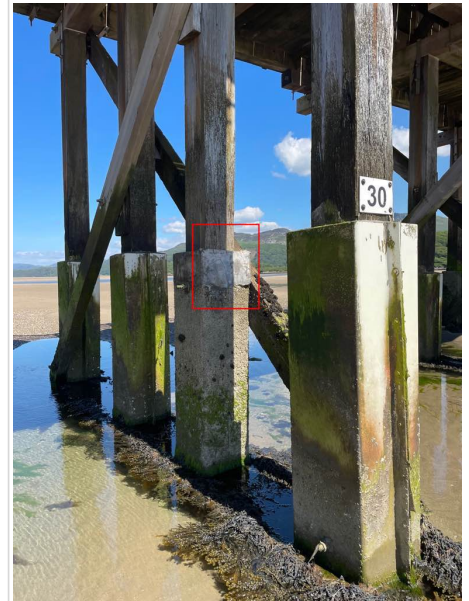


Repairs at span 30

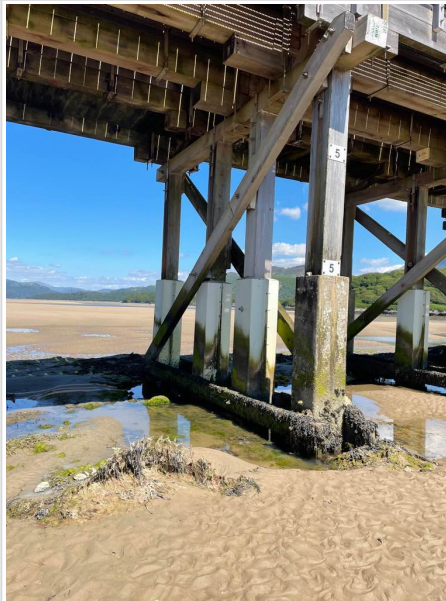

Areas of new timbers and repairs

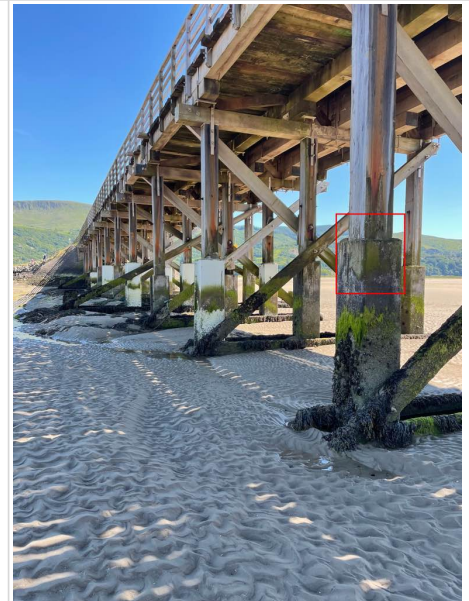

FF08 Structure Minor Works PPM Scoping Document

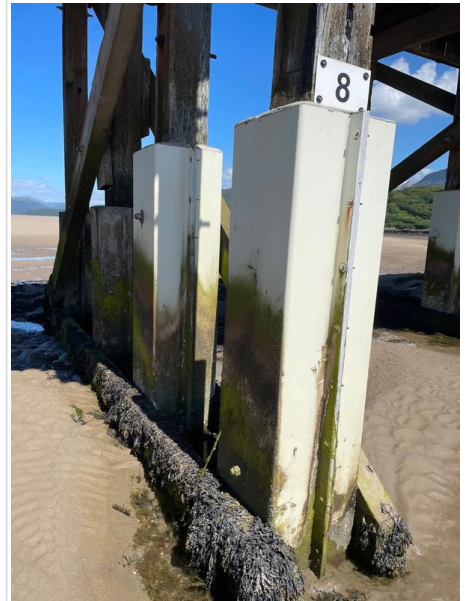

New pile casings

