
VolkerLaser

Newport Transporter Bridge - CL32 July

TASK filter: Data Date -4weeks.

#	Activity ID	Activity Name	At Completion Duration	Start	Finish	Expected Finish	BL Project Start	BL Project Finish	Variance - BL Project Finish Date	Total Float
1		**Newport Transporter Bridge - CL32 July 2026**	1208	29-Apr-22 A	12-Mar-27	15-Jan-27	29-Apr-22	09-Mar-27	-3	0
2		**MILESTONES / CONTRACT ADMIN**	439	06-Jun-25 A	12-Mar-27	15-Jan-27	06-Jun-25	09-Mar-27	-3	0
3		**Contract Data Part 1**	198	26-Aug-26 A	12-Mar-27		26-Aug-26	09-Mar-27	-3	0
4	A4680	Potential Contract Completion Date Pending Ongoing EoT Assessment	0		26-Aug-26 A			26-Aug-26	1	
5	A4730	Current Variance to Potential Contract Date (Cal Days) under Review	198	26-Aug-26 A	11-Mar-27		27-Aug-26	08-Mar-27	-3	0
6	MS0090	Planned Completion	0		11-Mar-27			08-Mar-27	-3	0
7	MS0100	Terminal Float (Working Days)	0	12-Mar-27	12-Mar-27		09-Mar-27	09-Mar-27	-3	-821
8		**PMIs**	80	16-Oct-26	19-Feb-27		02-Oct-26	05-Feb-27	-10	4
9		**PMI-147 Sidesway Buffers Design**	80	16-Oct-26	19-Feb-27		02-Oct-26	05-Feb-27	-10	4
10	A4200	Procurement and Installation of Sidesway Buffers Provisional activity - TBC Duration	80	16-Oct-26	19-Feb-27		02-Oct-26	05-Feb-27	-10	4
11		**Non-Implemented CE's**	405	06-Jun-25 A	22-Jan-27	15-Jan-27	06-Jun-25	15-Jan-27	-5	34
12		**Non-Implemented Draft CE's Pending Quote**	405	06-Jun-25 A	22-Jan-27	15-Jan-27	06-Jun-25	15-Jan-27	-5	34
13		**CEN-95 Subsidence of Combined Drainage in Site Boundary**	332	06-Jun-25 A	01-Oct-26	01-Oct-26	06-Jun-25	01-Sep-26	-22	107
14	A5470	Temp Road Plate Covers	332	06-Jun-25 A	01-Oct-26	01-Oct-26	06-Jun-25	01-Sep-26	-22	107
15		**CE-104 EAB Parapet Lattice**	50	04-Nov-26	22-Jan-27		22-Oct-26	11-Jan-27	-9	0
16	A6500	Parapet Material Procurement and Off-Site Preparations	30	04-Nov-26	15-Dec-26		22-Oct-26	02-Dec-26	-9	0
17	A6480	CE-104 - Parapet Install (North)	10	16-Dec-26	08-Jan-27		03-Dec-26	16-Dec-26	-9	0
18	A6490	CE-104 - Parapet Install (South)	10	11-Jan-27	22-Jan-27		17-Dec-26	11-Jan-27	-9	0
19		**CE-118 Additional DB Cables**	157	29-May-26 A	15-Jan-27	15-Jan-27	29-May-26	15-Jan-27	0	34
20	A6380	Radeilli lead time - underpinned by supplier latest forecast	150	29-May-26 A	15-Jan-27	15-Jan-27	29-May-26	15-Jan-27	0	34
21	A6830	Additional DB Cables Radeilli lead time - Summary	157	29-May-26 A	15-Jan-27		29-May-26	15-Jan-27	0	34
22		**CE-128 Delayed Electrical Design**	61	27-Jun-26 A	26-Aug-26 A		27-Jun-26	26-Aug-26	0	
23	A6550	CE-128 Estimated EoT - TBC with Quotation	61	27-Jun-26 A	26-Aug-26 A		27-Jun-26	26-Aug-26	0	
24		**CE-132 Re-Start Blasting**	0	06-Aug-26 A	06-Aug-26 A					
25	A6860	CE-132 - Notification - Re-Start Blasting	0		06-Aug-26 A					
26		**Implemented CE's**	28	01-Jul-26 A	07-Aug-26 A		01-Jul-26	07-Aug-26	0	
27		**CE-83 Change of Hanger Rod Replacement / Repair Method**	28	01-Jul-26 A	07-Aug-26 A		01-Jul-26	07-Aug-26	0	
28	A6810	CE-83 Hanger Rod Temporary Works Design and Approvals (Curtins)	28	01-Jul-26 A	07-Aug-26 A		01-Jul-26	07-Aug-26	0	
29		**SUMMARY BARS - LEVEL OF EFFORT**	1209	29-Apr-22 A	11-Mar-27		29-Apr-22	08-Mar-27	-3	0
30		**Management Prelims**	1209	29-Apr-22 A	11-Mar-27		29-Apr-22	08-Mar-27	-3	0
31	PW630	Overall Project duration - (WAS 97.6 Weeks)	1209	29-Apr-22 A	11-Mar-27		29-Apr-22	08-Mar-27	-3	0
32		**TEMPORARY WORKS**	16	10-Aug-26 A	01-Sep-26	01-Sep-26	10-Aug-26	21-Aug-26	-6	3
33		**N1 - Lift out Girders East Approach Bridge**	16	10-Aug-26 A	01-Sep-26	01-Sep-26	10-Aug-26	21-Aug-26	-6	3
34	TW0650	N1 Lift out Girders East Approach - Issue to Client (For Information Only)	1	10-Aug-26 A	10-Aug-26 A		10-Aug-26	10-Aug-26	0	
35	TW0740	N1 Lift out Girders East Approach - Review Lift Plan	1	01-Sep-26	01-Sep-26	01-Sep-26	10-Aug-26	21-Aug-26	-6	3
36		**PROCUREMENT**	554	22-Nov-24 A	25-Feb-27		22-Nov-24	12-Feb-27	-9	0
37	A4660	Storage of Timbers at Volker Laser Yard	552	22-Nov-24 A	25-Feb-27		22-Nov-24	12-Feb-27	-9	0
38	A5150	Procurement - BACs Anchor Bars and Clamps	81	01-May-26 A	25-Aug-26 A		01-May-26	04-Aug-26	-15	
39	PROC1120	Railings - Procure Painting	40	01-Sep-26	26-Oct-26		03-Aug-26	28-Sep-26	-20	67
40		**STAKEHOLDER MANAGEMENT**	923	30-Jan-23 A	09-Oct-26	10-Oct-26	30-Jan-23	10-Sep-26	-21	63
41	SH1010	TTRO Application (West Approach) (for West BACs)	923	30-Jan-23 A	09-Oct-26	10-Oct-26	30-Jan-23	10-Sep-26	-21	63
42		**DOCUMENTATION**	302	19-Jun-25 A	02-Sep-26	02-Sep-26	19-Jun-25	14-Aug-26	-12	79
43		**Risk Assessment & Method Statement (RAMS) & Inspection Test Plans (ITP)**	302	19-Jun-25 A	02-Sep-26	02-Sep-26	19-Jun-25	14-Aug-26	-12	79
44		**East Approach Bridge**	285	19-Jun-25 A	07-Aug-26 A		19-Jun-25	07-Aug-26	0	
45		**East Approach Bridge -Access, Removal & Installation**	285	19-Jun-25 A	07-Aug-26 A		19-Jun-25	07-Aug-26	0	
46	A5560	Crane Lift Plan Delays - see EWN-122	285	19-Jun-25 A	07-Aug-26 A		19-Jun-25	07-Aug-26	0	
47		**Main Boom Cable Replacement**	10	19-Aug-26 A	02-Sep-26	02-Sep-26	03-Aug-26	14-Aug-26	-12	79
48		**Main Boom Cable Replacement - Boom End Anchors (BACs)**	10	19-Aug-26 A	02-Sep-26	02-Sep-26	03-Aug-26	14-Aug-26	-12	79
49	DOC2000	Main Boom Cable Replacement - Boom End Anchor - Client Review & Comment	10	19-Aug-26 A	02-Sep-26	02-Sep-26	03-Aug-26	14-Aug-26	-12	79
50	DOC1990	Main Boom Cable Replacement - Boom End Anchor - Issue to Client	0		01-Sep-26			03-Aug-26	-20	-8
51	DOC2010	Main Boom Cable Replacement - Boom End Anchor - RAMS Approved	0		02-Sep-26			14-Aug-26	-12	79
52		**CONSTRUCTION**	403	21-Jul-25 A	04-Mar-27	28-Sep-26	21-Jul-25	22-Feb-27	-8	5
53		**East Boom Scaffolding, Steelwork, Blasting, Painting**	171	05-May-26 A	12-Jan-27		05-May-26	01-Dec-26	-22	32
54		**Ch14 - Ch26m Frame Scaffold and Encapsulation**	119	05-May-26 A	20-Oct-26		05-May-26	02-Oct-26	-12	79
55	A6050	Ch14-27m Scaffold Access, Blasting, Repairs, Painting	113	05-May-26 A	12-Oct-26		05-May-26	24-Sep-26	-12	0
56	C13050	Install Frame/Boom Scaffolding (inc Materials Dis)	24	07-Jul-26 A	07-Aug-26 A		07-Jul-26	07-Aug-26	0	
57	C13060	Install Encapsulation - Leaks fixing, issues sealing around traveller	20	03-Aug-26 A	28-Aug-26 A		03-Aug-26	14-Aug-26	-10	
58	C13070	Blasting	5	01-Sep-26	05-Sep-26		15-Aug-26	20-Aug-26	-13	1
59	C13080	CEN-32 Additional Blasting Quantity	5	07-Sep-26	11-Sep-26		21-Aug-26	25-Aug-26	-14	1
60	C13100	Replace/Repair Steel Members / Pin Assembly Works	9	14-Sep-26	24-Sep-26		26-Aug-26	08-Sep-26	-12	0
61	C13090	Steelwork Inspection	1	14-Sep-26	14-Sep-26		26-Aug-26	26-Aug-26	-12	0

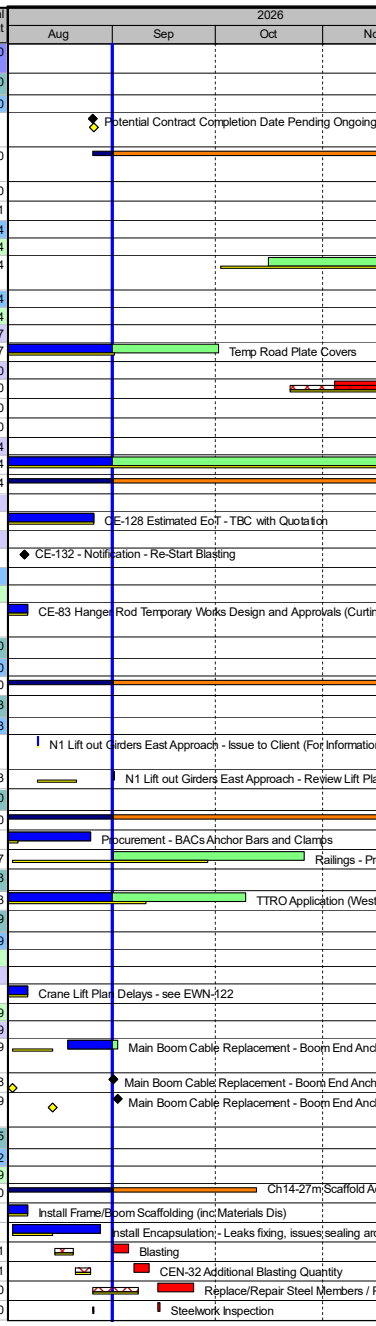

Critical Remaining Work
WBS Summary
Remaining Work
Actual Work
Remaining Level of Effort
Actual Level of Effort
Milestone
Baseline Milestone
Primary Baseline
Critical BL


PROJECT NAME: Newport Transporter Bridge - CL32 July 2026
PROJECT ID: 23826-C14990-CL32-42a
PROJECT BASELINE: Newport Transporter Bridge - CL32 July 2026

VolkerLaser

Newport Transporter Bridge - CL32 July

TASK filter: Data Date -4weeks.

#	Activity ID	Activity Name	At Completion Duration	Start	Finish	Expected Finish	BL Project Start	BL Project Finish	Variance - BL Project Finish Date	Total Float
62	C13110	Complete Weld Inspections	1	24-Sep-26	24-Sep-26		08-Sep-26	08-Sep-26	-12	0
63	C16420	Sweep Blast and Prime	2	25-Sep-26	28-Sep-26		09-Sep-26	10-Sep-26	-12	0
64	C13120	Additional Mastic Application	2	29-Sep-26	30-Sep-26		11-Sep-26	14-Sep-26	-12	0
65	C13130	Carry out Painting to Steel	5	01-Oct-26	07-Oct-26		15-Sep-26	21-Sep-26	-12	0
66	C16430	Scaffolding Contact Points - Shift	2	08-Oct-26	09-Oct-26		22-Sep-26	23-Sep-26	-12	0
67	C16440	Paint Contact Points	3	08-Oct-26	12-Oct-26		22-Sep-26	24-Sep-26	-12	0
68	C13150	Remove Frame/Boom Scaffolding	1	13-Oct-26	13-Oct-26		25-Sep-26	25-Sep-26	-12	7
69	C13160	Remove Underslung Scaffolding	5	14-Oct-26	20-Oct-26		28-Sep-26	02-Oct-26	-12	79
70	**Ch8 - Ch14m Underslung Scaffold**		8	13-Oct-26	22-Oct-26		26-Aug-26	07-Sep-26	-33	0
71	C11950	Install Underslung Scaffold	8	13-Oct-26	22-Oct-26		26-Aug-26	07-Sep-26	-33	0
72	**Ch0- Ch16m Frame Scaffold and Encapsulation**		50	23-Oct-26	12-Jan-27		28-Sep-26	01-Dec-26	-22	32
73	C13170	Install Frame/Boom Scaffolding (inc Materials Dis) (Logic Update -	8	23-Oct-26	03-Nov-26		28-Sep-26	07-Oct-26	-19	0
74	A6110	Ch0-16m Encapsulation, Blasting, Repairs, Painting	44	23-Oct-26	04-Jan-27		28-Sep-26	23-Nov-26	-22	0
75	C13180	Install Encapsulation	7	04-Nov-26	12-Nov-26		08-Oct-26	16-Oct-26	-19	0
76	C13190	Blasting	4	13-Nov-26	17-Nov-26		17-Oct-26	21-Oct-26	-23	0
77	C13200	CEN-32 Additional Blasting Quantity	4	18-Nov-26	21-Nov-26		22-Oct-26	26-Oct-26	-23	0
78	C13220	Replace/Repair Steel Members / Pin Assembly Works	9	23-Nov-26	03-Dec-26		27-Oct-26	06-Nov-26	-19	0
79	C13210	Steelwork Inspection	1	23-Nov-26	23-Nov-26		27-Oct-26	27-Oct-26	-19	0
80	C13230	Complete Weld Inspections	1	03-Dec-26	03-Dec-26		06-Nov-26	06-Nov-26	-19	0
81	C16450	Sweep Blast and Prime	2	04-Dec-26	07-Dec-26		09-Nov-26	10-Nov-26	-19	0
82	C13240	Additional Mastic Application	2	08-Dec-26	09-Dec-26		11-Nov-26	12-Nov-26	-19	0
83	C13250	Carry out Painting to Steel	5	10-Dec-26	16-Dec-26		13-Nov-26	19-Nov-26	-19	0
84	C16460	Scaffolding Contact Points - Shift	2	17-Dec-26	04-Jan-27		20-Nov-26	23-Nov-26	-19	0
85	C16470	Paint Contact Points	2	17-Dec-26	04-Jan-27		20-Nov-26	23-Nov-26	-19	0
86	A6120	Complete East Boom Steelwork Repairs and Painting	0		04-Jan-27			23-Nov-26	-22	0
87	C13270	Remove Frame/Boom Scaffolding	1	05-Jan-27	05-Jan-27		24-Nov-26	24-Nov-26	-22	32
88	C13280	Remove Underslung Scaffolding	5	06-Jan-27	12-Jan-27		25-Nov-26	01-Dec-26	-22	32
89	**West Boom Scaffolding, Steelwork, Blasting, Painting**		154	09-Jun-26 A	21-Jan-27		09-Jun-26	16-Dec-26	-18	35
90	**Ch211-Ch 223 Frame Scaffold and Encapsulation**		94	09-Jun-26 A	19-Oct-26		09-Jun-26	06-Oct-26	-9	51
91	A6080	Ch211-223 Encapsulation, Blasting, Repairs, Painting	84	09-Jun-26 A	05-Oct-26		09-Jun-26	22-Sep-26	-9	25
92	CE40-A1030	CEN-32 Additional Blasting Quantity	40	13-Jul-26 A	27-Aug-26 A		13-Jul-26	14-Aug-26	-11	
93	A6570	PMI-292 Stop Blasting - Works on Stop	12	22-Jul-26 A	06-Aug-26 A		22-Jul-26	06-Aug-26	0	
94	CE40-A1040	Steelwork Inspection	1	28-Aug-26 A	28-Aug-26 A		17-Aug-26	17-Aug-26	-9	
95	CE40-A1050	Replace/Repair Steel Members / Pin Assembly Works	10	01-Sep-26	14-Sep-26		18-Aug-26	01-Sep-26	-9	25
96	CE40-A1060	Complete Weld Inspections	1	14-Sep-26	14-Sep-26		01-Sep-26	01-Sep-26	-9	25
97	A5880	Sweep Blast and Prime	2	15-Sep-26	16-Sep-26		02-Sep-26	03-Sep-26	-9	25
98	CE40-A1070	Additional Mastic Application	3	17-Sep-26	21-Sep-26		04-Sep-26	08-Sep-26	-9	25
99	CE40-A1080	Carry out Painting to Steel	6	22-Sep-26	29-Sep-26		09-Sep-26	16-Sep-26	-9	25
100	CE40-A1090	Scaffolding Contact Points - Shift	3	30-Sep-26	02-Oct-26		17-Sep-26	21-Sep-26	-9	25
101	CE40-A1100	Paint Contact Points	4	30-Sep-26	05-Oct-26		17-Sep-26	22-Sep-26	-9	25
102	CE40-A1110	Remove Frame/Boom Scaffolding	5	06-Oct-26	12-Oct-26		23-Sep-26	29-Sep-26	-9	51
103	C15800	Remove Underslung Scaffolding	5	13-Oct-26	19-Oct-26		30-Sep-26	06-Oct-26	-9	51
104	**Ch221-Ch 236 Frame Scaffold and Encapsulation**		70	06-Oct-26	21-Jan-27		17-Aug-26	16-Dec-26	-18	35
105	B1170	Install Frame/Boom Scaffolding (inc Materials Dis)	8	06-Oct-26	15-Oct-26		17-Aug-26	26-Aug-26	-35	25
106	B1230	Install Encapsulation	8	16-Oct-26	27-Oct-26		23-Sep-26	02-Oct-26	-17	25
107	A6090	Ch221-236 Encapsulation, Blasting, Repairs, Painting	52	16-Oct-26	07-Jan-27		23-Sep-26	02-Dec-26	-18	25
108	B1220	Blasting	5	28-Oct-26	02-Nov-26		03-Oct-26	08-Oct-26	-21	30
109	B1250	CEN-32 Additional Blasting Quantity	8	03-Nov-26	11-Nov-26		09-Oct-26	17-Oct-26	-21	30
110	B1240	Steelwork Inspection	1	12-Nov-26	12-Nov-26		19-Oct-26	19-Oct-26	-18	25
111	B1210	Replace/Repair Steel Members / Pin Assembly Works	15	13-Nov-26	03-Dec-26		20-Oct-26	09-Nov-26	-18	25
112	B1200	Complete Weld Inspections	1	03-Dec-26	03-Dec-26		09-Nov-26	09-Nov-26	-18	25
113	B1300	Sweep Blast and Prime	2	04-Dec-26	07-Dec-26		10-Nov-26	11-Nov-26	-18	25
114	B1260	Additional Mastic Application	3	08-Dec-26	10-Dec-26		12-Nov-26	16-Nov-26	-18	22
115	B1190	Carry out Painting to Steel	8	11-Dec-26	22-Dec-26		17-Nov-26	26-Nov-26	-18	25
116	B1270	Scaffolding Contact Points - Shift	3	04-Jan-27	06-Jan-27		27-Nov-26	01-Dec-26	-15	25
117	B1280	Paint Contact Points	4	04-Jan-27	07-Jan-27		27-Nov-26	02-Dec-26	-15	25
118	A6100	Complete West Boom Repairs and Painting	0		07-Jan-27			02-Dec-26	-18	45
119	B1180	Remove Frame/Boom Scaffolding	5	08-Jan-27	14-Jan-27		03-Dec-26	09-Dec-26	-18	25
120	B1150	Remove Underslung Scaffolding	5	15-Jan-27	21-Jan-27		10-Dec-26	16-Dec-26	-18	25
121	**Belleville Washer Replacement - Compensation Event CE43**		212	08-Apr-26 A	12-Feb-27	28-Sep-26	08-Apr-26	22-Feb-27	6	14
122	CE43-A3690	Curtins / Norse Approval of Mitigated Temp Works Scaffold Design	86	08-Apr-26 A	07-Aug-26 A		08-Apr-26	28-Aug-26	15	
123	CE43-A3450	Completion of blast and painting incl removal of associated scaffold EXCL Ch0-20m and Ch228-236m	0		07-Aug-26 A			06-Oct-26	42	
124	CE43-A3460	Procure and Fabricate Temporary Works Struts, etc	36	07-Aug-26 A	28-Sep-26	28-Sep-26	03-Aug-26	28-Sep-26	0	9
125	A6030	Belleville Washer Replacements	127	07-Aug-26 A	12-Feb-27		07-Oct-26	22-Feb-27	6	14
126	A6850	TQ Full Close out re Expansion Joint Loads / Meeting to confirm	0		07-Aug-26 A					
127	**EXJ02 Belleville Washer Replacement (Mid Span)**		51	07-Aug-26 A	19-Oct-26		07-Oct-26	06-Nov-26	14	9

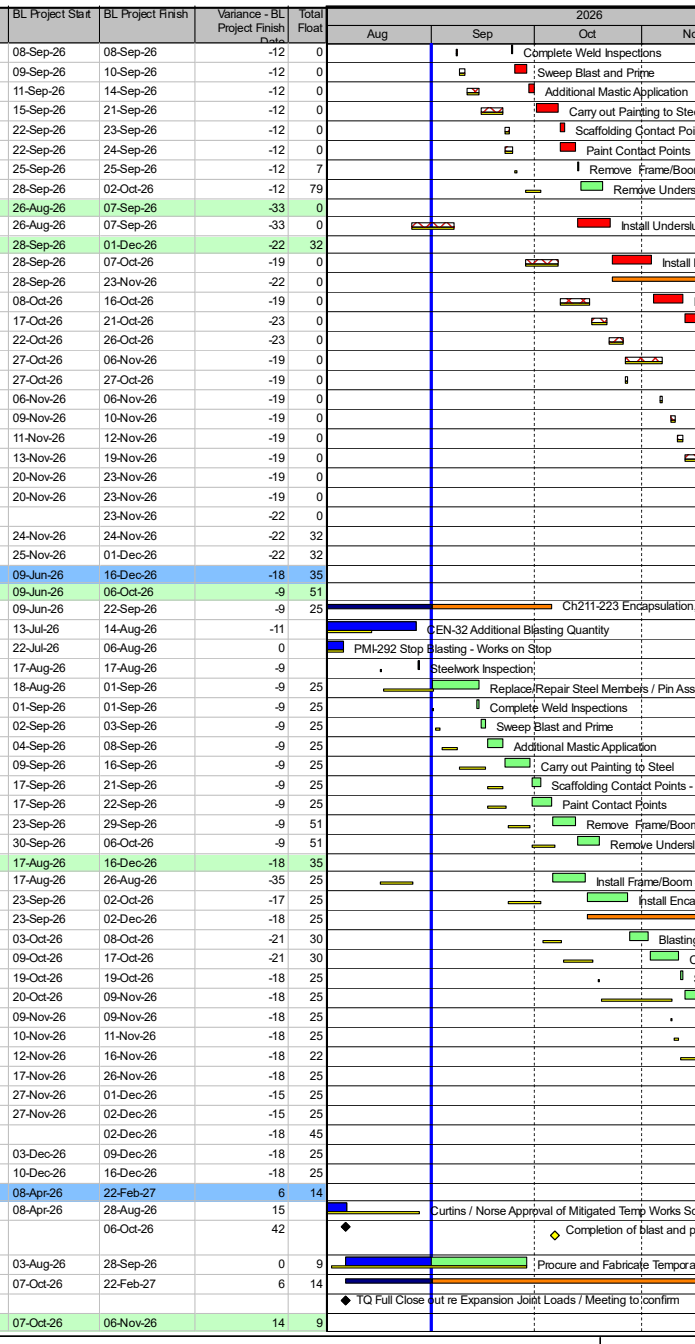

Critical Remaining Work
WBS Summary
Remaining Work
Actual Work
Remaining Level of Effort
Actual Level of Effort
Milestone
Baseline Milestone
Primary Baseline
Critical BL


PROJECT NAME: Newport Transporter Bridge - CL32 July 2026
PROJECT ID: 23826-C14990-CL32-42a
PROJECT BASELINE: Newport Transporter Bridge - CL32 July 2026

VolkerLaser

Newport Transporter Bridge - CL32 July

TASK filter: Data Date -4weeks.

#	Activity ID	Activity Name	At Completion Duration	Start	Finish	Expected Finish	BL Project Start	BL Project Finish	Variance - BL Project Finish Date	Total Float
128	CE43-B1010	Install supporting underslung ladder deck and scaffold to EXJ02 Mid Span Boom (North and South Sides)	16	07-Aug-26 A	28-Aug-26 A		07-Oct-26	16-Oct-26	34	
129	CE43-A3620	Mid Span - Replace EXJ02(North) and EXJ02 (South) Concurrently (incl Temp Works)	15	29-Sep-26	19-Oct-26		19-Oct-26	06-Nov-26	14	9
130	**EXJ01 Belleville Washer Replacement (West Boom)**		50	01-Sep-26	09-Nov-26		19-Oct-26	27-Nov-26	14	9
131	CE43-B1020	Install supporting underslung ladder deck and scaffold to EXJ01 West Boom (North and South Sides)	16	01-Sep-26	22-Sep-26		19-Oct-26	28-Oct-26	26	28
132	CE43-A3610	Western Boom - Replace EXJ01(North) and EXJ01 (South) Concurrently (incl Temp Works)	15	20-Oct-26	09-Nov-26		09-Nov-26	27-Nov-26	14	9
133	**EXJ03 Belleville Washer Replacement (East Boom)**		31	10-Nov-26	06-Jan-27		30-Nov-26	14-Jan-27	6	9
134	CE43-B1000	Install supporting underslung ladder deck and scaffold to EXJ03 East Boom (North and South Sides)	16	10-Nov-26	01-Dec-26		30-Nov-26	09-Dec-26	6	9
135	CE43-A3630	East Boom - Replace EXJ03(North) and EXJ03 (South) Concurrently (incl Temp Works)	15	02-Dec-26	06-Jan-27		10-Dec-26	14-Jan-27	6	9
136	**Final 'Snugging' of Belleville Washers - 6no. EX Joints**		3	07-Jan-27	11-Jan-27		15-Jan-27	19-Jan-27	6	9
137	CE43-A3640	Final Adjustment of Spring washer stacks to remove Slack	3	07-Jan-27	11-Jan-27		15-Jan-27	19-Jan-27	6	9
138	**Belleville Washer Scaffold Removal**		24	12-Jan-27	12-Feb-27		20-Jan-27	22-Feb-27	6	14
139	CE43-A3560	Strip Scaffold @ EXJ01 West Boom and Remove from Bridge	8	12-Jan-27	21-Jan-27		20-Jan-27	29-Jan-27	6	9
140	CE43-B1030	Painting Scaffold Contact Points - EXJ01 West Boom	6	14-Jan-27	21-Jan-27		22-Jan-27	29-Jan-27	6	18
141	CE43-A3570	Strip Scaffold @ EXJ02 Mid Span and Remove from Bridge	8	22-Jan-27	02-Feb-27		01-Feb-27	10-Feb-27	6	9
142	CE43-B1040	Painting Scaffold Contact Points - EXJ02 Mid Boom	6	26-Jan-27	02-Feb-27		03-Feb-27	10-Feb-27	6	16
143	CE43-A3580	Strip Scaffold @ EXJ03 East Boom and Remove from Bridge	8	03-Feb-27	12-Feb-27		11-Feb-27	22-Feb-27	6	9
144	CE43-B1050	Painting Scaffold Contact Points - EXJ03 East Boom	6	05-Feb-27	12-Feb-27		15-Feb-27	22-Feb-27	6	14
145	**CE-83 Hanger Rods**		121	24-Aug-26 A	19-Feb-27	07-Sep-26	10-Aug-26	05-Feb-27	-10	4
146	A6820	Hanger Rod Replacements	121	24-Aug-26 A	19-Feb-27		10-Aug-26	05-Feb-27	-10	4
147	**CE-83 Location #1 Hanger Rods**		26	24-Aug-26 A	29-Sep-26	07-Sep-26	10-Aug-26	15-Sep-26	-10	4
148	A6600	CE-83 - Location #1 Scaffold and Wrapping	10	24-Aug-26 A	07-Sep-26	07-Sep-26	10-Aug-26	21-Aug-26	-10	4
149	A6670	CE-83 - Location #1 Drop Rod Replace and Re-Paint	6	08-Sep-26	15-Sep-26		24-Aug-26	01-Sep-26	-10	4
150	A6740	CE-83 - Location #1 Scaffold Strip	10	16-Sep-26	29-Sep-26		02-Sep-26	15-Sep-26	-10	4
151	**CE-83 Location #2 Hanger Rods**		26	16-Sep-26	21-Oct-26		02-Sep-26	07-Oct-26	-10	4
152	A6610	CE-83 - Location #2 Scaffold and Wrapping	10	16-Sep-26	29-Sep-26		02-Sep-26	15-Sep-26	-10	4
153	A6680	CE-83 - Location #2 Drop Rod Replace and Re-Paint	6	30-Sep-26	07-Oct-26		16-Sep-26	23-Sep-26	-10	4
154	A6750	CE-83 - Location #2 Scaffold Strip	10	08-Oct-26	21-Oct-26		24-Sep-26	07-Oct-26	-10	4
155	**CE-83 Location #3 Hanger Rods**		26	08-Oct-26	12-Nov-26		24-Sep-26	29-Oct-26	-10	4
156	A6620	CE-83 - Location #3 Scaffold and Wrapping	10	08-Oct-26	21-Oct-26		24-Sep-26	07-Oct-26	-10	4
157	A6690	CE-83 - Location #3 Drop Rod Replace and Re-Paint	6	22-Oct-26	29-Oct-26		08-Oct-26	15-Oct-26	-10	4
158	A6760	CE-83 - Location #3 Scaffold Strip	10	30-Oct-26	12-Nov-26		16-Oct-26	29-Oct-26	-10	4
159	**CE-83 Location #4 Hanger Rods**		26	30-Oct-26	04-Dec-26		16-Oct-26	20-Nov-26	-10	4
160	A6630	CE-83 - Location #4 Scaffold and Wrapping	10	30-Oct-26	12-Nov-26		16-Oct-26	29-Oct-26	-10	4
161	A6700	CE-83 - Location #4 Drop Rod Replace and Re-Paint	6	13-Nov-26	20-Nov-26		30-Oct-26	06-Nov-26	-10	4
162	A6770	CE-83 - Location #4 Scaffold Strip	10	23-Nov-26	04-Dec-26		09-Nov-26	20-Nov-26	-10	4
163	**CE-83 Location #5 Hanger Rods**		26	23-Nov-26	07-Jan-27		09-Nov-26	14-Dec-26	-10	4
164	A6640	CE-83 - Location #5 Scaffold and Wrapping	10	23-Nov-26	04-Dec-26		09-Nov-26	20-Nov-26	-10	4
165	A6710	CE-83 - Location #5 Drop Rod Replace and Re-Paint	6	07-Dec-26	14-Dec-26		23-Nov-26	30-Nov-26	-10	4
166	A6780	CE-83 - Location #5 Scaffold Strip	10	15-Dec-26	07-Jan-27		01-Dec-26	14-Dec-26	-10	4
167	**CE-83 Location #6 Hanger Rods**		25	15-Dec-26	28-Jan-27		01-Dec-26	14-Jan-27	-10	4
168	A6650	CE-83 - Location #6 Scaffold and Wrapping	10	15-Dec-26	07-Jan-27		01-Dec-26	14-Dec-26	-10	4
169	A6720	CE-83 - Location #6 Drop Rod Replace and Re-Paint	5	08-Jan-27	14-Jan-27		15-Dec-26	21-Dec-26	-10	4
170	A6790	CE-83 - Location #6 Scaffold Strip	10	15-Jan-27	28-Jan-27		22-Dec-26	14-Jan-27	-10	4
171	**CE-83 Location #7 Hanger Rods**		26	15-Jan-27	19-Feb-27		22-Dec-26	05-Feb-27	-10	4
172	A6660	CE-83 - Location #7 Scaffold and Wrapping	10	15-Jan-27	28-Jan-27		22-Dec-26	14-Jan-27	-10	4
173	A6730	CE-83 - Location #7 Drop Rod Replace and Re-Paint	6	29-Jan-27	05-Feb-27		15-Jan-27	22-Jan-27	-10	4
174	A6800	CE-83 - Location #7 Scaffold Strip	10	08-Feb-27	19-Feb-27		25-Jan-27	05-Feb-27	-10	4
175	**Cable Works**		169	01-May-26 A	07-Jan-27		01-May-26	02-Dec-26	-18	45
176	**East Boom - Ch 0-60**		169	01-May-26 A	07-Jan-27		01-May-26	02-Dec-26	-18	45
177	**Painting**		8	17-Dec-26	07-Jan-27		20-Nov-26	02-Dec-26	-18	45
178	OCTCL32-A18	Cable Works - Painting to Existing Diagonal Bracing (DB) Cables - Ch 0-60	3	17-Dec-26*	21-Dec-26		20-Nov-26	24-Nov-26	-19	47
179	OCTCL32-A18	Cable Works - Painting to Existing Diagonal Bracing (DB) Cables - Ch 60-120	3	22-Dec-26	05-Jan-27		25-Nov-26	27-Nov-26	-19	47
180	OCTCL32-A17	Cable Works - Painting to Existing Diagonal Bracing (DB) Cables - Ch 180-240	3	05-Jan-27	07-Jan-27		30-Nov-26	02-Dec-26	-18	45
181	**Boom Anchor Cable (BAC) Cable**		93	01-May-26 A	12-Sep-26		01-May-26	24-Aug-26	-13	73
182	A5100	Procure Equipment for BAC Installation	81	01-May-26 A	25-Aug-26 A		01-May-26	11-Aug-26	-10	
183	OCTCL32-A	Cable Works - Boom Anchor Cable (BAC) & Fixings (4no)	10	03-Sep-26	12-Sep-26		15-Aug-26	24-Aug-26	-19	114
184	A6130	East Boom BAC Cable Replacements	10	03-Sep-26	12-Sep-26		15-Aug-26	24-Aug-26	-19	114
185	**East Tower Cable Works**		25	14-Sep-26	16-Oct-26		25-Aug-26	29-Sep-26	-13	86
186	C1810	Cable Works - Painting to main Anchor Cables	20	14-Sep-26	09-Oct-26		25-Aug-26	22-Sep-26	-13	86
187	C2150	Cable Works - Remove Scaffold Access to Tower	5	12-Oct-26	16-Oct-26		23-Sep-26	29-Sep-26	-13	86
188	**West Boom - Ch 180-236**		60	01-Sep-26	23-Nov-26		03-Aug-26	23-Oct-26	-21	65

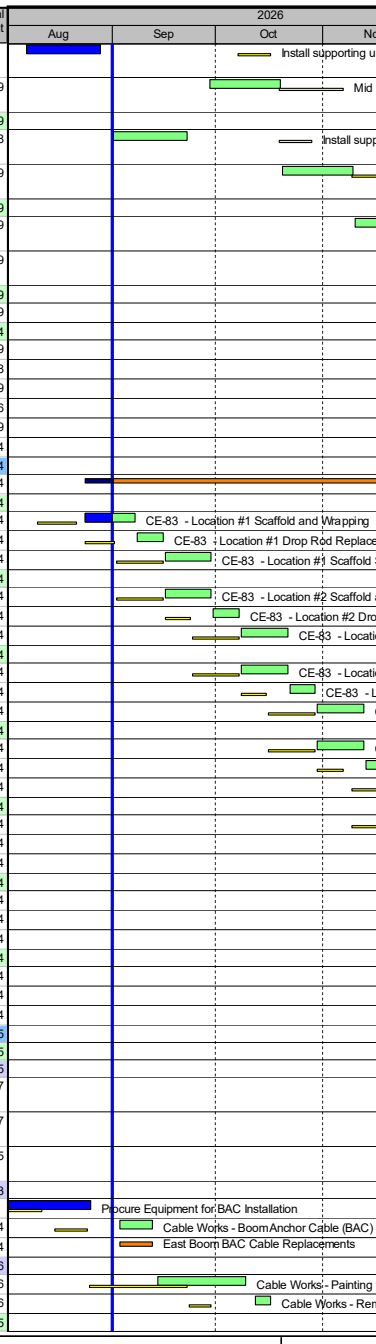

Critical Remaining Work
WBS Summary
Remaining Work
Actual Work
Remaining Level of Effort
Actual Level of Effort
Milestone
Baseline Milestone
Primary Baseline
Critical BL


PROJECT NAME: Newport Transporter Bridge - CL32 July 2026
PROJECT ID: 23826-C14990-CL32-42a
PROJECT BASELINE: Newport Transporter Bridge - CL32 July 2026

VolkerLaser

Newport Transporter Bridge - CL32 July

TASK filter: Data Date -4weeks.

#	Activity ID	Activity Name	At Completion Duration	Start	Finish	Expected Finish	BL Project Start	BL Project Finish	Variance - BL Project Finish Date	Total Float
189		**Cable Works - Diagonal Bracing (DB) Cables West Boom**	6	01-Sep-26	08-Sep-26		03-Aug-26	10-Aug-26	-20	-43
190		**Painting**	6	01-Sep-26	08-Sep-26		03-Aug-26	10-Aug-26	-20	-43
191	OCTCL32-A2	Cable Works - Painting to Existing Diagonal Bracing (DB) Cables - Ch 240-225	3	01-Sep-26	03-Sep-26		03-Aug-26	05-Aug-26	-20	-43
192	OCTCL32-A2	Cable Works - Painting to Existing Diagonal Bracing (DB) Cables - Ch 225-210	3	04-Sep-26	08-Sep-26		06-Aug-26	10-Aug-26	-20	-43
193		**Boom Anchor Cable (BAC) Cable @ Ch 236m**	26	14-Sep-26	19-Oct-26		25-Aug-26	20-Sep-26	-21	65
194	OCTCL32-A23	Cable Works - Lessons Learned Period from East BACs before SDR Works	10	14-Sep-26	25-Sep-26		25-Aug-26	08-Sep-26	-13	70
195	OCTCL32-A	Cable Works - Boom Anchor Cable (BAC) & Fixings (3no) - Nights	10	10-Oct-26*	19-Oct-26		11-Sep-26	20-Sep-26	-29	101
196	A6140	West Boom BAC Cable Replacements	10	10-Oct-26	19-Oct-26		11-Sep-26	20-Sep-26	-29	101
197		**West Tower Cable Works**	25	20-Oct-26	23-Nov-26		21-Sep-26	23-Oct-26	-21	65
198	C3600	Cable Works - Painting to main Anchor Cables	20	20-Oct-26	16-Nov-26		21-Sep-26	16-Oct-26	-21	65
199	C3590	Cable Works - Remove Scaffold Access to Tower	5	17-Nov-26	23-Nov-26		19-Oct-26	23-Oct-26	-21	65
200		**Motor House Refurbishment**	154	09-Mar-26 A	15-Oct-26	18-Sep-26	09-Mar-26	11-Sep-26	-24	97
201	OCTCL32-A105(	Motor House Refurbishment - Carry-out Repairs & Restoration works to the Windows	135	09-Mar-26 A	18-Sep-26	18-Sep-26	09-Mar-26	14-Aug-26	-24	-116
202	OCTCL32-A106(	Motor House Refurbishment - Carry-out Repairs & Restoration works to the Walls	135	09-Mar-26 A	18-Sep-26	18-Sep-26	09-Mar-26	14-Aug-26	-24	-121
203	A6180	Motorhouse Refurbishment	154	09-Mar-26 A	15-Oct-26		09-Mar-26	11-Sep-26	-24	97
204	OCTCL32-A104(	Motor House Refurbishment - Carry-out Repairs & Restoration works to the Walkway & Railings	130	16-Mar-26 A	18-Sep-26	18-Sep-26	16-Mar-26	14-Aug-26	-24	97
205	A6190	Provisional Lead in Period for materials pending TQ details	57	01-Jul-26 A	18-Sep-26	18-Sep-26	01-Jul-26	14-Aug-26	-24	97
206	OCTCL32-A10	Motor House Refurbishment - Carry-out Final Repairs & Restoration	19	21-Sep-26	15-Oct-26		17-Aug-26	11-Sep-26	-24	97
207		**Gondola & Traveller Restoration**	333	28-Oct-25 A	04-Mar-27		28-Oct-25	02-Feb-27	-22	0
208		**Steel Repairs Gondola**	232	28-Oct-25 A	02-Oct-26		28-Oct-25	27-Aug-26	-25	22
209	A6200	Gondola Steelwork Repairs	232	28-Oct-25 A	02-Oct-26		28-Oct-25	27-Aug-26	-25	22
210	A5890	Steel Repairs Gondola - Sweep Blast	10	02-Sep-26*	15-Sep-26		04-Aug-26	10-Aug-26	-25	22
211	A1295	Steel Repairs Gondola - Prime Steel	2	16-Sep-26	17-Sep-26		11-Aug-26	12-Aug-26	-25	22
212	OCTCL32-A1:	Steel Repairs Gondola - Carry out Painting to Steel	6	18-Sep-26	25-Sep-26		13-Aug-26	20-Aug-26	-25	22
213	OCTCL32-A1:	Steel Repairs Gondola - Remove Encapsulation	1	28-Sep-26	28-Sep-26		21-Aug-26	21-Aug-26	-25	22
214	OCTCL32-A1:	Steel Repairs Gondola - Re-install Deck to Gondola	2	29-Sep-26	30-Sep-26		24-Aug-26	25-Aug-26	-25	22
215	OCTCL32-A1:	Steel Repairs Gondola - Remove Access	2	01-Oct-26	02-Oct-26		26-Aug-26	27-Aug-26	-25	22
216		**Gondola Restoration Works**	61	05-Oct-26	07-Jan-27		28-Aug-26	23-Nov-26	-25	22
217	OCTCL32-A134	Gondola Restoration - Install Temporary East Approach Bridge Walkway	5	05-Oct-26	09-Oct-26		28-Aug-26	04-Sep-26	-25	22
218	OCTCL32-A1:	Gondola Restoration - Carry-out Paint Analysis	10	12-Oct-26	23-Oct-26		07-Sep-26	18-Sep-26	-25	22
219	A6210	Gondola Refursbishment	56	12-Oct-26	07-Jan-27		07-Sep-26	23-Nov-26	-25	22
220	OCTCL32-A13!	Gondola Restoration - Carry-out Repairs & Restoration works to Pilot House roof	10	26-Oct-26	06-Nov-26		21-Sep-26	02-Oct-26	-25	22
221	OCTCL32-A137	Gondola Restoration - Carry-out Repairs & Restoration to Passenger Shelters roof	10	09-Nov-26	20-Nov-26		05-Oct-26	16-Oct-26	-25	28
222	OCTCL32-A138	Gondola Restoration - Carry-out Repairs & Restoration works to Pilot House walls	16	09-Nov-26	30-Nov-26		05-Oct-26	26-Oct-26	-25	22
223	OCTCL32-A136	Gondola Restoration - Carry-out Repairs & Restoration to Passenger Shelters walls	10	01-Dec-26	14-Dec-26		27-Oct-26	09-Nov-26	-25	22
224	OCTCL32-A1:	Gondola Restoration - Carry-out Repairs & Restoration to Gates	10	15-Dec-26	07-Jan-27		10-Nov-26	23-Nov-26	-25	22
225		**Traveller & Cable Works**	38	05-Jan-27	25-Feb-27		24-Nov-26	26-Jan-27	-22	0
226		**Traveller**	38	05-Jan-27	25-Feb-27		24-Nov-26	26-Jan-27	-22	0
227	OCTCL32-A'	Traveller & Cable Works - Establish Access to Traveller	2	05-Jan-27	06-Jan-27		24-Nov-26	25-Nov-26	-22	0
228	OCTCL32-A'	Traveller & Cable Works - Install Encapsulation	3	07-Jan-27	11-Jan-27		26-Nov-26	30-Nov-26	-22	7
229	OCTCL32-A'	Remove Traveller Timber	10	07-Jan-27	20-Jan-27		26-Nov-26	09-Dec-26	-22	0
230	OCTCL32-A11	Traveller & Cable Works - Carry out repairs to steel including paint work	10	21-Jan-27	03-Feb-27		10-Dec-26	04-Jan-27	-22	0
231	OCTCL32-A'	Traveller & Cable Works - Remove Encapsulation	1	04-Feb-27	04-Feb-27		05-Jan-27	05-Jan-27	-22	0
232	OCTCL32-A11	Traveller & Cable Works - Install Temporary Works to enable restoration of Traveller moving mechanism	3	05-Feb-27	09-Feb-27		06-Jan-27	08-Jan-27	-22	0
233	OCTCL32-A11	Traveller & Cable Works - Carry out Restoration to Traveller Wheels & Mechanism	5	10-Feb-27	16-Feb-27		11-Jan-27	15-Jan-27	-22	0
234	OCTCL32-A'	Traveller & Cable Works - Remove Temporary Works	5	17-Feb-27	23-Feb-27		18-Jan-27	22-Jan-27	-22	0
235	OCTCL32-A'	Traveller & Cable Works - Remove Access	2	24-Feb-27	25-Feb-27		25-Jan-27	26-Jan-27	-22	0
236		**Testing & Commissioning**	5	26-Feb-27	04-Mar-27		27-Jan-27	02-Feb-27	-22	0
237	OCTCL32-A1:	Test & Commissioning of Gondola & Traveller (Only without Power-On	5	26-Feb-27	04-Mar-27		27-Jan-27	02-Feb-27	-22	0
238	A6260	Commissioning of Gondola & Traveller (Only Without Power-On)	5	26-Feb-27	04-Mar-27		27-Jan-27	02-Feb-27	-22	0
239		**Railings**	18	08-Jan-27	02-Feb-27		24-Nov-26	17-Dec-26	-25	22
240	OCTCL32-A14	Railings - Dismantle existing Railings	3	08-Jan-27	12-Jan-27		24-Nov-26	26-Nov-26	-25	22
241	OCTCL32-A14	Railings - Reinstate & Install new Railings	15	13-Jan-27	02-Feb-27		27-Nov-26	17-Dec-26	-25	22
242		**East Approach Bridge Refurbishment**	403	21-Jul-25 A	04-Mar-27	04-Sep-26	21-Jul-25	19-Feb-27	-9	5
243		**Procurement & Manufacture**	347	21-Jul-25 A	07-Dec-26	04-Sep-26	21-Jul-25	24-Nov-26	-9	61
244	A5570	EAB - Trailer Storage pending crane issues - EWN-125	282	21-Jul-25 A	04-Sep-26	04-Sep-26	21-Jul-25	07-Aug-26	-19	0

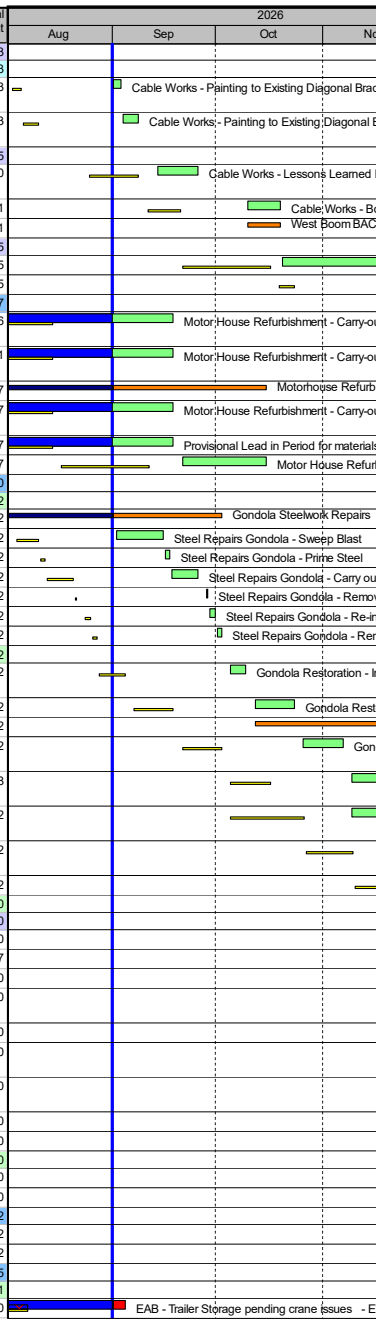


Critical Remaining Work
WBS Summary
Remaining Work
Actual Work
Remaining Level of Effort
Actual Level of Effort
Milestone
Baseline Milestone
Primary Baseline
Critical BL

PROJECT NAME: Newport Transporter Bridge - CL32 July 2026
PROJECT ID: 23826-C14990-CL32-42a
PROJECT BASELINE: Newport Transporter Bridge - CL32 July 2026

Newport Transporter Bridge - CL32 July

TASK filter: Data Date -4weeks.

#	Activity ID	Activity Name	At Completion Duration	Start	Finish	Expected Finish	BL Project Start	BL Project Finish	Variance - BL Project Finish Date	Total Float
245	PW1210	East Approach Bridge - Deliver 7no Inner Beams	20	07-Sep-26	02-Oct-26		10-Aug-26	07-Sep-26	-19	0
246	PW1250	East Approach Bridge - Procure Materials for 2no Outer Beams	20	21-Sep-26	16-Oct-26		08-Sep-26	05-Oct-26	-9	0
247	A6840	EAB - Blasting of Beams @ Factory	5	21-Sep-26	25-Sep-26					111
248	PW1230	East Approach Bridge - Re-Work 2no Outer Beams	30	19-Oct-26	27-Nov-26		06-Oct-26	16-Nov-26	-9	0
249	PW1220	East Approach Bridge - Treatment to 2no Outer Beams	10	23-Nov-26	04-Dec-26		10-Nov-26	23-Nov-26	-9	0
250	PW1200	East Approach Bridge - Deliver 2no Outer Beams	0	07-Dec-26	07-Dec-26		24-Nov-26	24-Nov-26	-9	0
251	**EAB Removal and Installation**		121	07-Sep-26	04-Mar-27		24-Aug-26	19-Feb-27	-9	0
252	C3540	East Approach Bridge - Remove 7no existing Beams	10	07-Sep-26	18-Sep-26		24-Aug-26	07-Sep-26	-9	0
253	C3450	East Approach Bridge - Remove Surfacing & Expose Beam Ends	10	07-Sep-26	18-Sep-26		24-Aug-26	07-Sep-26	-9	25
254	A6220	East Approach Bridge - Existing Beam Removal and Off-Site Refurbishment	65	07-Sep-26	04-Dec-26		24-Aug-26	23-Nov-26	-9	0
255	C3550	East Approach Bridge - Inspect & Refurbish Beams (Offsite Rework 7no to Fab 2no Outer Beams)	30	21-Sep-26	30-Oct-26		08-Sep-26	19-Oct-26	-9	25
256	C3640	East Approach Bridge - Install 7no New Inner Beams	10	21-Sep-26	02-Oct-26		08-Sep-26	21-Sep-26	-9	45
257	C3560	East Approach Bridge - Install Refurbished 2no. Outer Beams	7	07-Dec-26	15-Dec-26		24-Nov-26	02-Dec-26	-9	0
258	A6230	East Approach Bridge - Install Refurbished Beams, Deck and Parapets	56	07-Dec-26	04-Mar-27		24-Nov-26	19-Feb-27	-9	0
259	C3610	East Approach Bridge - Reinstate Parapet	2	14-Dec-26	15-Dec-26		01-Dec-26	02-Dec-26	-9	0
260	C3570	East Approach Bridge - Reinstate Deck	9	25-Jan-27	04-Feb-27		12-Jan-27	22-Jan-27	-9	0
261	C3840	CE-9 Timber Replacement - Duration TBC once CE evaluated	15	05-Feb-27	25-Feb-27		25-Jan-27	12-Feb-27	-9	0
262	C3630	East Approach Bridge - Reinstate Ground & Road Surfacing	5	26-Feb-27	04-Mar-27		15-Feb-27	19-Feb-27	-9	0
263	**Buffer Refurbishment**		39	20-Oct-26	11-Dec-26		07-Oct-26	30-Nov-26	-9	51
264	A6240	East and West Buffer Refurbishment	39	20-Oct-26	11-Dec-26		07-Oct-26	30-Nov-26	-9	51
265	**West Buffer**		37	20-Oct-26	09-Dec-26		07-Oct-26	26-Nov-26	-9	53
266	OCTCL32-A1	West Buffer - Remove Gondola Buffer Counter Weight	5	20-Oct-26	26-Oct-26		07-Oct-26	13-Oct-26	-9	51
267	OCTCL32-A1	West Buffer - Refurbish Gondola Buffer Counter Weight	30	27-Oct-26	07-Dec-26		14-Oct-26	24-Nov-26	-9	53
268	OCTCL32-A1	West Buffer - Install Gondola Buffer Counter Weight	2	08-Dec-26	09-Dec-26		25-Nov-26	26-Nov-26	-9	53
269	**East Buffer**		34	27-Oct-26	11-Dec-26		14-Oct-26	30-Nov-26	-9	51
270	OCTCL32-A1	East Buffer - Remove Gondola Buffer Counter Weight	2	27-Oct-26	28-Oct-26		14-Oct-26	15-Oct-26	-9	51
271	OCTCL32-A1	East Buffer - Refurbish Gondola Buffer Counter Weight	30	29-Oct-26	09-Dec-26		16-Oct-26	26-Nov-26	-9	51
272	OCTCL32-A1	East Buffer - Install Refurbish Buffer	2	10-Dec-26	11-Dec-26		27-Nov-26	30-Nov-26	-9	51
273	**PROJECT CLOSE-OUT**		14	22-Feb-27	11-Mar-27		08-Feb-27	08-Mar-27	-3	0
274	OCTCL32-A100	Remove Hoists Access @ East Tower	5	22-Feb-27	26-Feb-27		23-Feb-27	01-Mar-27	1	4
275	OCTCL32-A101	Remove Hoists Access @ West Tower	5	22-Feb-27	26-Feb-27		08-Feb-27	12-Feb-27	-10	4
276	OCTCL32-A103	Demobilise	5	05-Mar-27	11-Mar-27		02-Mar-27	08-Mar-27	-3	0
277	A6250	Site Demobisation	5	05-Mar-27	11-Mar-27		02-Mar-27	08-Mar-27	-3	0
278	OCTCL32-A102	Handover Complete	0		11-Mar-27			08-Mar-27	-3	0
279	**RETIRED**		1042	14-Nov-22 A	29-Jan-27	17-Jul-26	14-Nov-22	21-Dec-26	-21	29

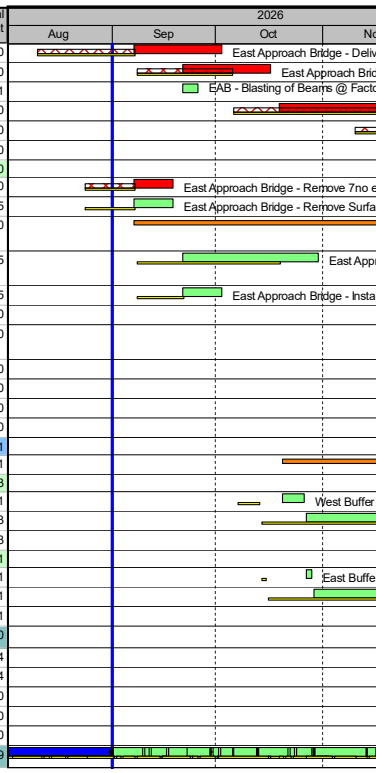

Critical Remaining Work
WBS Summary
Remaining Work
Actual Work
Remaining Level of Effort
Actual Level of Effort
Milestone
Baseline Milestone
Primary Baseline
Critical BL

PROJECT NAME: Newport Transporter Bridge - CL32 July 2026
PROJECT ID: 23826-C14990-CL32-42a
PROJECT BASELINE: Newport Transporter Bridge - CL32 July 2026
